

LAB REPORT

Software Project Management



Student Name: Nguyễn Văn Minh

ID: 22003405

Class: DHKTPM18

Course: 2025-2026




Contents

Module 1:	3
Exercise 1: Creating a link	3
Exercise 2: Setting duration	3
Exercise 3: Creating phases	4
Exercise 4: Noah - Linking	5
Exercise 5: Pyramid - Multi level grouping.....	6
Exercise 6: Creating a plan for Staff Training	7
Exercise 7: Recurring Tasks	8
Exercise 8: Travelling – tasks calendar.....	9
Module 2:	9
Exercise 1: Part Time - creating new calendar	9
Exercise 2: Changing Working Time	14
Exercise 3: Changing Working Time	19
Exercise 4: Changing Working Time	23
Exercise 5: Create the private Time for a project	26
Exercise 6: My project	30
Module 3: Working with Tasks	32
Exercise 1: Changing Working Time (Start Date Feb 2st 2026)	32
Exercise 2: Changing Working Time (Start Date Feb 2rd 2026)	34
Exercise 3: Scheduling – Task dependencies.....	36
Module 4: Assigning resources to the tasks in Project	40
Exercise 1: Entering Resources.....	40
Exercise 2: Entering resources	41
Exercise 3: Entering resources	42
Exercise 4: Entering resources	43
Exercise 5: Resources with the private working time	45
Exercise 6: The Engagement planning.....	45


Lab report – Project Management

Module 1:

Exercise 1: Creating a link

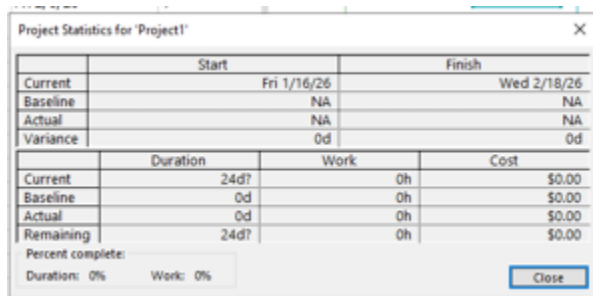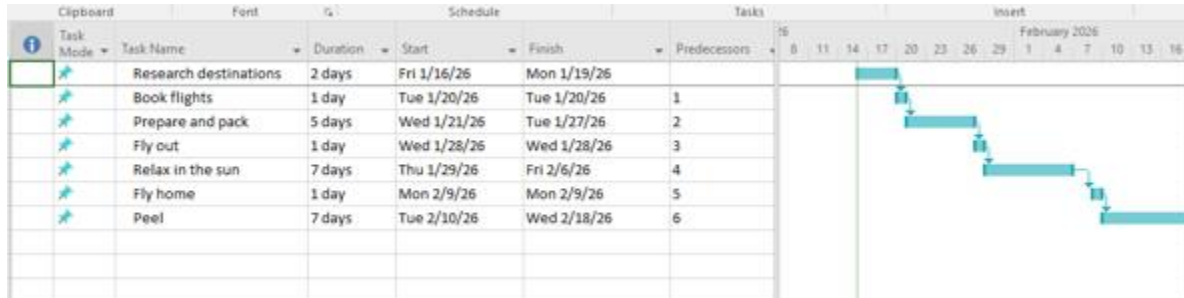

Exercise 2: Setting duration

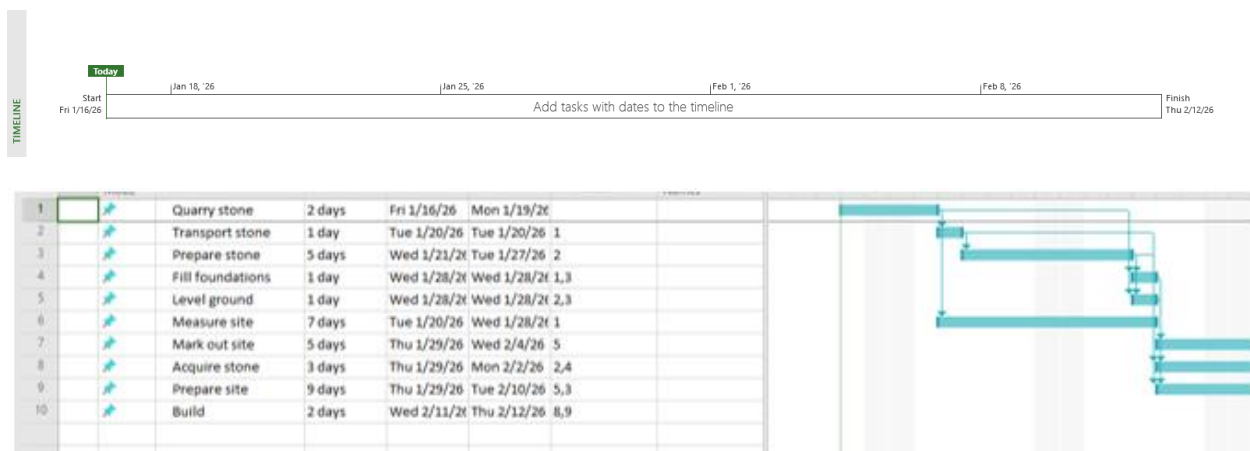

Lab report – Project Management


Project Statistics for 'ex02.mpp'

	Start	Finish
Current	Fri 1/16/26	Thu 2/12/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	20d?	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	20d?	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close

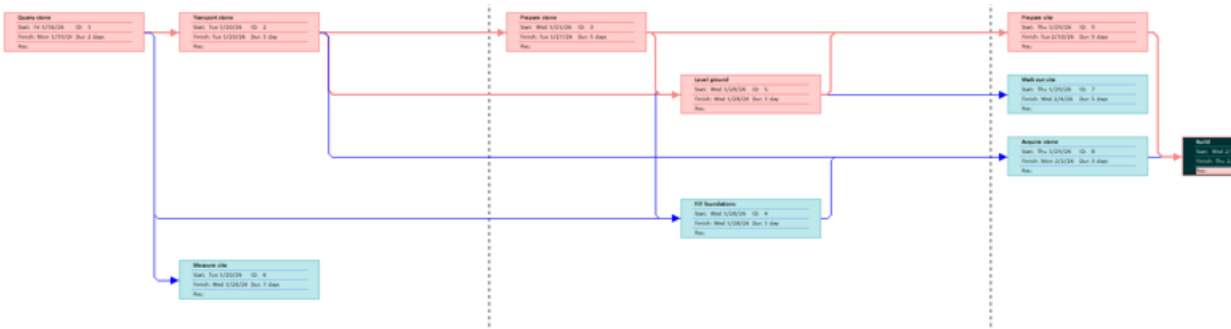

Exercise 3: Creating phases

Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
	Pre-heat oven	5 mins	Fri 1/16/26	Fri 1/16/26		
	Prepare meat	5 mins	Fri 1/16/26	Fri 1/16/26	1	
	Prepare veg	5 mins	Fri 1/16/26	Fri 1/16/26	2	
	Heat pan	5 mins	Fri 1/16/26	Fri 1/16/26	3	
	Fry veg	5 mins	Fri 1/16/26	Fri 1/16/26	4	
	Brown meat	5 mins	Fri 1/16/26	Fri 1/16/26	5	
	Add stock and bring to a simmer	5 mins	Fri 1/16/26	Fri 1/16/26	6	
	Cook in oven	45 mins	Fri 1/16/26	Fri 1/16/26	7	



Today 9:00 AM

Start Fri 1/16/26

Add tasks with dates to the timeline

9:00 AM



Finish Fri 1/16/26

Lab report – Project Management

Project Statistics for 'ex03.mpp'			
	Start	Finish	
Current	Fri 1/16/26	Fri 1/16/26	
Baseline	NA	NA	
Actual	NA	NA	
Variance	0d	0d	
	Duration	Work	Cost
Current	0.17d?	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	0.17d?	0h	\$0.00
Percent complete:			
Duration: 0% Work: 0%			
Close			

Exercise 4: Noah - Linking

	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		Build boat	7 days	Fri 1/16/26	Mon 1/26/26		
2		Load supplies	3 days	Tue 1/27/26	Thu 1/29/26	1	
3		Load family	6 days	Tue 1/27/26	Tue 2/3/26	1	
4		Load animals	7 days	Tue 1/27/26	Wed 2/4/26	1	
5		Collect animals A-M	12 days	Thu 2/5/26	Fri 2/20/26	1,4	
6		Collect animals N-Z	10 days	Thu 2/5/26	Wed 2/18/26	2,4	
7		Float around	7 days	Mon 2/23/26	Tue 3/3/26	5,6	

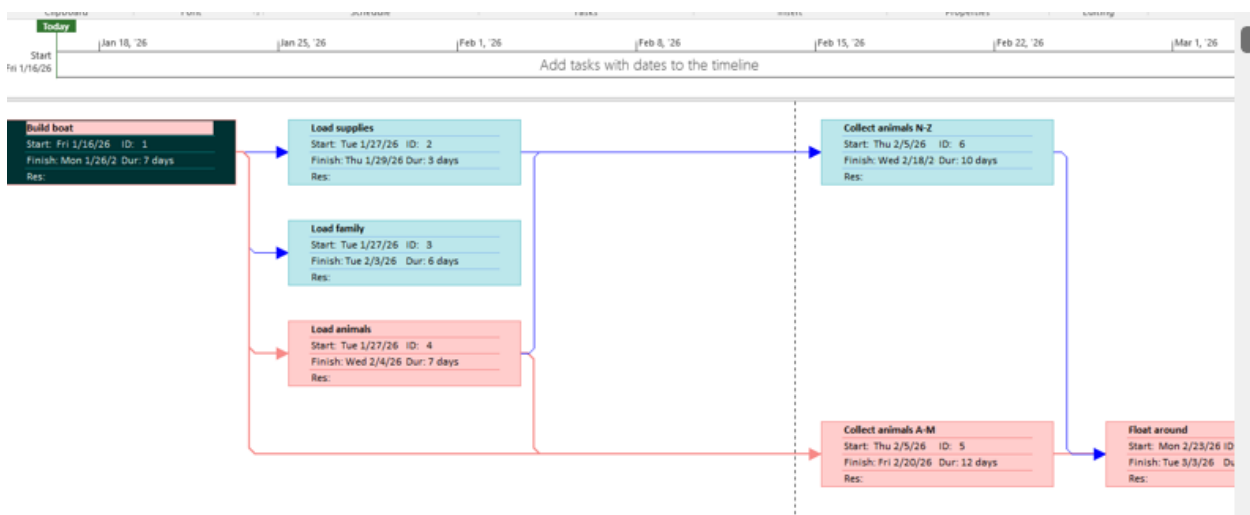

Lab report – Project Management





	Start	Finish
Current	Fri 1/16/26	Tue 3/3/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	33d7	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	33d7	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close



Exercise 5: Pyramid - Multi level grouping

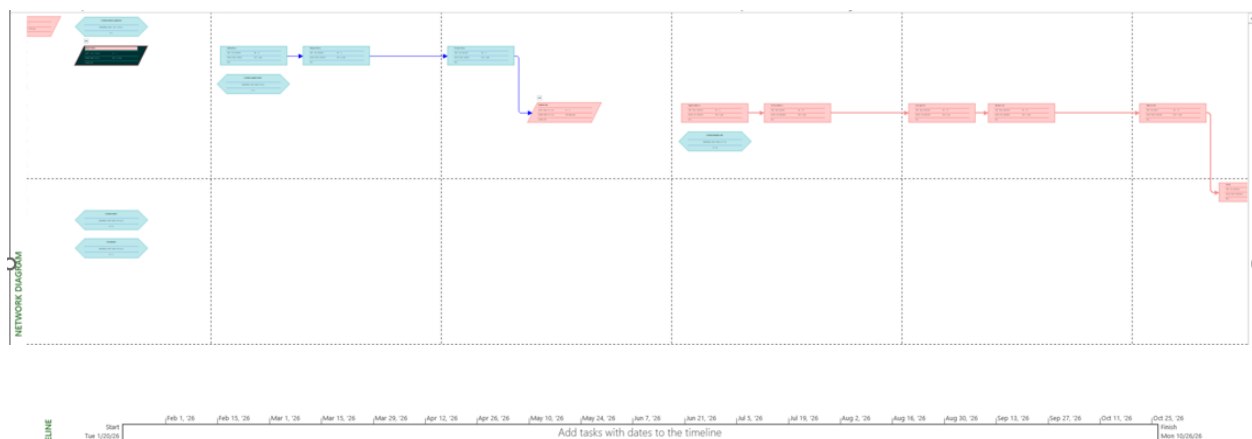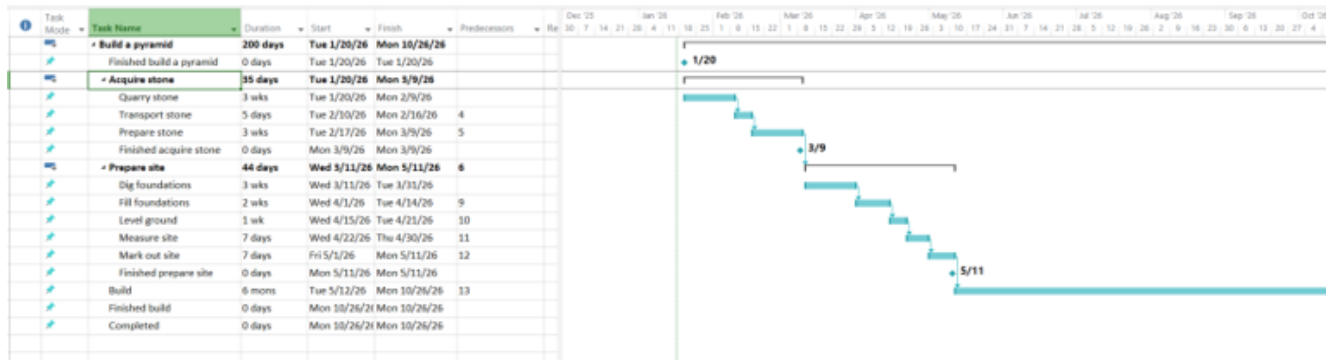

Lab report – Project Management



Exercise 7: Recurring Tasks

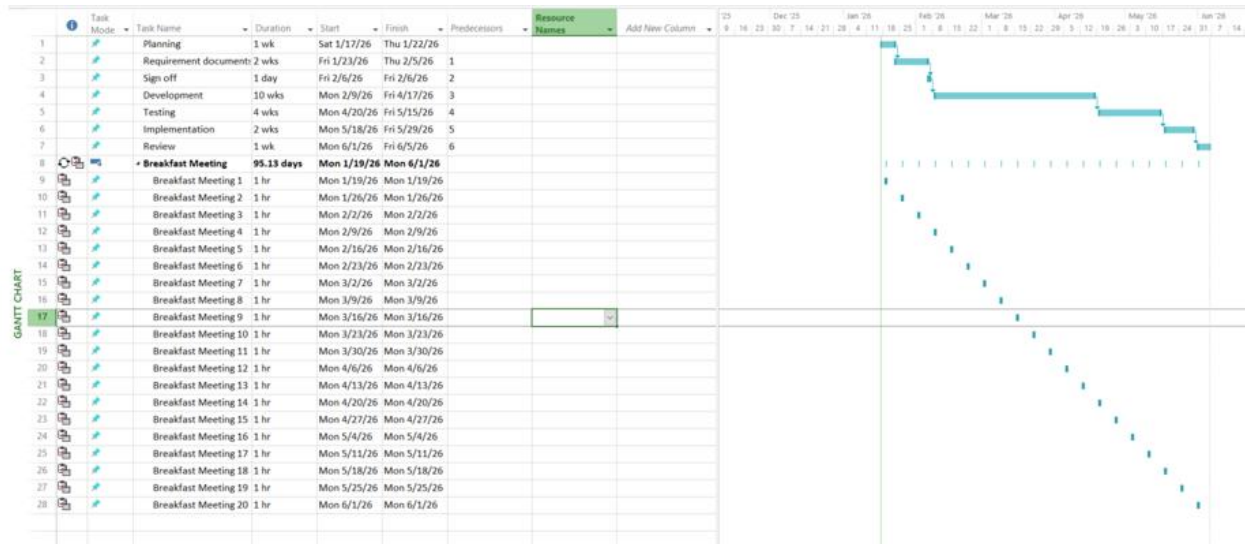

Project Statistics for 'ex07.mpp'

	Start	Finish
Current	Sat 1/17/26	Fri 6/5/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	100d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	100d	0h	\$0.00

Percent complete:


Duration: 0%Work: 0%

Close

Lab report – Project Management

Exercise 8: Travelling – tasks calendar

Travelling – task calendar You intend to travel from HCM to Kuala Lumpur, Bangkok and then, come back to HCM. Creating a plan for your trip.

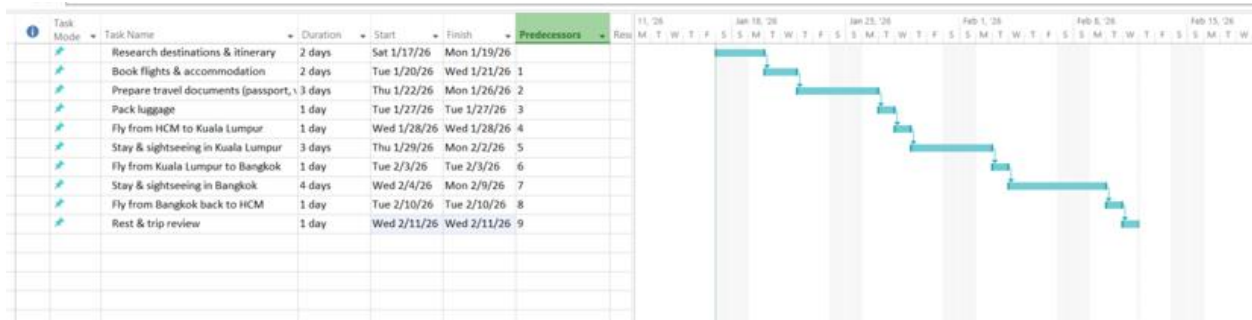


Project Statistics for 'ex08.mpp'

	Start	Finish
Current	Sat 1/17/26	Wed 2/11/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	18d?	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	18d?	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close

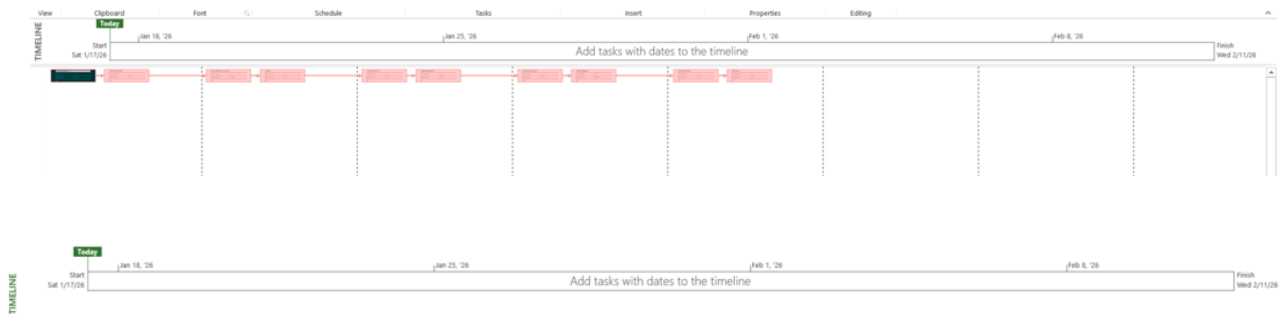

Module 2:


Exercise 1: Part Time - creating new calendar

Part Time - creating new calendar

Open project file Ex2 (Module 1), Use the Project Information dialog box to:

Lab report – Project Management


A part-time worker will be used on this project. Go to the Change Working Time dialog box and create a new copy of the Standard calendar, calling it "Part Time".

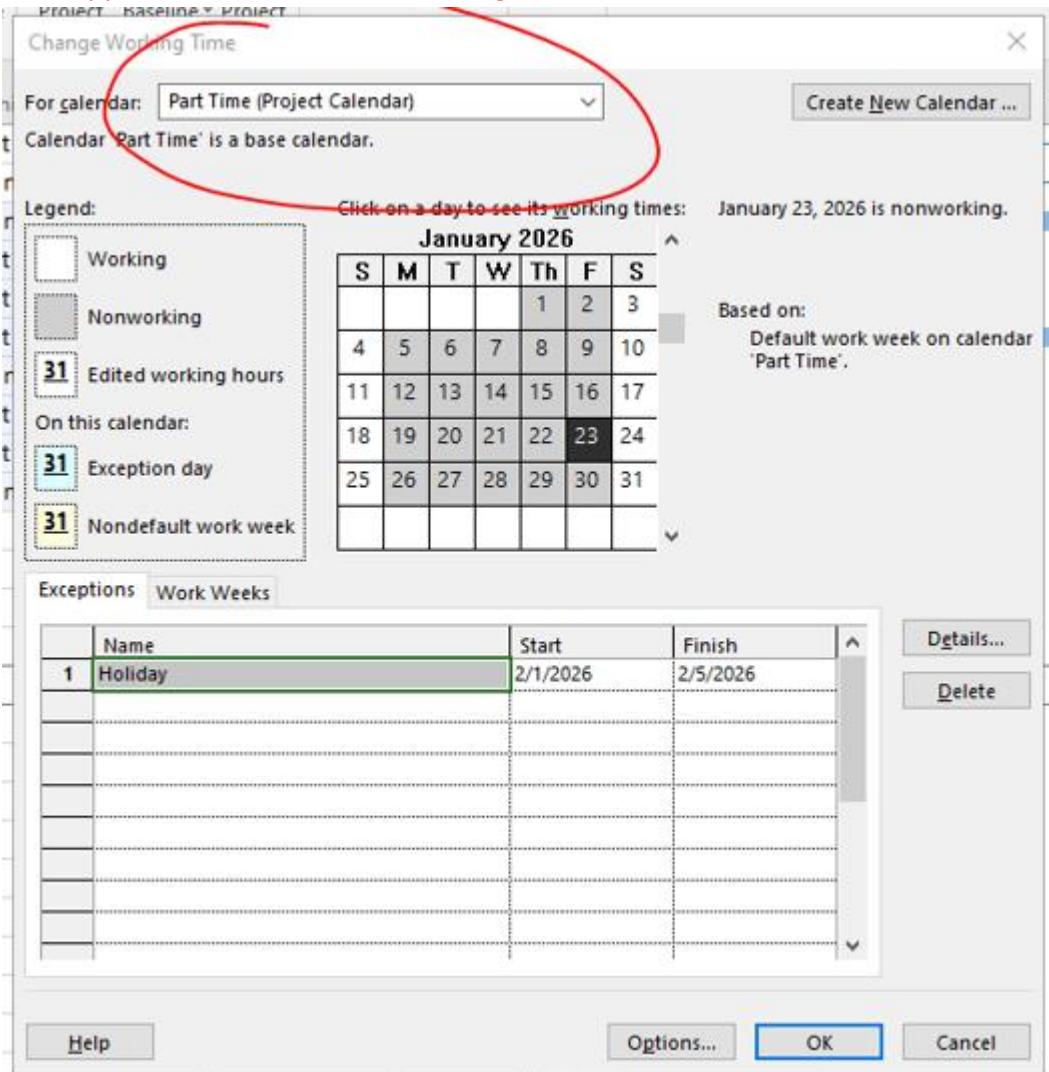


Update the working time of your new calendar so that:

- Mondays to Fridays are nonworking time
- The remaining 2 weekdays have working time of 10:00 to 16:00 (no breaks)

Lab report – Project Management

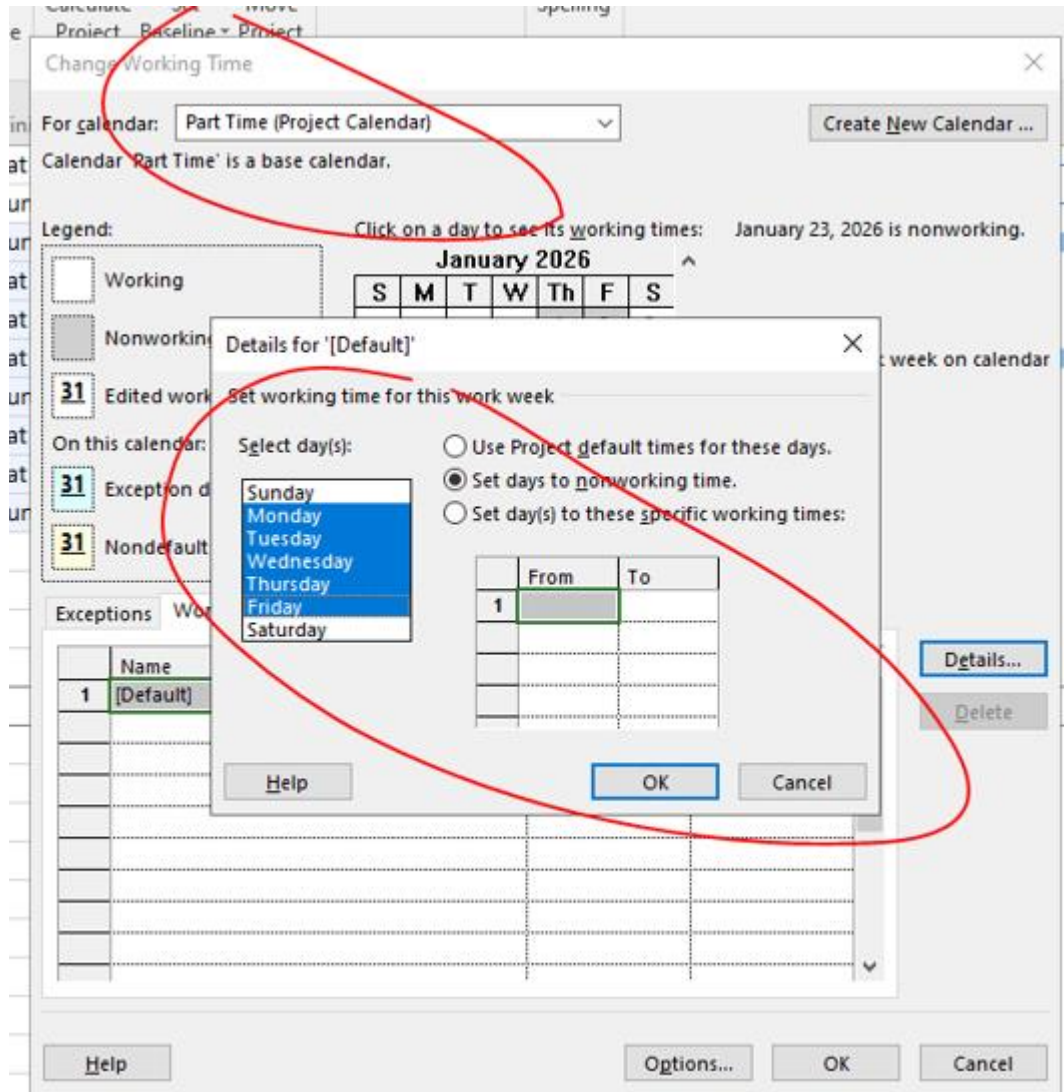

Lab report – Project Management

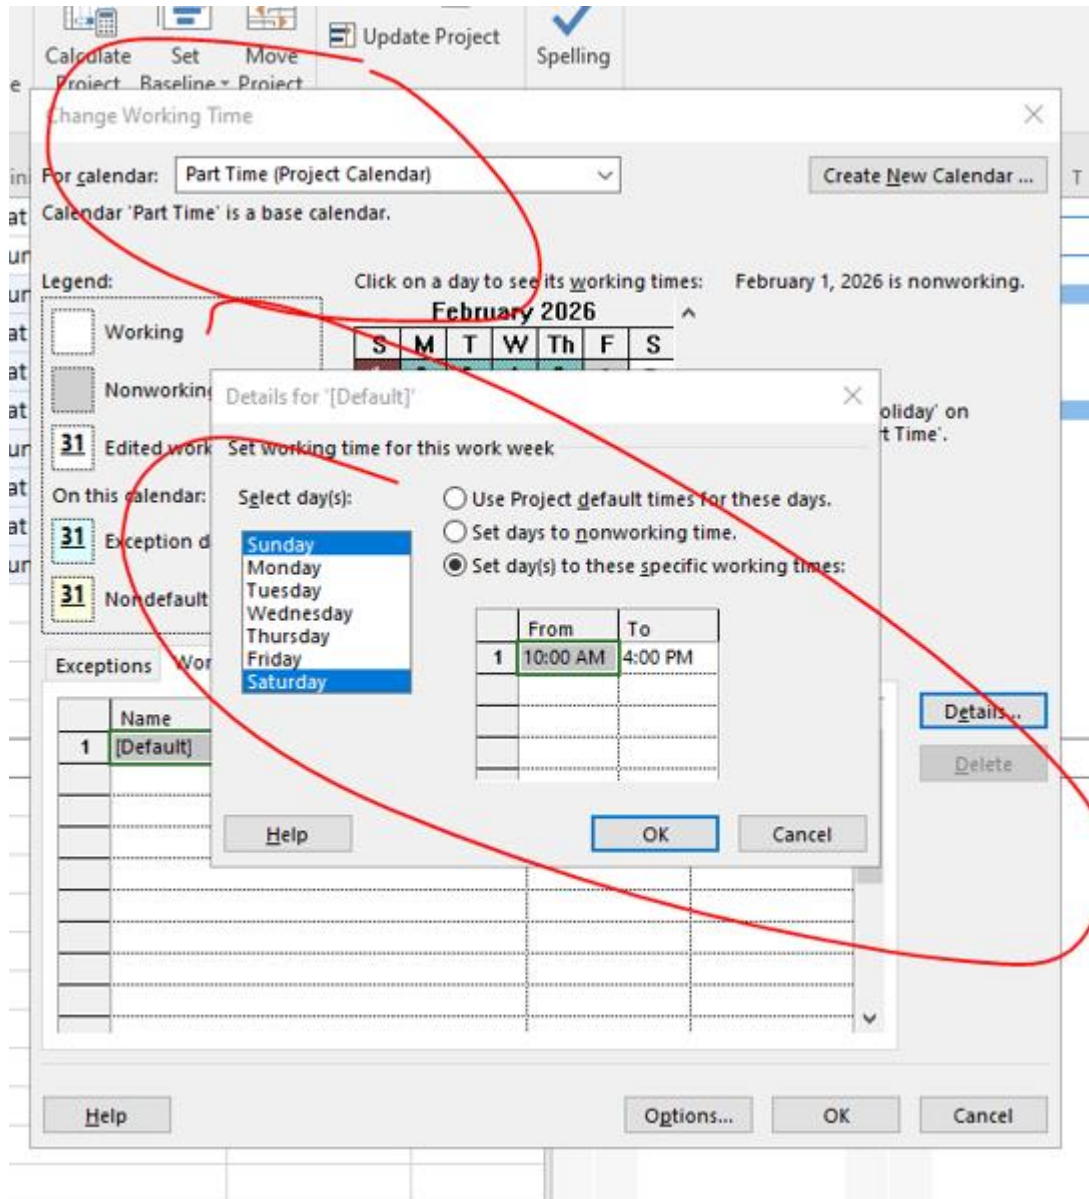

The Part time has also booked a holiday from 1st to Feb 5th . Create an Exception to their calendar with a Holiday name and these days as nonworking

Lab report – Project Management

Change Working Time

For calendar: **Part Time (Project Calendar)** Create New Calendar ...

Calendar 'Part Time' is a base calendar.

Legend:

- ☐ Working
- ☐ Nonworking
- 31** Edited working hours

On this calendar:

- 31** Exception day
- 31** Nondefault work week

Click on a day to see its working times: February 1, 2026 is nonworking.

Based on:
Exception 'Holiday' on calendar 'Part Time'.

February 2026

S	M	T	W	Th	F	S
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28

Exceptions

	Name	Start	Finish
1	Holiday	2/1/2026	2/5/2026

Details...
Delete

Help Options... OK Cancel

Display the Project Information.

Project Statistics for 'module02_ex01.mpp'

	Start	Finish
Current	Sat 1/17/26	Sun 4/19/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	20d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	20d	0h	\$0.00

Percent complete:

Duration: 0% Work: 0%

Close

Exercise 2: Changing Working Time

Changing Working Time

Open project file Ex4 (Module 1) Use the Project Information dialog box to:

Start Date: Nov 20th 2025

Project Information for 'module02_ex02'

Start date: **Thu 11/20/25** Current date: Fri 1/23/26

Finish date: Mon 1/5/26 Status date: NA

Schedule from: Project Start Date Calendar: Standard

All tasks begin as soon as possible. Priority: 500

Enterprise Custom Fields

Department:

Custom Field Name	Value
-------------------	-------

Help Statistics... OK Cancel

Go to the Change Working Time dialog box and create an Exception called "Tet Holidays" during from Dec 24th 2026 to Jan 5th 2026 into nonworking time.

Lab report – Project Management

Change Working Time

For calendar: Standard (Project Calendar) Create New Calendar ...

Calendar 'Standard' is a base calendar.

Legend:

- Working
- Nonworking
- 31 Edited working hours
- 31 Exception day
- 31 Nondefault work week

Click on a day to see its working times: December 24, 2025 is nonworking.

December 2025

S	M	T	W	Th	F	S
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Based on:
Exception 'Tet holidays' on calendar 'Standard'.

Exceptions Work Weeks

Name	Start	Finish
1 Tet holidays	12/24/2025	1/5/2026


Details... Delete

Help Options... OK Cancel

Change Work Weeks time of Standard calendar's default working week. This project's standard working time are:

- 08:30 to 17:30 Monday to Thursday (no lunch break)
- 08:30 to 16:00 on Fridays (no lunch break)
- Add a new Work Week to the Standard calendar named "Xmas Slowdown". Use this to model a 12:30 finish on every weekday from Dec 10th 2025 to Dec 23rd 2025.
- Capture the Work weeks time

Lab report – Project Management

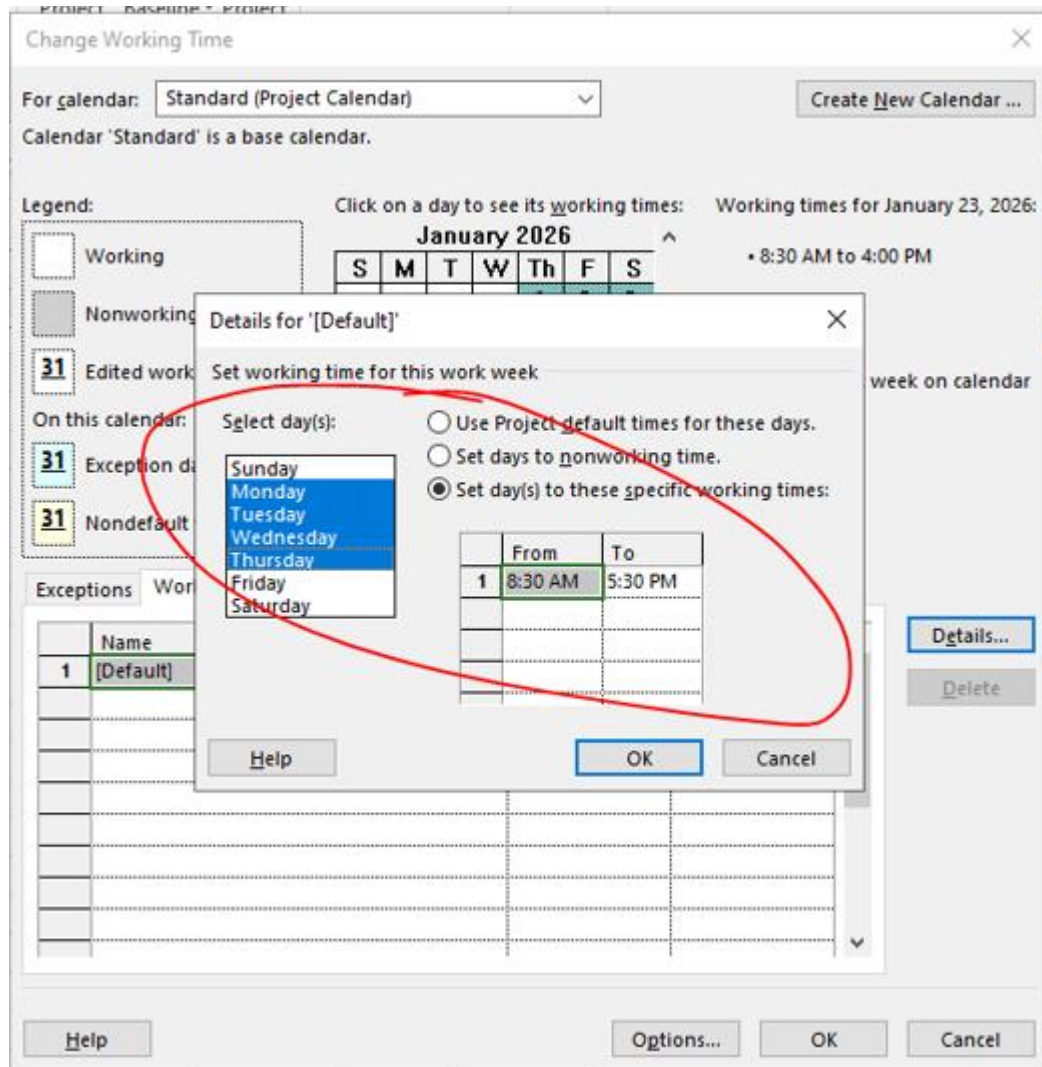

Lab report – Project Management

Change Working Time

For calendar: Standard (Project Calendar) Create New Calendar ...

Calendar 'Standard' is a base calendar.

Legend:

- Working
- Nonworking
- Edited work
- Exception d
- Nondefault

Click on a day to see its working times: Working times for January 23, 2026: 8:30 AM to 4:00 PM

January 2026

S	M	T	W	Th	F	S

Details for '[Default]'

Set working time for this work week

Select day(s):

- Sunday
- Monday
- Tuesday
- Wednesday
- Thursday
- Friday
- Saturday

☐ Use Project default times for these days.

☐ Set days to nonworking time.

☒ Set day(s) to these specific working times:

	From	To
1	8:30 AM	4:00 PM

Help OK Cancel

Details... Delete

Help Options... OK Cancel

Lab report – Project Management

Change Working Time

For calendar: Standard (Project Calendar)

Calendar 'Standard' is a base calendar.

Legend:

- Working
- Nonworking
- 31 Edited working hours
- 31 Exception day
- 31 Nondefault work week

Exceptions

Name	Start	End
1 (Default)		
2 Xmas slowdown	12/10/2025	12/23/2025

Details for 'Xmas slowdown'

Set working time for this work week

Select day(s):

- ☐ Use times from default work week for these days.
- ☐ Set days to nonworking time.
- ☒ Set day(s) to these specific working times:

From	To
1 8:30 AM	12:00 PM

Project Statistics for 'module02_ex02.mpp'


	Start	Finish
Current	Thu 11/20/25	Thu 1/22/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	33d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	33d	0h	\$0.00

Percent complete:

Duration: 0% Work: 0%

Lab report – Project Management



Exercise 3: Changing Working Time

Open project file **Ex5 (Module 1)**, Use the Project Information dialog box to:

Star Date: Apr 5th 2026

	Start	Finish
Current	Sun 4/5/26	Thu 1/7/27
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d


	Duration	Work	Cost
Current	199d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	199d	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close


The office will shut down for 2 weeks in the summer. Use the Change Working Time dialog box to create an Exception called "Summer Shutdown" and make the first 14 workdays of August nonworking time

Lab report – Project Management

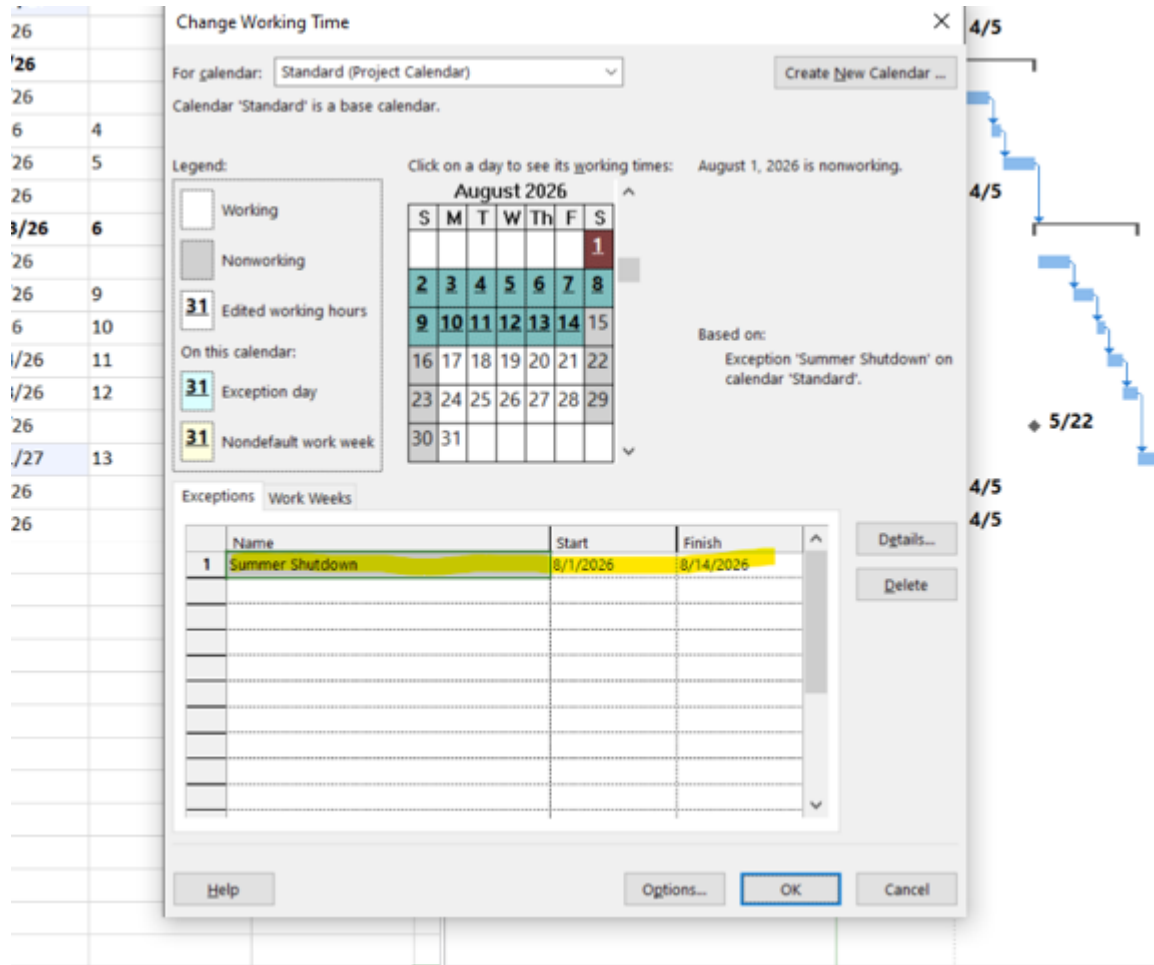


Create an Exception called “Independence Days” is 2 Sep nonworking time.

Lab report – Project Management

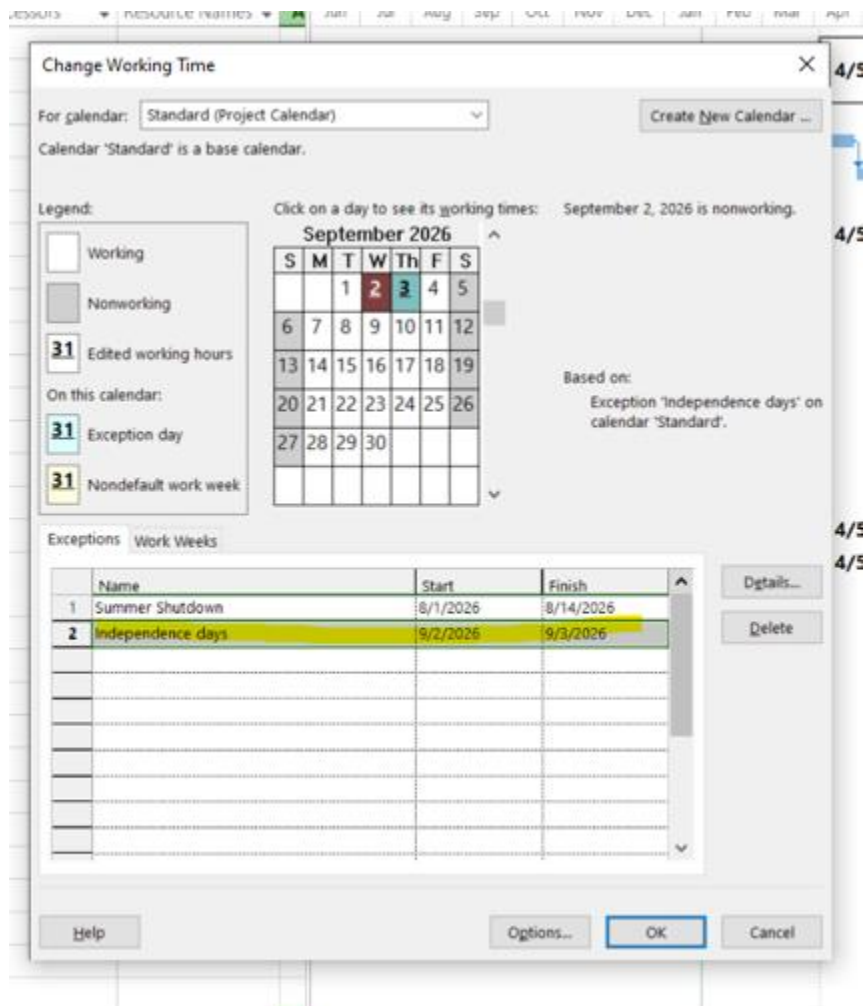


Create an Exception called “International Labor days” is Apr 30th and May 1st nonworking time

Lab report – Project Management

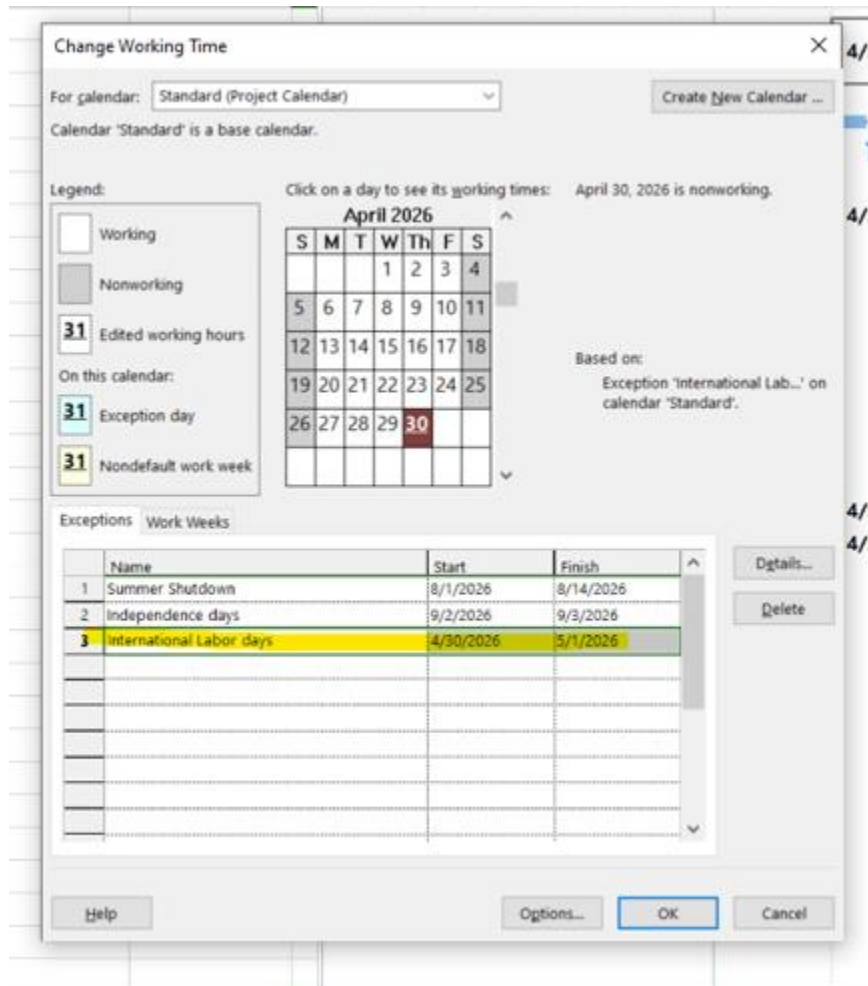


Display the Project Information

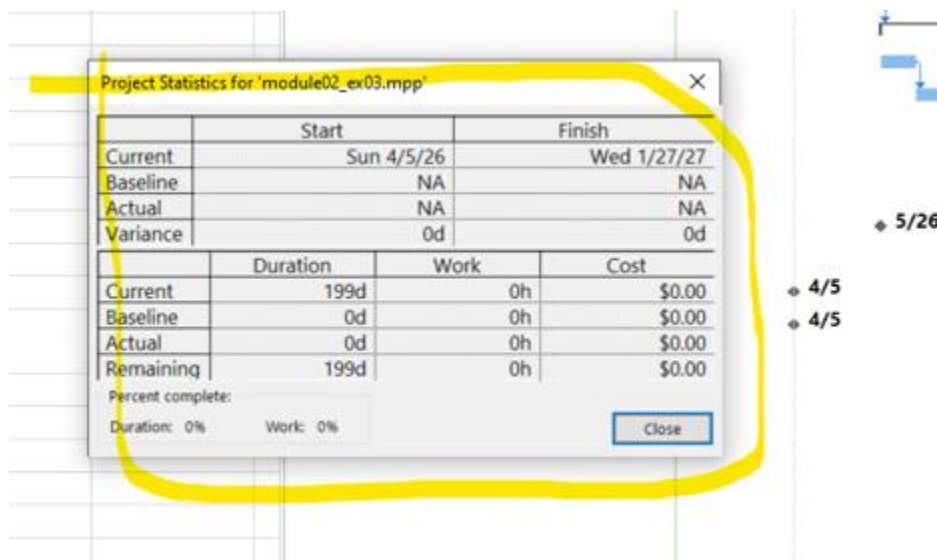

Lab report – Project Management


Exercise 4: Changing Working Time

Open project file Ex6 (Module 1), Use the Project Information dialog box to:

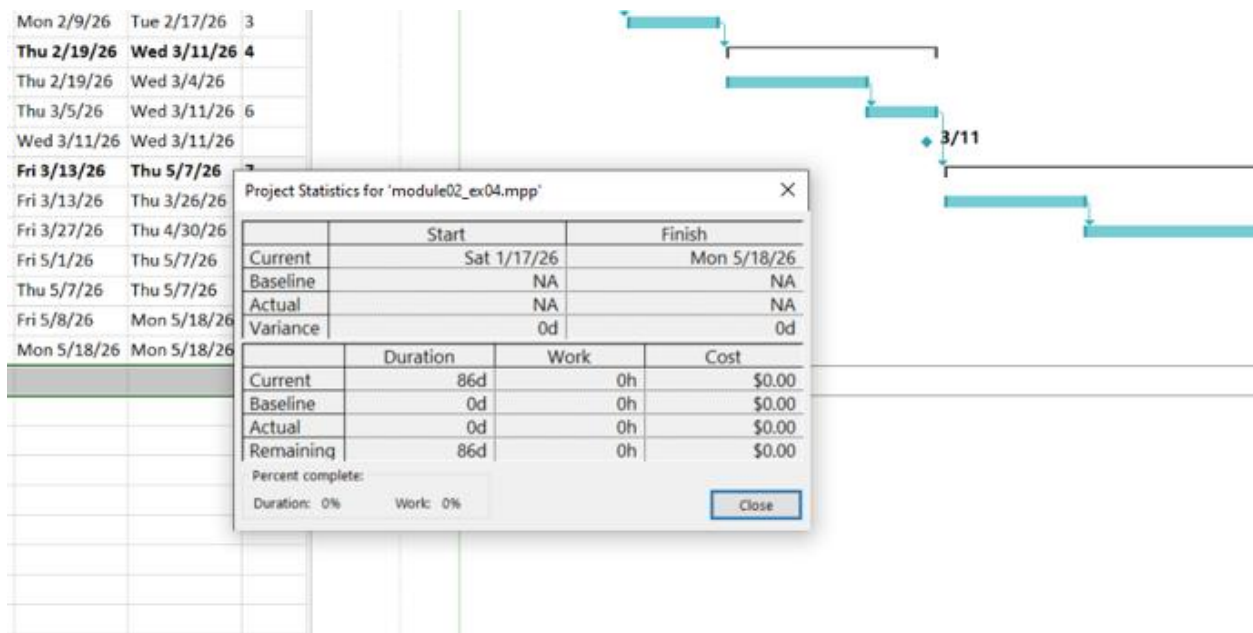


Modify the Standard calendar and change the [Default] work week to use the hours shown below:

Lab report – Project Management

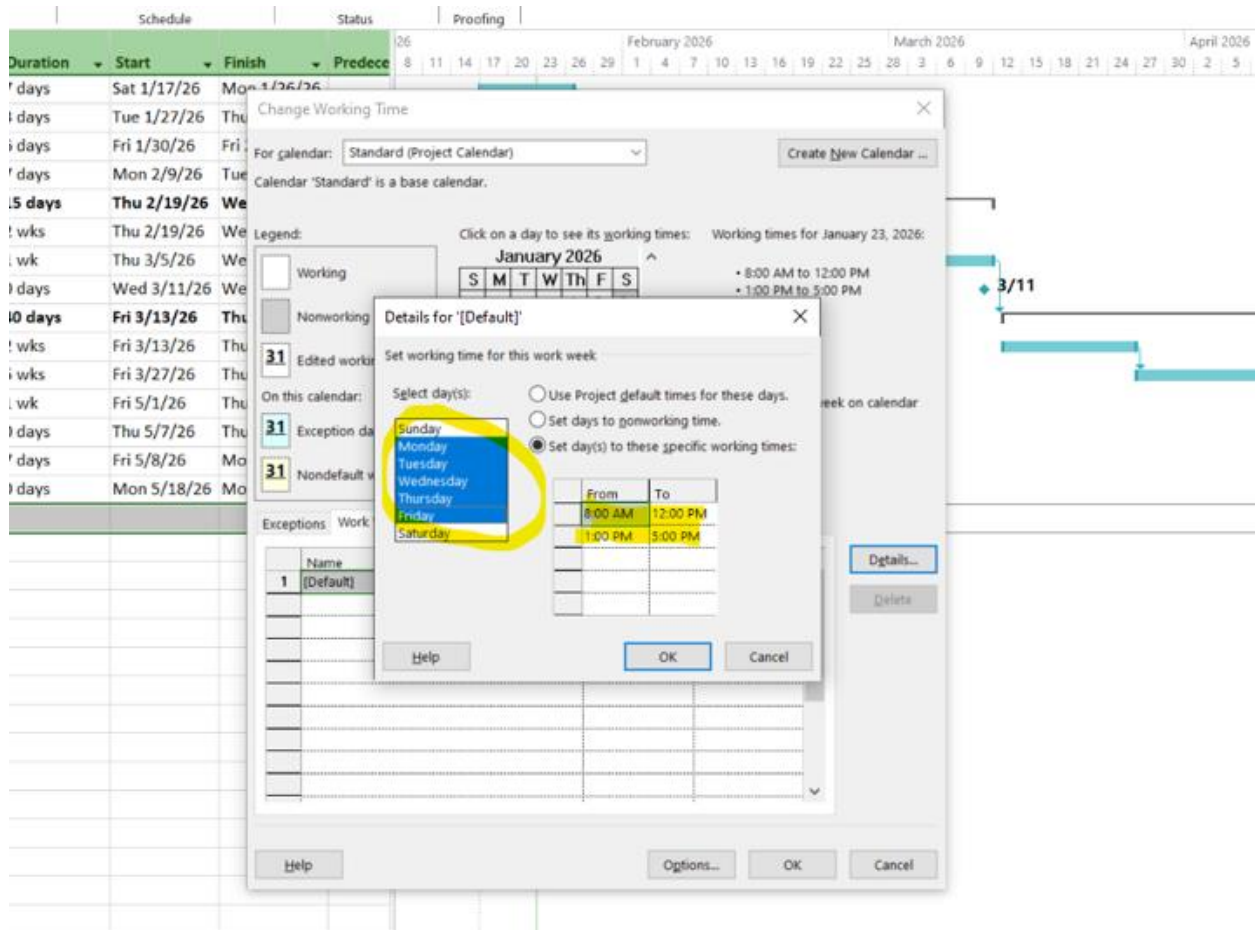


Add an exception in the Standard calendar called Recovery with in 7 later workdays of March is non-working days.

Lab report – Project Management

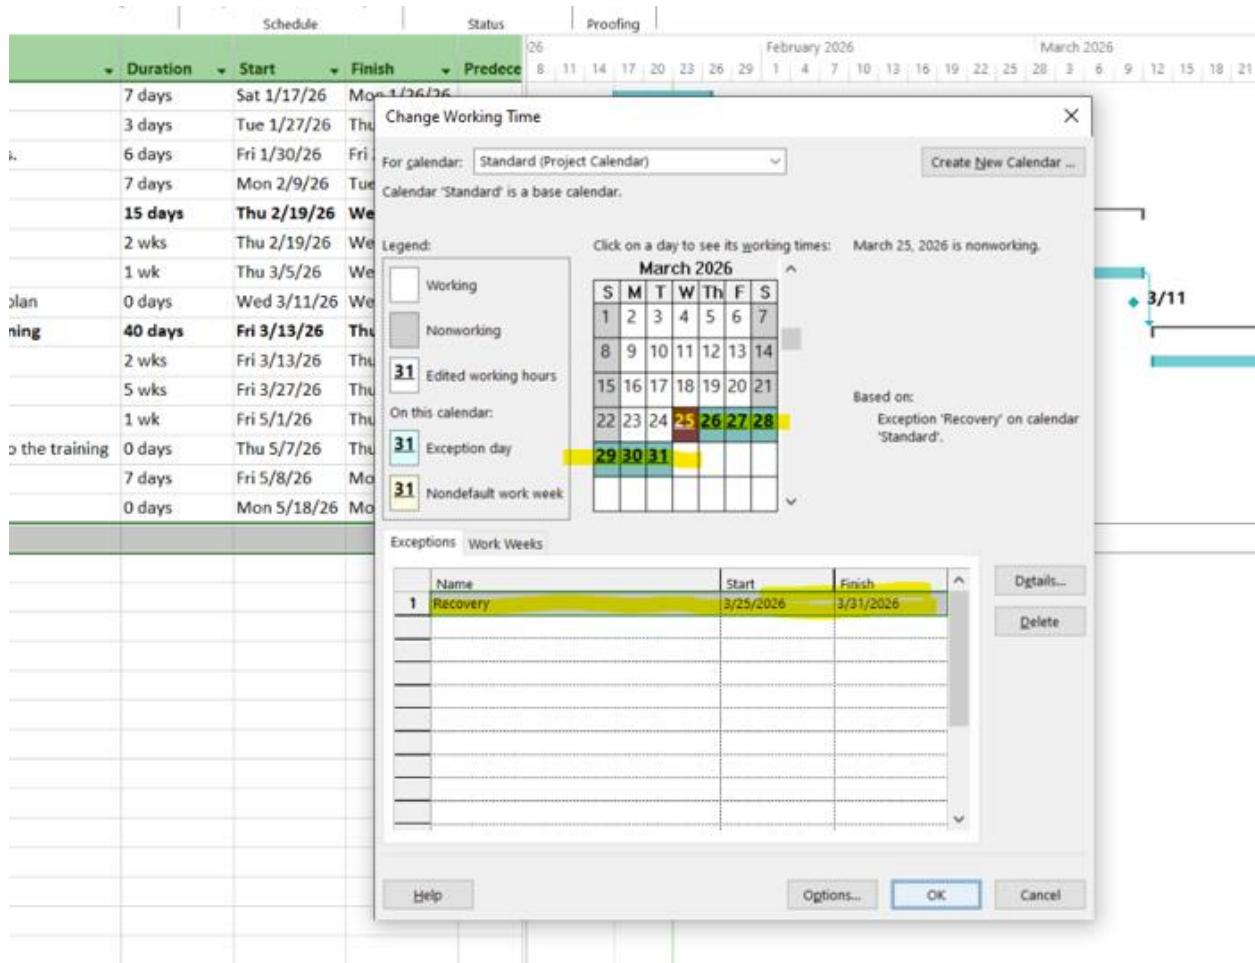

Display the Project Information.

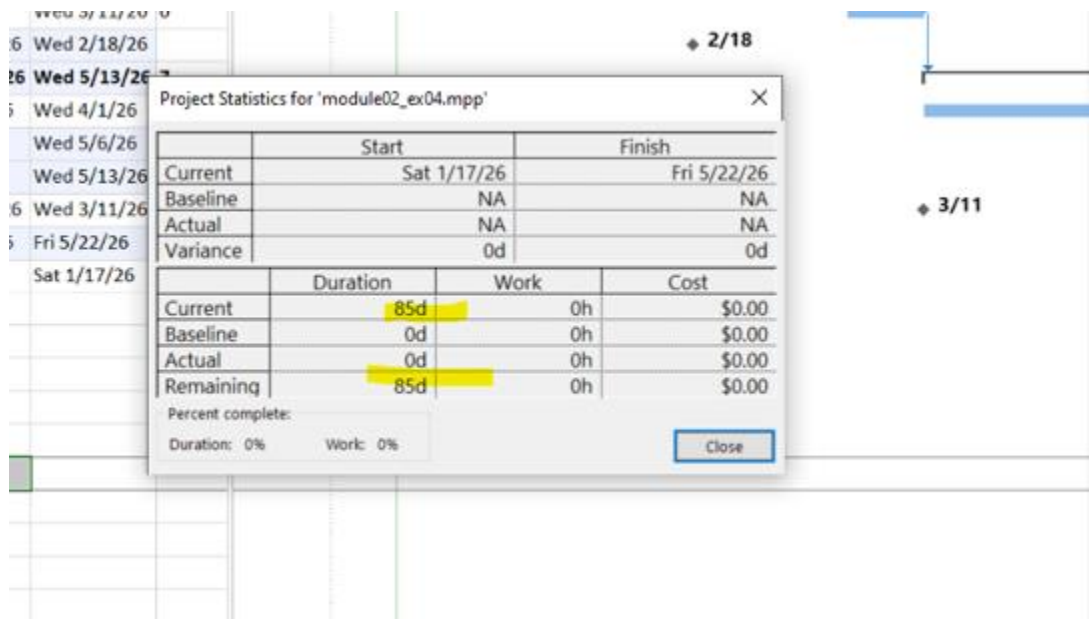


Lab report – Project Management

Exercise 5: Create the private Time for a project

Open project file Ex7 (Module 1), Use the Project Information dialog box to:

Create the new Time Work for your project.


[NameTimeProject] {Name: Your Name - Ex: MinhTimeProject}

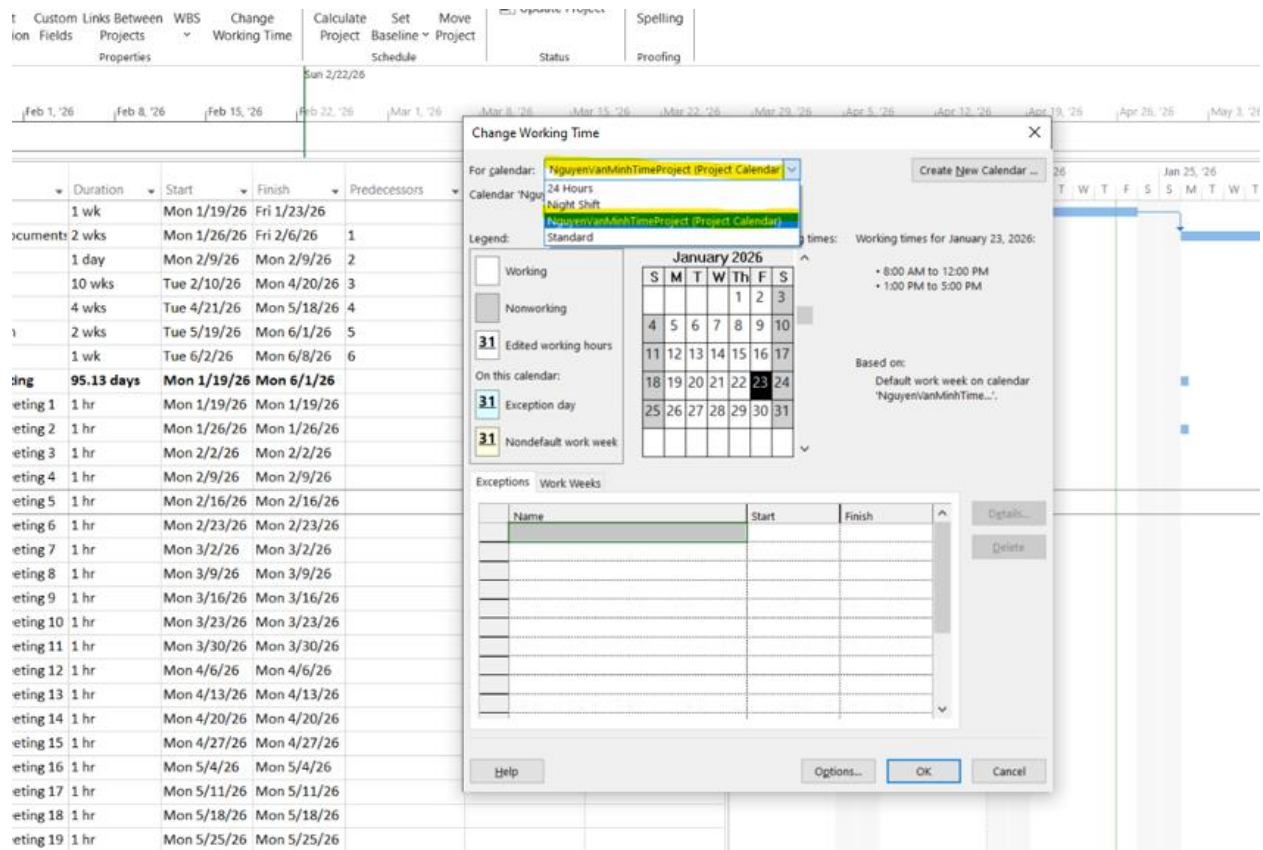

Change Work Weeks time of Standard calendar's default working week. This project's standard working time are:


08:00 to 12:00 on Mon, Wed, Fri

Lab report – Project Management

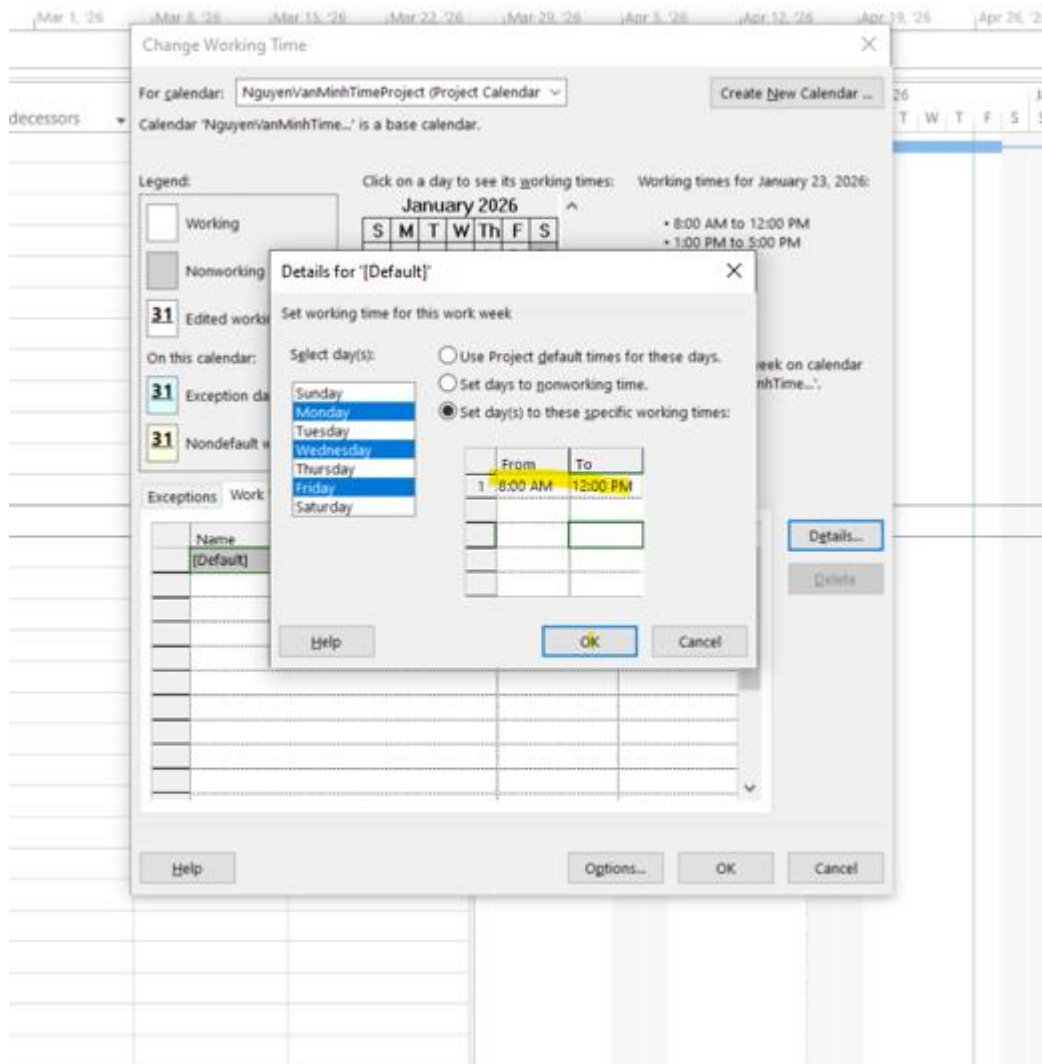


13:00 to 16:00 on Tue, Thu, Sat

Lab report – Project Management

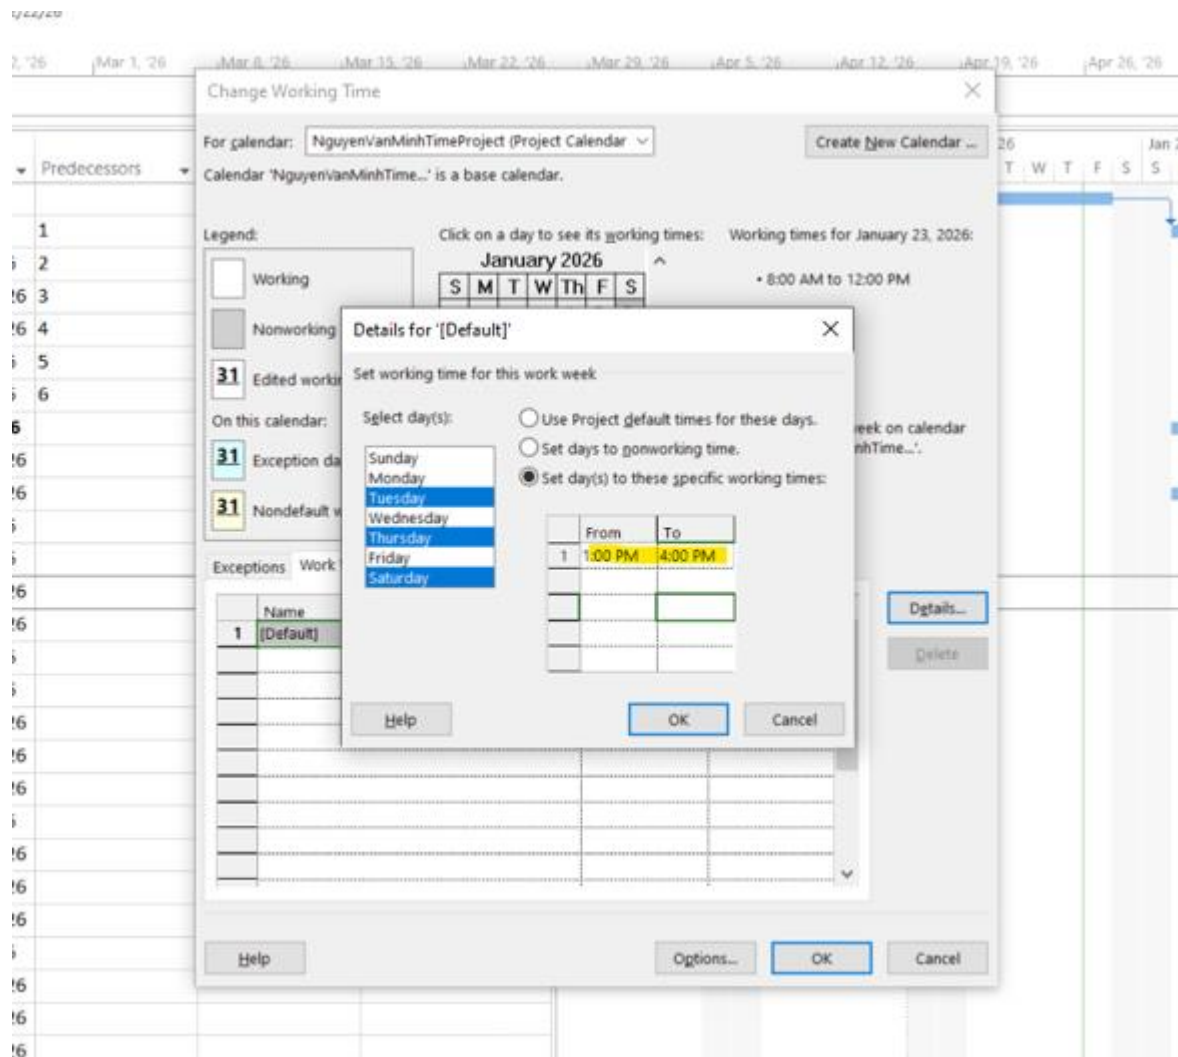

Create an Exception called “International Labor days” is Apr 30th and May 1st nonworking time

Lab report – Project Management

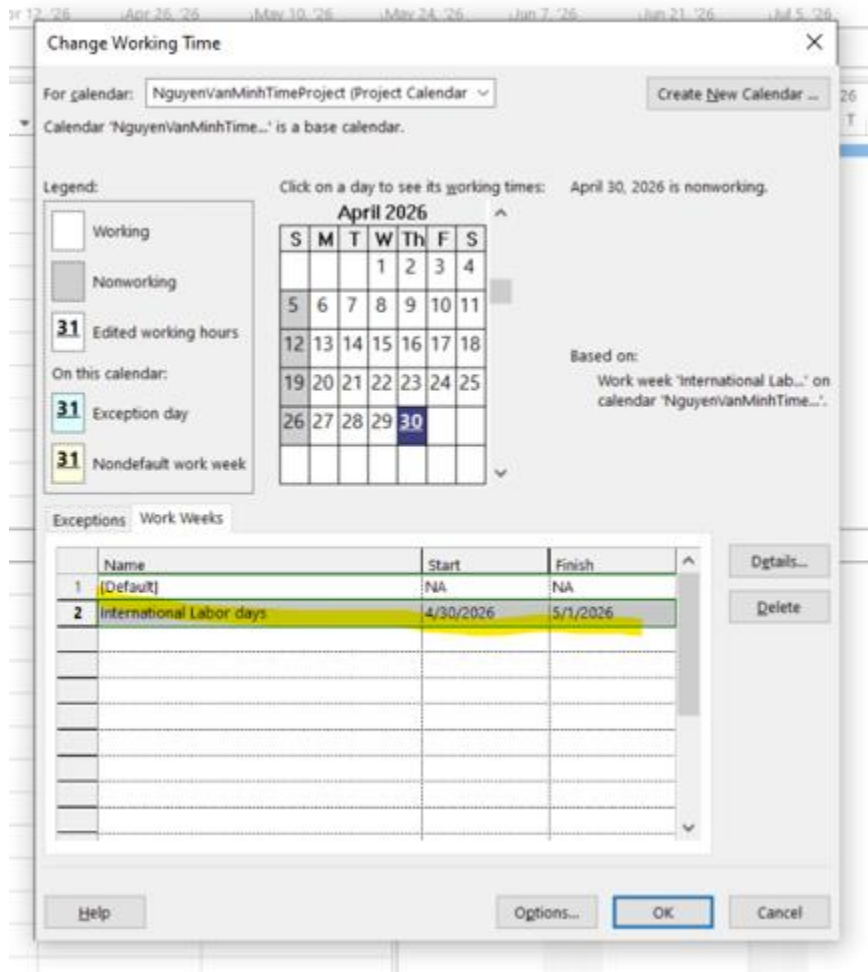

Capture the Work weeks time



Lab report – Project Management

Project Statistics for 'module02_ex05.mpp'

	Start	Finish
Current	Sat 1/17/26	Tue 10/13/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	101d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	101d	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close

Exercise 6: My project

Create your plan from Monday to Sunday. It will list all of your activities, your time you spend and resources joining in each task.

Create a new calendar called Student based on the Standard calendar.



Change the [Default] work week so that the hours match to your calendar everyday

Using Note function in MP 2010 to take note for important tasks in your plan.

The screenshot displays the Microsoft Project 2010 interface. On the left, a Gantt chart shows a project plan starting on Jan 25, '26, with tasks listed in the Task Name column. The tasks include 'Kế hoạch công việc tháng phát triển dự án phần mềm job freelancer của Nguyễn Văn Minh' (24 days), 'Phân tích yêu cầu hệ thống' (2 days), 'Thiết kế kiến trúc phần mềm' (2 days), 'Thiết kế cơ sở dữ liệu' (2 days), 'Lập trình Backend' (5 days), 'Lập trình Frontend' (4 days), 'Tích hợp Frontend & Backend' (2 days), 'Kiểm thử chức năng (Testing)' (3 days), 'Sửa lỗi & tối ưu code' (2 days), 'Viết tài liệu kỹ thuật' (1 day), and 'Triển khai hệ thống (Deployment)' (1 day). The 'Start' column shows the start dates for each task.

Overlaid on the right is the 'Change Working Time' dialog box. It shows the 'For calendar' dropdown set to 'Student (Project Calendar)'. The 'Calendar' dropdown is also set to 'Student (Project Calendar)'. The 'Legend' section shows 'Working' (light blue) and 'Nonworking' (light grey). The 'On this calendar' section shows '31 Edited working hours' and '31 Exception day'. The 'Nondefault work week' section is empty. The 'Exceptions' table is also empty. The 'Work Weeks' table is empty. The 'Based on' section shows 'Default work week on calendar "Student"'. The 'Working times for January 23, 2026' are listed as '8:00 AM to 12:00 PM' and '1:00 PM to 5:00 PM'. The 'Options...' button is visible at the bottom right of the dialog box.

Lab report – Project Management

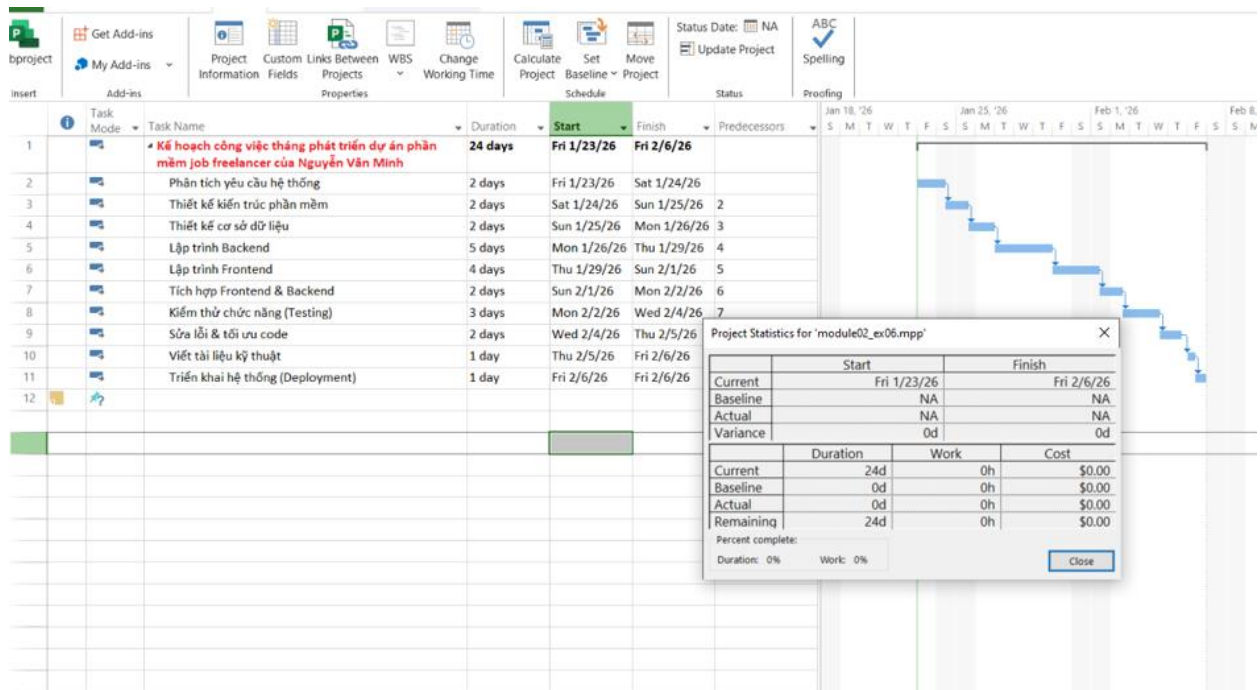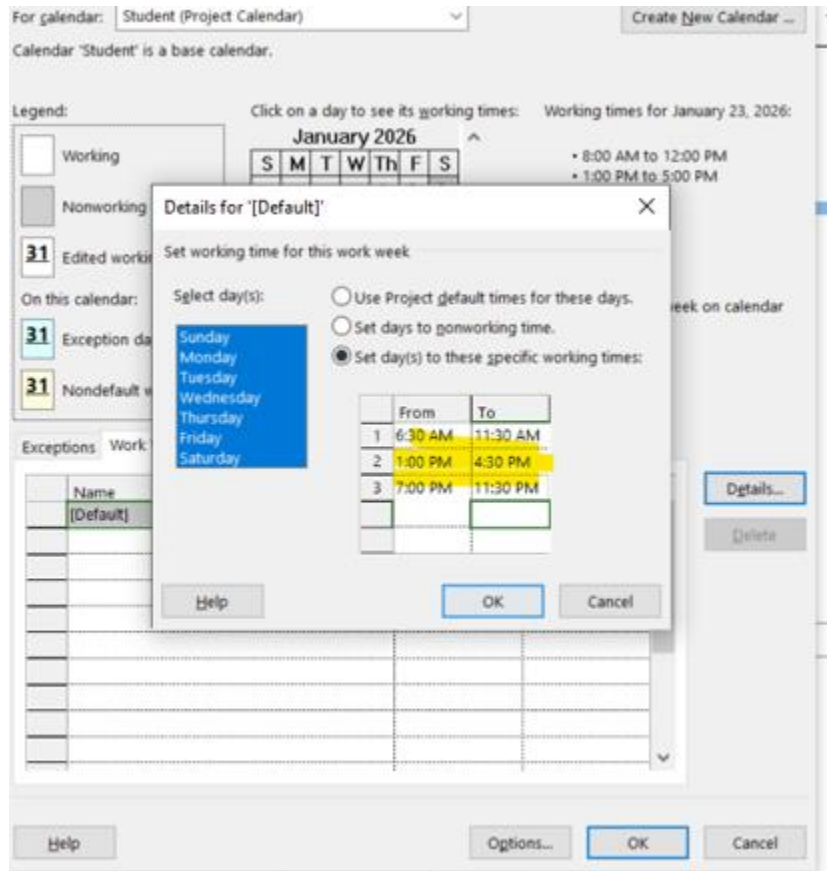


Lab report – Project Management


Module 3: Working with Tasks

Exercise 1: Changing Working Time (Start Date Feb 2st 2026)

Display the Project Information.

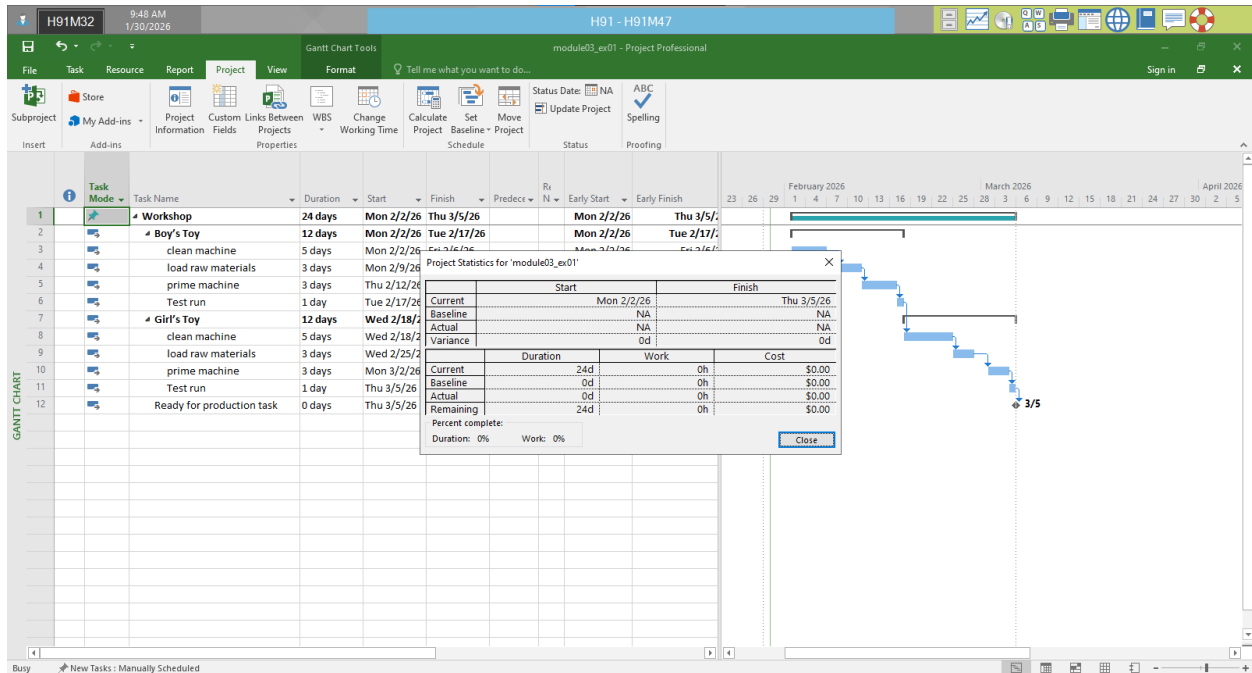


View Project Timeline

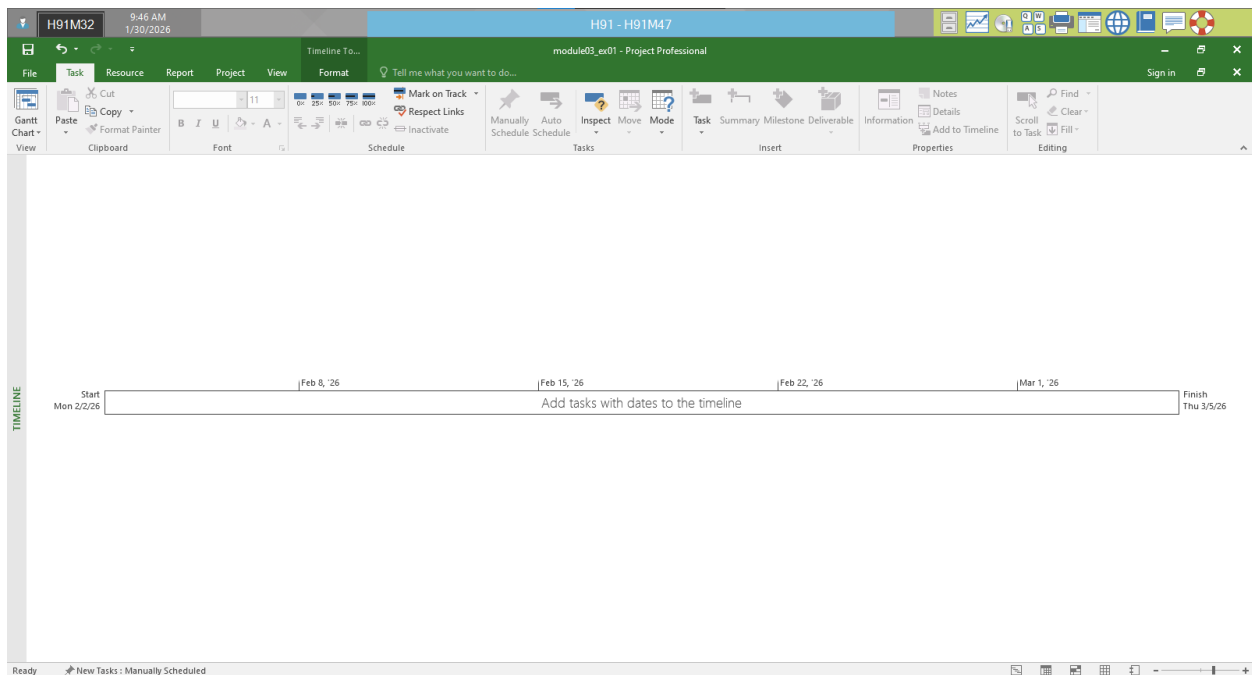


Lab report – Project Management

Gantt Chart

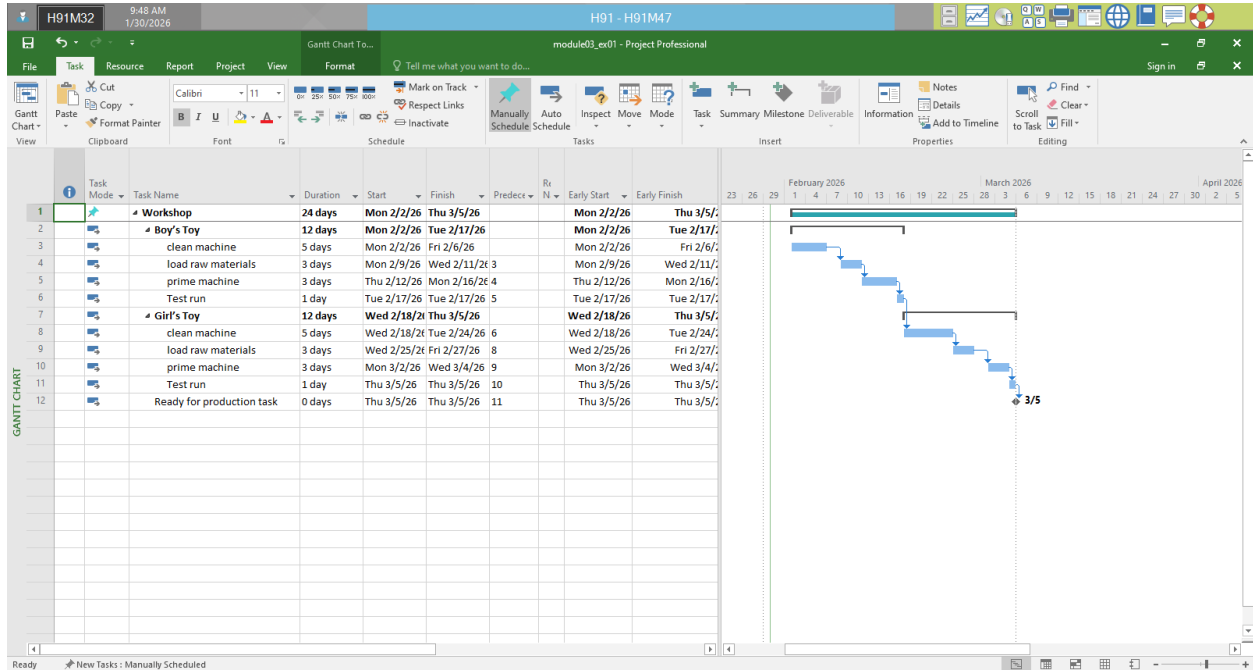


view CP

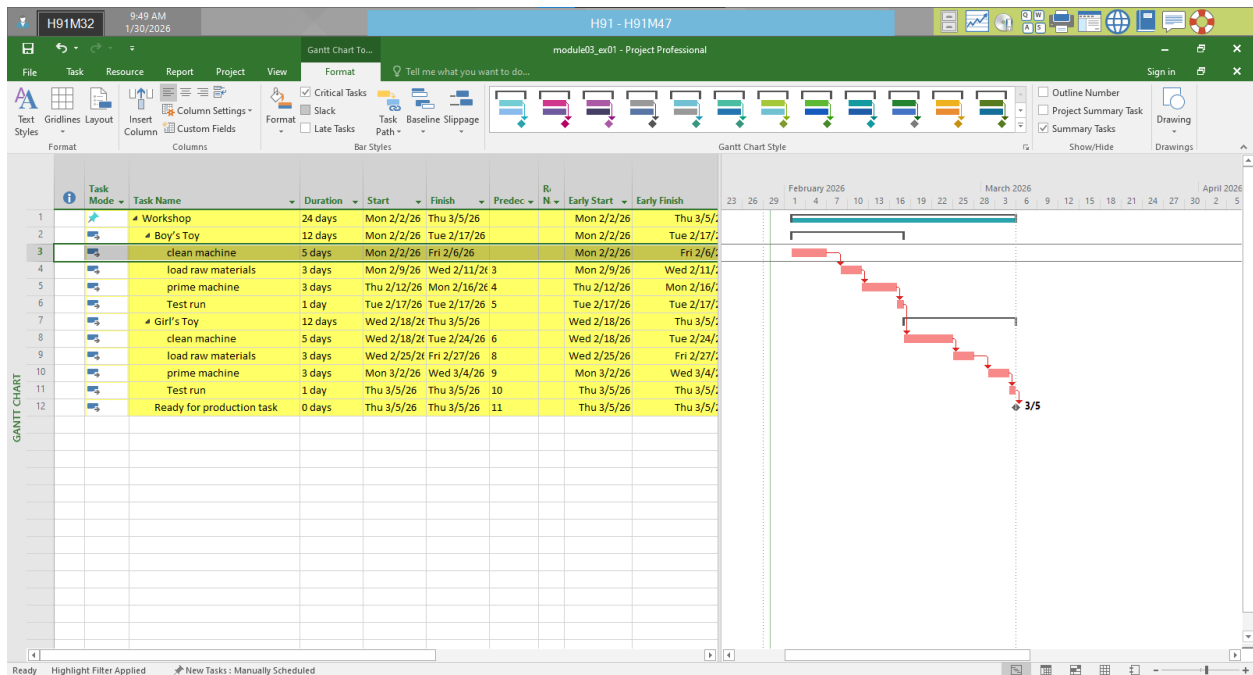


Total Slack

Lab report – Project Management

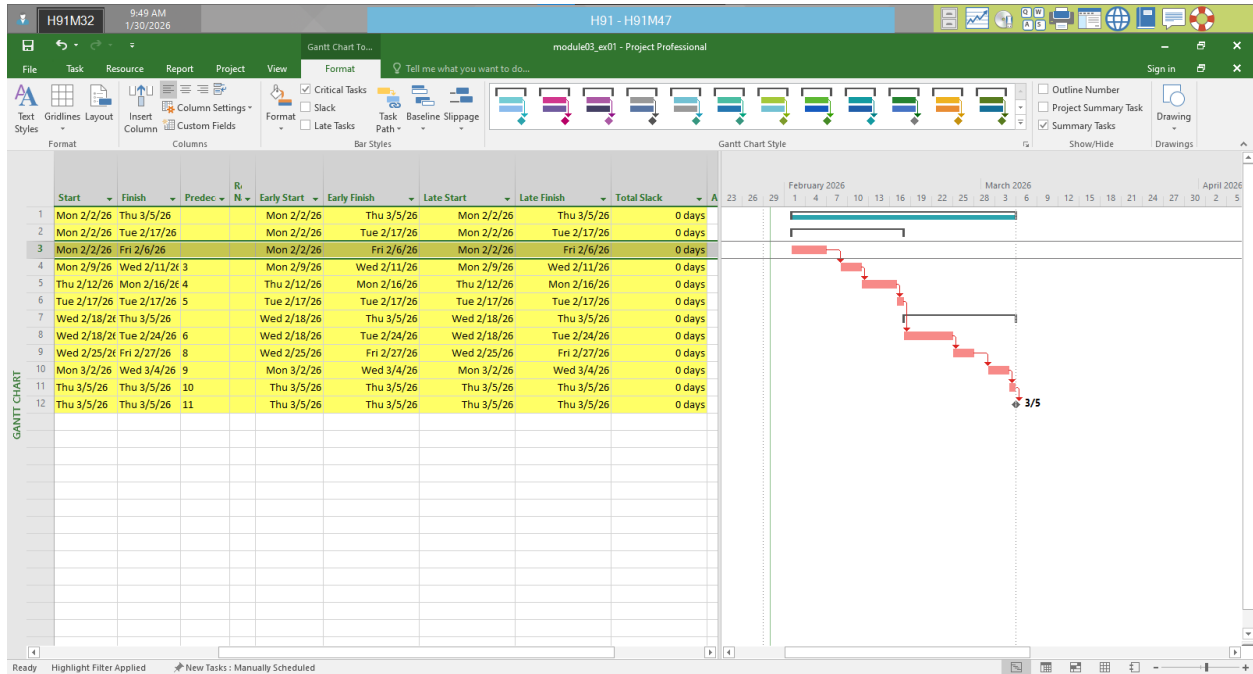


Exercise 2: Changing Working Time (Start Date Feb 2nd 2026)

Timeline

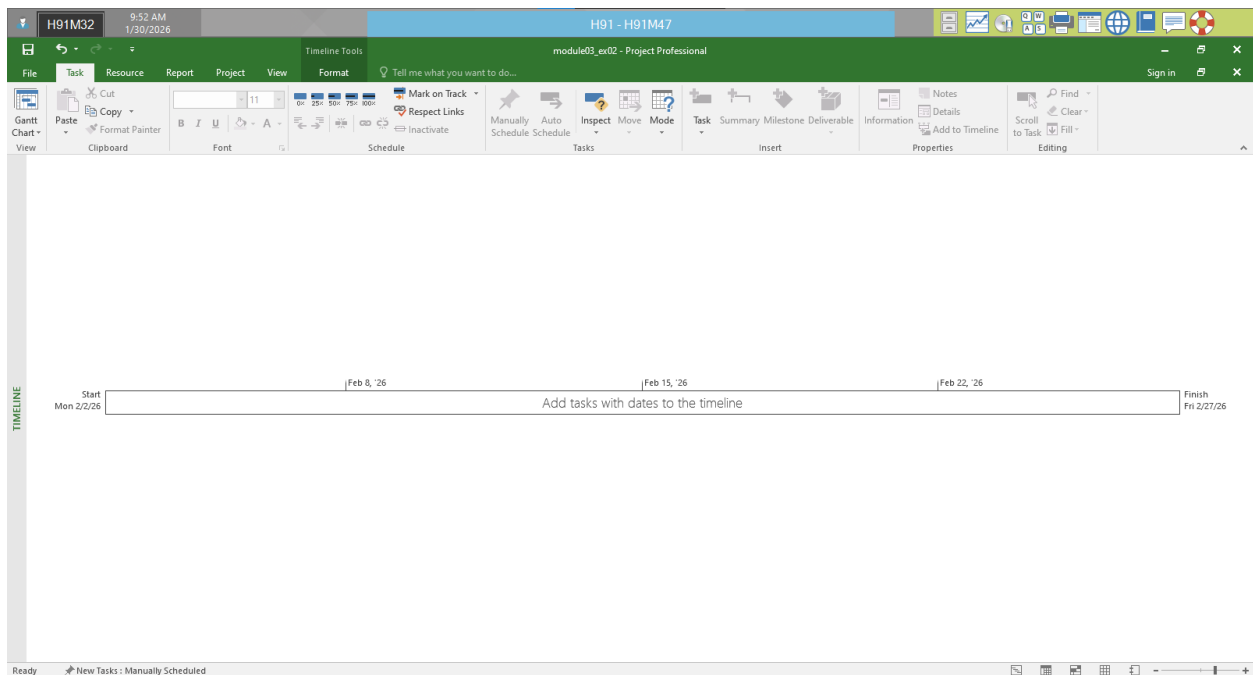


Gantt Chart

Lab report – Project Management

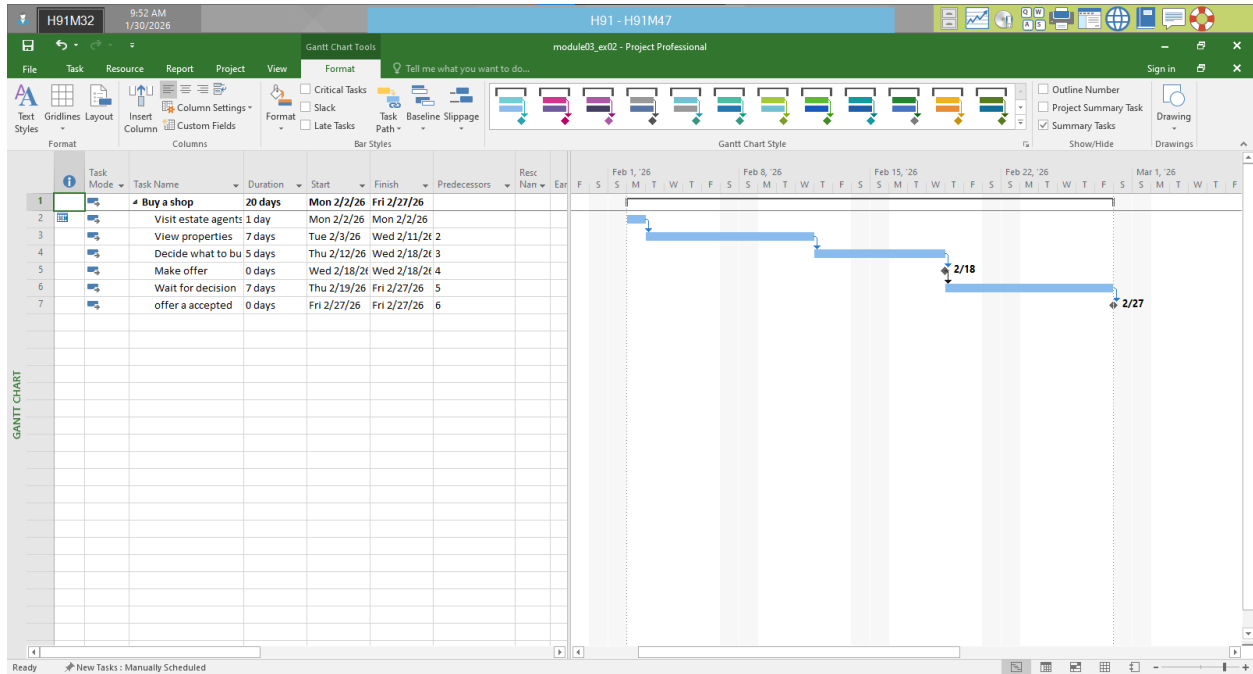


view CP

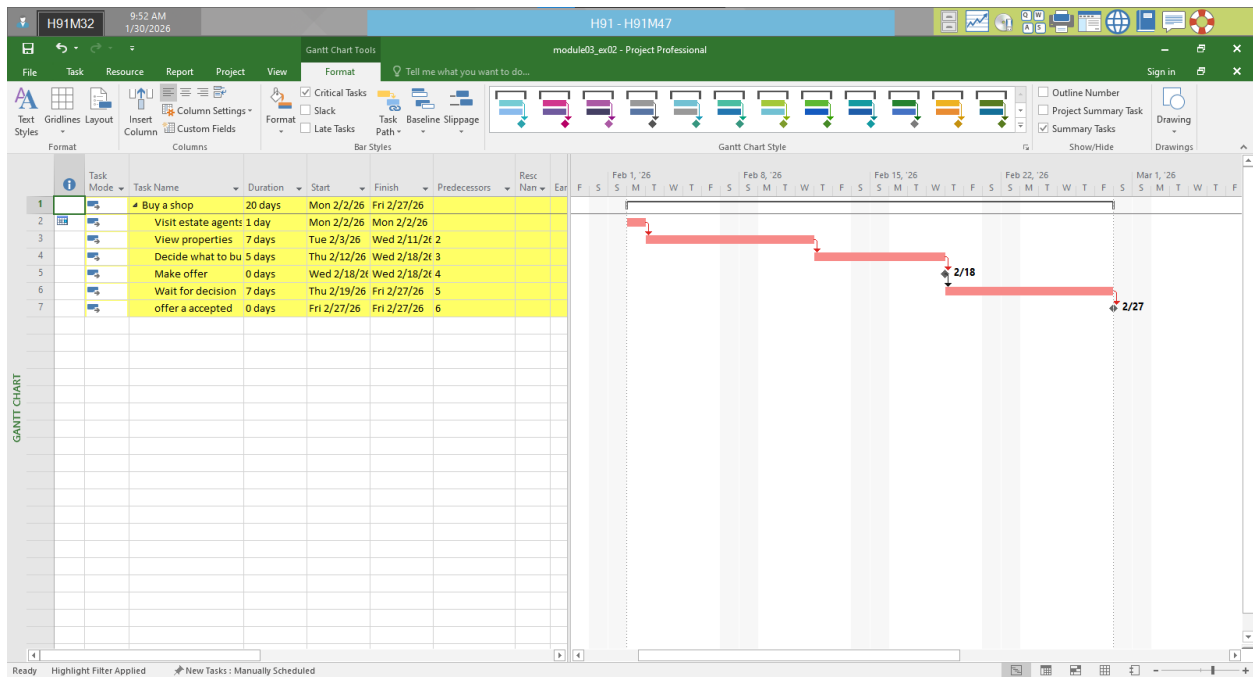


Total Slack

Lab report – Project Management

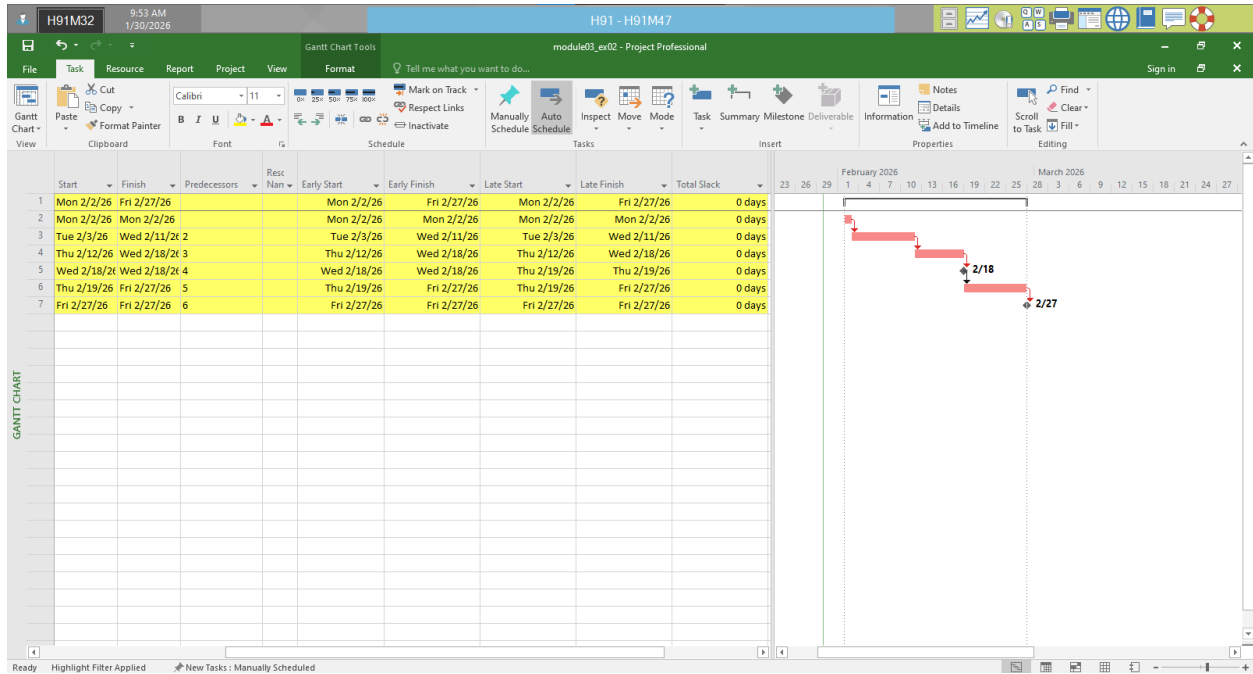



Exercise 3: Scheduling – Task dependencies

Display the Project Information.

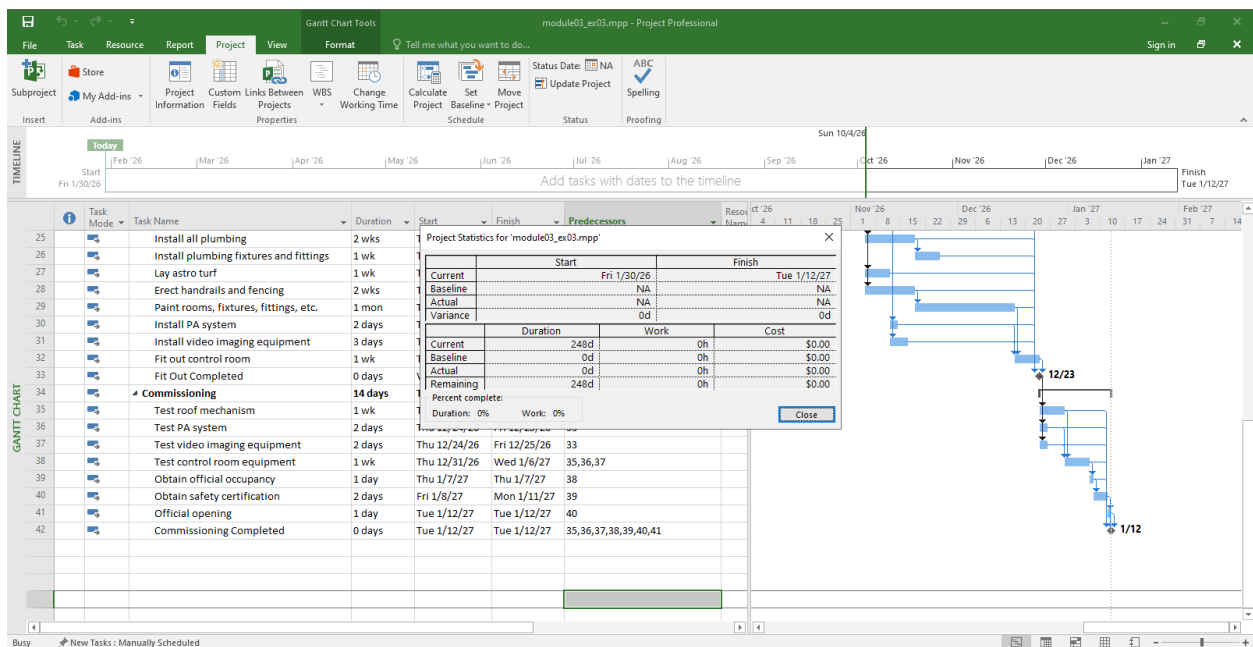


View the project in Gantt Chart and define CP and Project Slack


Lab report – Project Management

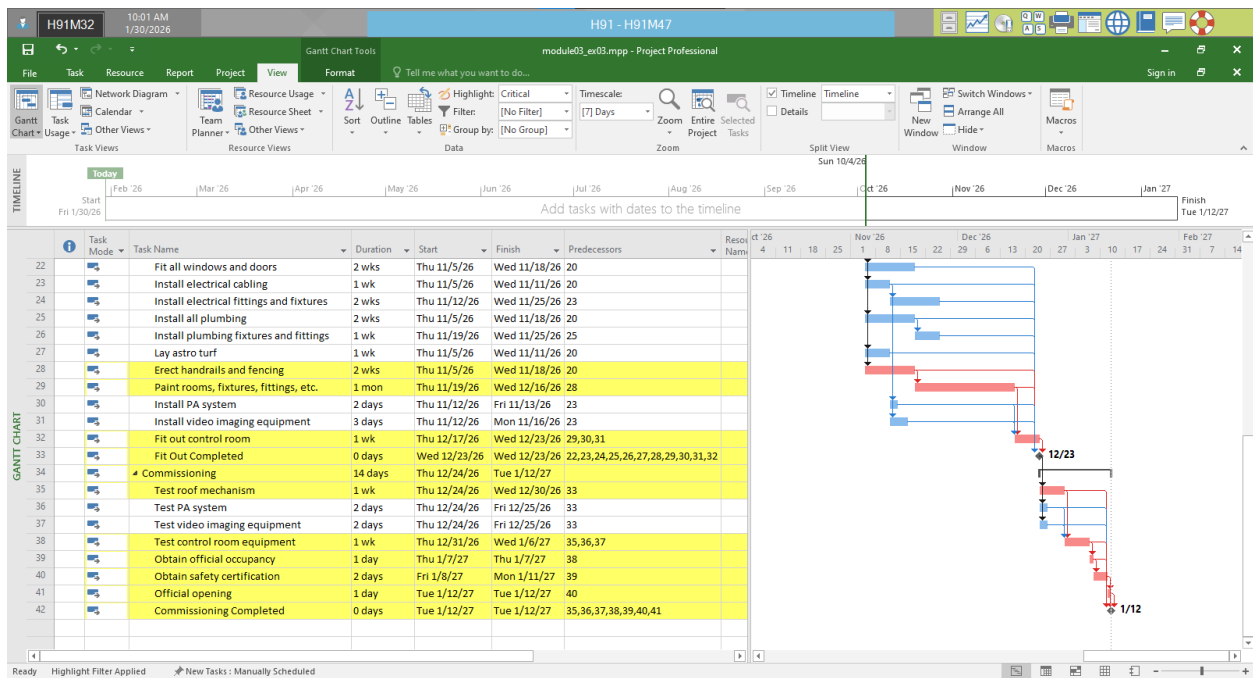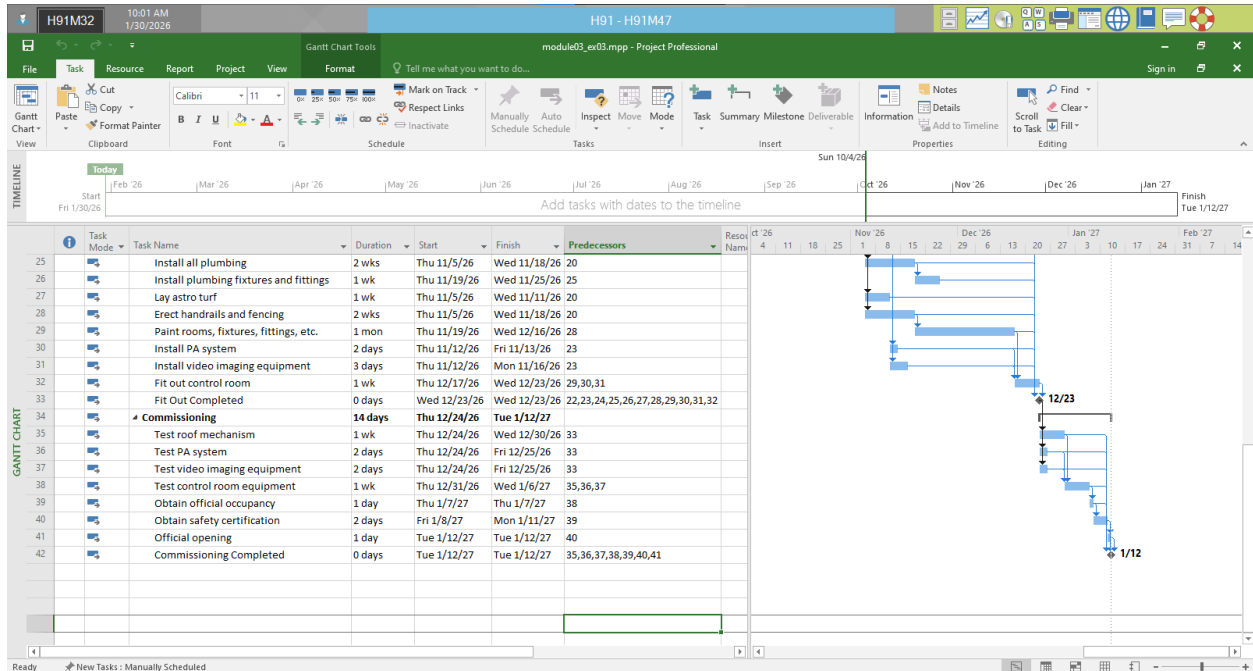

Lab report – Project Management


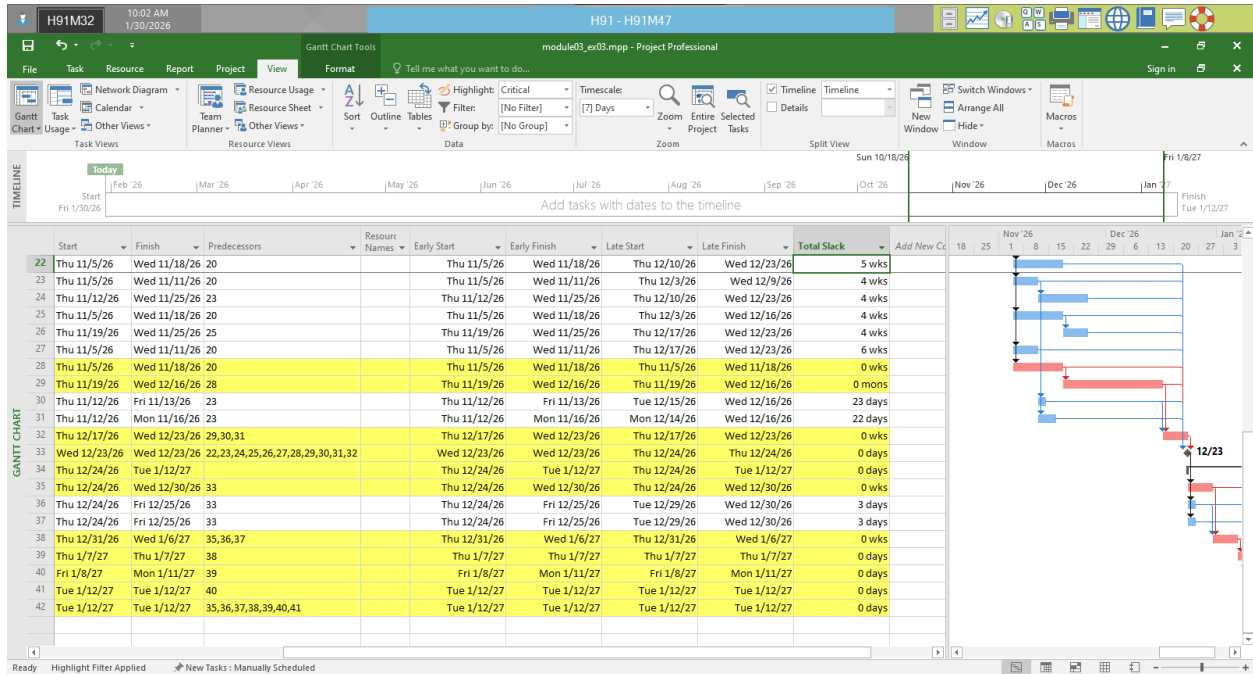


Choose Gantt Chart Format tab ◊ check on Critical Tasks in Bar Styles.

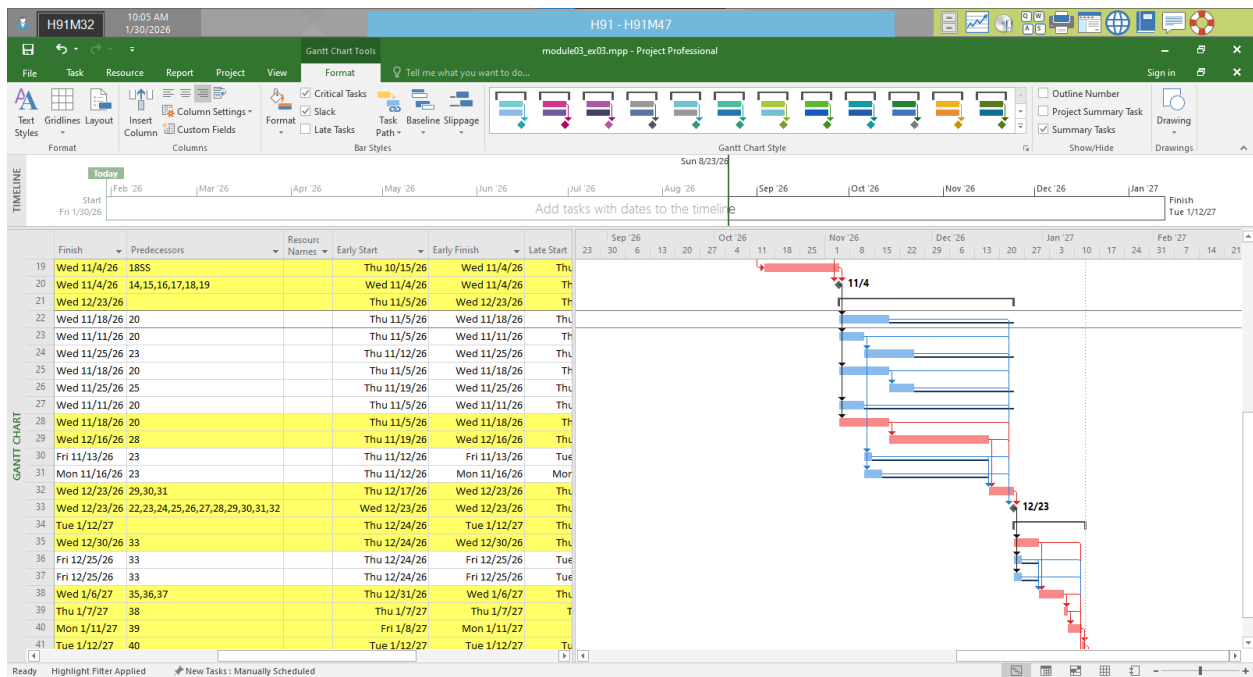

On the table data Add column Late Start, Late Finish, Total Slack


Lab report – Project Management

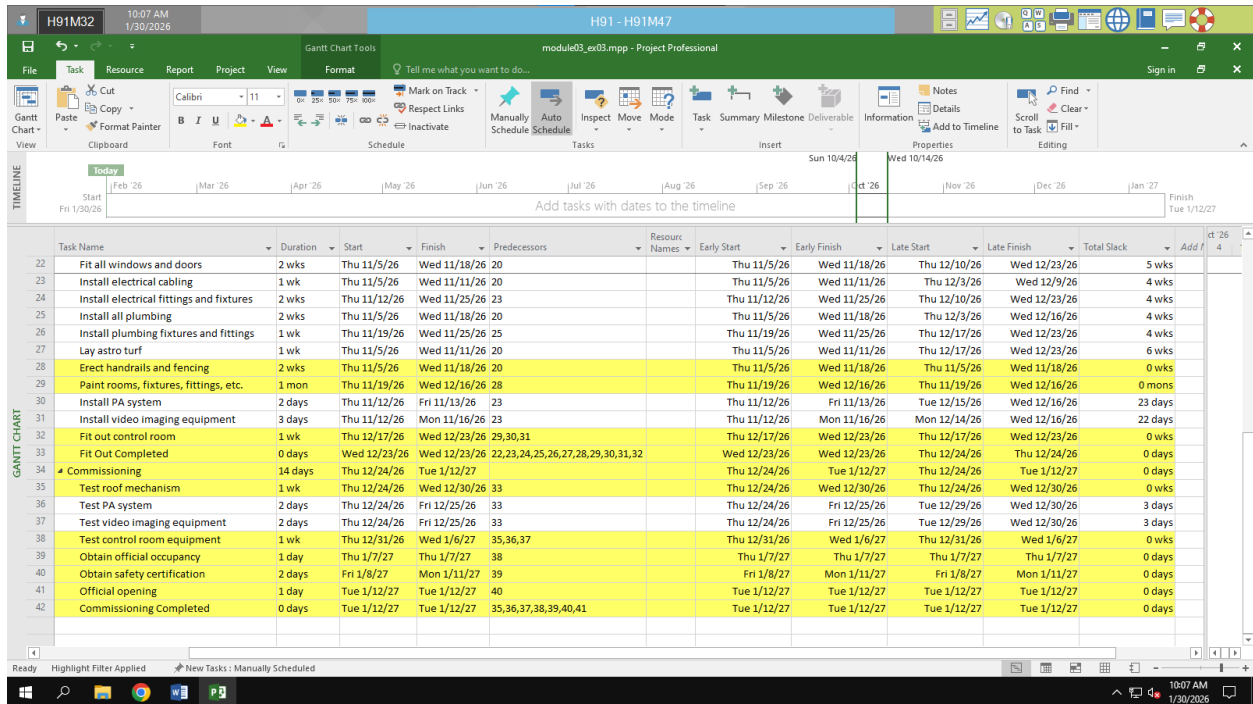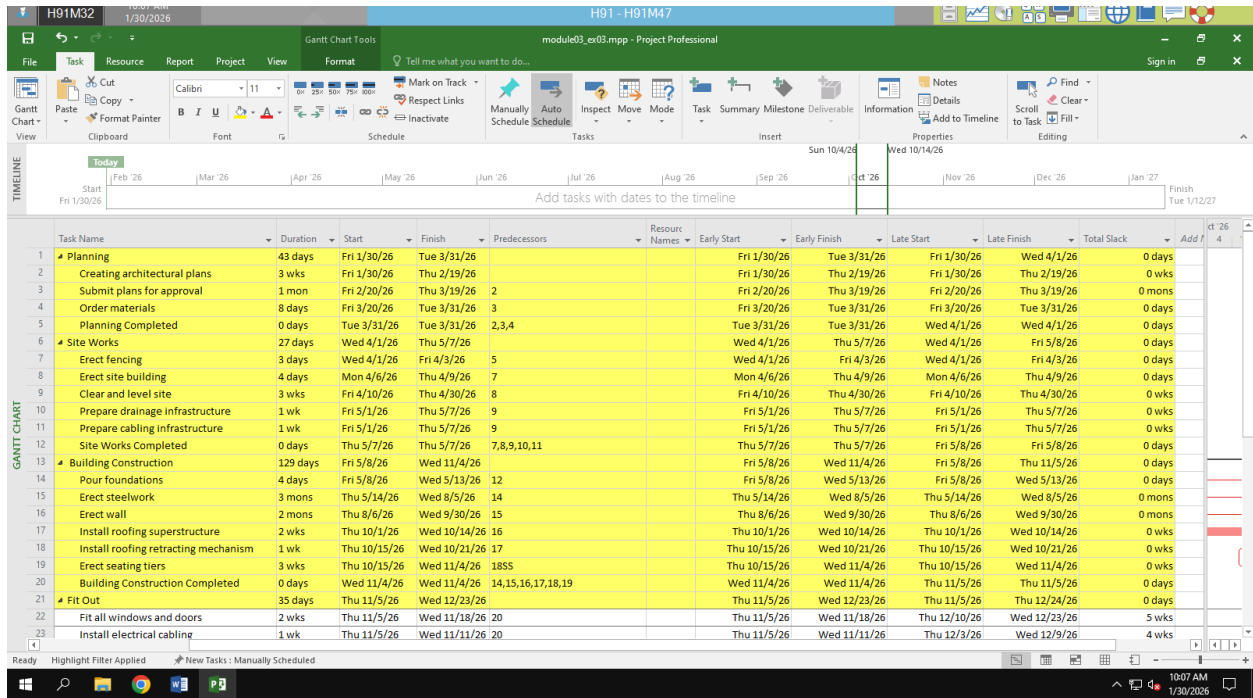

Module 4: Assigning resources to the tasks in Project

Exercise 1: Entering Resources

- Gantt Chart

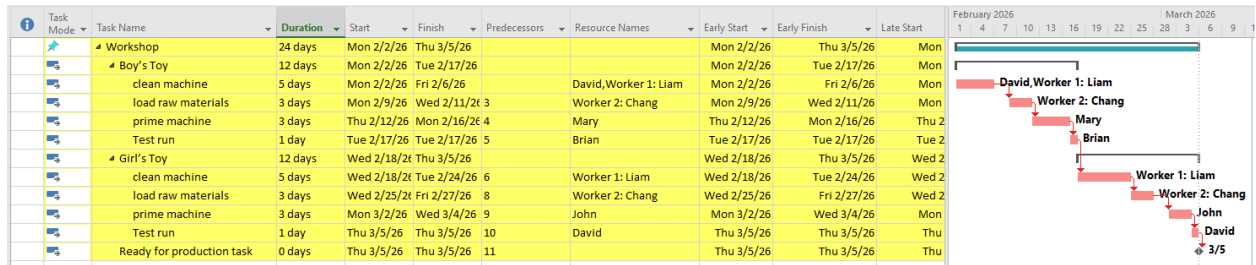

- Display the Project Information (Statics): Duration, Hours, Cost

Project Statistics for 'module04_ex01'

	Start	Finish
Current	Mon 2/2/26	Thu 3/5/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	24d	232h	\$1,544.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	24d	232h	\$1,544.00

Percent complete:

Duration: 0%Work: 0%

Close

- Resource Sheet

Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt.	Cost/Use	Accrue	Base
David	Work		D	Consultar	100%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Brian	Work		B	Staff	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Mary	Work		M	Staff	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
John	Work		J	Staff	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Worker 1: Liam	Work		W	Worker	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Worker 2: Chang	Work		W	Worker	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard

- Resource Usage

RESOURCE USAGE

- Gantt Chart (Resource Name, Cost Column)

Project Statistics for 'module04_ex02'

	Start	Finish
Current	Mon 2/2/26	Tue 3/3/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	22d	0h	\$780.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	22d	0h	\$780.00

Percent complete:

Duration: 0% Work: 0%

Close

Lab report – Project Management

- Resource Sheet

ew		Clipboard	Font	Font	Schedule		Tasks					
	i	Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt.	Cost/Use	Accrue	Base
1		MDF	Material	Sheet	M	Material		\$20.00		\$0.00	Prorated	
2		Flooring	Material	Pack	F	Material		\$80.00		\$0.00	Prorated	
3		Purple Material	Material	Roll	P	Material		\$30.00		\$0.00	Prorated	
4		Orange Material	Material	Roll	O	Material		\$120.00		\$0.00	Prorated	

- Resource Usage

Paste		Format Painter		B I U		Font		Schedule		Manually Schedule		Auto Schedule		Inspect M	
Clipboard														Tasks	
i		Resource Name		Work		Add New Column		Details		M		T		W	
1		MDF		2 Sheet				Work (Sheet)							
		Visit estate a		2 Sheet				Work (Sheet)							
2		Flooring		4 Pack				Work (Pack)							
		View propert		2 Pack				Work (Pack)							
		Make offer		1 Pack				Work (Pack)							
		Wait for decis		1 Pack				Work (Pack)							
3		Purple Material		2 Roll				Work (Roll)							
		Decide what i		1 Roll				Work (Roll)							
		Make offer		1 Roll				Work (Roll)							
4		Orange Material		3 Roll				Work (Roll)							
		Wait for decis		1 Roll				Work (Roll)							
		offer a accep		2 Roll				Work (Roll)							
								Work							
								Work							
								Work							

Exercise 3: Entering resources

- Gantt Chart (Resource Name, Cost Column)

	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost	
1		Planning	1 wk	Fri 3/13/26	Thu 3/19/26		PM	\$400.00	
2		Requirement documents	2 wks	Fri 3/20/26	Thu 4/2/26	1	Designer, PM	\$1,280.00	
3		Sign off	1 day	Fri 4/3/26	Fri 4/3/26	2	PM	\$80.00	
4		Development	10 wks	Mon 4/6/26	Fri 6/12/26	3	Developer, Operating System[1 Unit], Visual Studio[1 Unit]	\$3,322.00	
5		Testing	4 wks	Mon 6/15/26	Fri 7/10/26	4	Tester	\$960.00	
6		Implementation	2 wks	Mon 7/13/26	Fri 7/24/26	5	Maintainer, Cable[100 M], Operating System[1 Unit], Visual Studio[1 Unit]	\$622.00	
7		Review	1 wk	Mon 7/27/26	Fri 7/31/26	6	Maintainer, PM	\$600.00	

- Display the Project Information (Statics): Duration, Hours, Cost

Lab report – Project Management

	Start	Finish
Current	Fri 3/13/26	Fri 7/31/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	101d	928h	\$7,264.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	101d	928h	\$7,264.00

Percent complete:
Duration: 0% Work: 0%

Close

- Resource Sheet

	Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt.	Cost/Use	Accrue	Base	Code	Add New Column
1	PM	Work		P	Sponsor	100%	\$10.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
2	Designer	Work		D	Staff	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
3	Developer	Work		D	Staff	100%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
4	Tester	Work		T	Staff	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
5	Maintainer	Work		M	Staff	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
6	Operating System	Material	Unit	O	Material		\$120.00		\$0.00	Prorated			
7	Internet Provider	Material	Unit	I	Material		\$100.00		\$0.00	Prorated			
8	Cable	Material	M	C	Material		\$1.00		\$0.00	Prorated			
9	Visual Studio	Material	Unit	V	Material		\$2.00		\$0.00	Prorated			

- Resource Usage

	Resource Name	Work	Add New Column	Details	M	T	W	T	F	S	Mar 15, '26	M	T	W	T	F	S	Mar 22, '26	M	T	W	T
1	PM	168 hrs		Work					8h													
	Planning	40 hrs		Work					8h													
	Requirement	80 hrs		Work							8h	8h	8h	8h	8h							
	Sign off	8 hrs		Work												8h						
	Review	40 hrs		Work																		
2	Designer	80 hrs		Work												8h			8h	8h	8h	
	Requirement	80 hrs		Work												8h			8h	8h	8h	
3	Developer	400 hrs		Work																		
	Development	400 hrs		Work																		
4	Tester	160 hrs		Work																		
	Testing	160 hrs		Work																		
5	Maintainer	120 hrs		Work																		
	Implementat	80 hrs		Work																		
	Review	40 hrs		Work																		
6	Operating System	2 Unit		Work																		
	Development	1 Unit		Work																		
	Implementat	1 Unit		Work																		
7	Internet Provider	0 Unit		Work																		
8	Cable	100 M		Work																		
	Implementat	100 M		Work																		
9	Visual Studio	2 Unit		Work																		
	Development	1 Unit		Work																		
	Implementat	1 Unit		Work																		

Exercise 4: Entering resources

- Gantt Chart (Resource Name, Cost Column)

Lab report – Project Management

Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Ear	Ear	L	L	T	T	Cost	2027	2028	2029	2030	2031
1	Planning	88 days	Fri 1/30/26	Tue 6/2/26									\$5,280.00					
2	Creating architectural plans	12 wks	Fri 1/30/26	Thu 4/23/26		Architect, Building Clerk[25%							\$2,880.00					
3	Submit plans for approval	1 mon	Fri 4/24/26	Thu 5/21/26	2	Architect							\$1,440.00					
4	Order materials	8 days	Fri 5/22/26	Tue 6/2/26	3	Building Clerk, Draftsperson							\$960.00					
5	Planning Completed	0 days	Tue 6/2/26	Tue 6/2/26	2,3,4								\$0.00					
6	Site Works	32 days	Wed 6/3/26	Thu 7/16/26									\$5,288.00					
7	Erect fencing	3 days	Wed 6/3/26	Fri 6/5/26	5	No Barrier Fencing							\$72.00					
8	Erect site building	4 days	Mon 6/8/26	Thu 6/11/26	7	Carpenter[400%], Labourer, N							\$896.00					
9	Clear and level site	3 wks	Fri 6/12/26	Thu 7/2/26	8	Supervisor, Driver[200%], Gra							\$3,120.00					
10	Prepare drainage infrastructure	2 wks	Fri 7/3/26	Thu 7/16/26	9	Plumber[200%], Supervisor[5							\$680.00					
11	Prepare cabling infrastructure	1 wk	Fri 7/3/26	Thu 7/9/26	9	Electrician[300%], Supervisor							\$520.00					
12	Site Works Completed	0 days	Thu 7/16/26	Thu 7/16/26	7,8,9,10,11								\$0.00					
13	Building Construction	334 days	Fri 7/17/26	Wed 10/27/27									\$57,888.00					
14	Pour foundations	4 days	Fri 7/17/26	Wed 7/22/26	12	Rock Solid Concrete							\$128.00					
15	Erect steelwork	6 mons	Thu 7/23/26	Wed 6/6/27	14	Boilermaker[600%], Driver[20							\$25,920.00					
16	Erect wall	8 mons	Thu 7/23/26	Wed 6/6/27	15	Supervisor[50%], Carpenter[7							\$18,560.00					
17	Install roofing superstructure	4 wks	Thu 8/19/27	Wed 9/15/27	16	Supervisor[50%], Rigger[500%							\$5,280.00					
18	Install roofing retracting mechanism	2 wks	Thu 9/16/27	Wed 9/29/27	17	Supervisor[50%], Welder, Boil							\$2,000.00					
19	Erect seating tiers	6 wks	Thu 9/16/27	Wed 10/27/27	1855	Supervisor[50%], Carpenter[8							\$6,000.00					
20	Building Construction Completed	0 days	Wed 10/27/27	Wed 10/27/27	14,15,16,17								\$0.00					
21	Fit Out	14 days	Thu 10/28/27	Tue 11/16/27									\$6,120.00					
22	Fit all windows and doors	1 wk	Thu 10/28/27	Wed 11/3/27	20	Carpenter[500%], Labourer[20							\$1,040.00					
23	Install electrical cabling	0.5 wks	Thu 10/28/27	Mon 11/1/27	20	Electrician[300%], Labourer[2							\$520.00					

Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Ear	Ear	L	L	T	T	Cost	2027	2028	2029	2030	2031
22	Fit all windows and doors	1 wk	Thu 10/28/27	Wed 11/3/27	20	Carpenter[500%], Labourer[20							\$1,040.00					
23	Install electrical cabling	0.5 wks	Thu 10/28/27	Mon 11/1/27	20	Electrician[300%], Labourer[2							\$520.00					
24	Install electrical fittings and fixtures	0.67 wks	Mon 11/1/27	Thu 11/4/27	23	Electrician[300%]							\$560.00					
25	Install all plumbing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Plumber[200%], Labourer[200							\$880.00					
26	Install plumbing fixtures and fittings	0.5 wks	Thu 11/4/27	Mon 11/8/27	25	Plumber[200%]							\$200.00					
27	Lay astro turf	1 wk	Thu 10/28/27	Wed 11/3/27	20	Pure Grass Turf							\$200.00					
28	Erect handrails and fencing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Welder[400%], Boilermaker[2							\$880.00					
29	Paint rooms, fixtures, fittings, etc.	0.2 mons	Thu 11/4/27	Tue 11/9/27	28	Painter[500%]							\$960.00					
30	Install PA system	2 days	Mon 11/1/27	Thu 11/3/27	23	Listen Ear Audio							\$80.00					
31	Install video imaging equipment	3 days	Mon 11/1/27	Thu 11/4/27	23	In Focus Video							\$120.00					
32	Fit out control room	1 wk	Wed 11/10/27	Tue 11/16/27	29,30,31	Electrician[200%], Listen Ear							\$680.00					
33	Fit Out Completed	0 days	Tue 11/16/27	Tue 11/16/27	22,23,24,25								\$0.00					
34	Commissioning	33.5 days	Wed 11/17/27	Mon 1/3/28									\$3,160.00					
35	Test roof mechanism	1 wk	Wed 11/17/27	Tue 11/23/27	33	Supervisor, Electrician[200%]							\$960.00					
36	Test PA system	2 days	Wed 11/17/27	Thu 11/18/27	33	Listen Ear Audio							\$80.00					
37	Test video imaging equipment	2 days	Wed 11/17/27	Thu 11/18/27	33	In Focus Video							\$80.00					
38	Test control room equipment	5 wks	Wed 11/24/27	Tue 12/28/27	35,36,37	Supervisor, Listen Ear Audio							\$1,520.00					
39	Obtain official occupancy	1 day	Wed 12/29/27	Wed 12/29/27	38	Architect, Building Clerk, Supe							\$232.00					
40	Obtain safety certification	2 days	Thu 12/30/27	Fri 12/31/27	39	Supervisor							\$192.00					
41	Official opening	0.5 days	Mon 1/3/28	Mon 1/3/28	40	Supervisor[200%]							\$96.00					
42	Commissioning Completed	0 days	Mon 1/3/28	Mon 1/3/28	35,36,37,38								\$0.00					

- Display the Project Information (Statics): Duration, Hours, Cost

Project Statistics for 'module04_ex04'			
	Start	Finish	
Current	Fri 1/30/26	Mon 1/3/28	
Baseline	NA	NA	
Actual	NA	NA	
Variance	0d	0d	
	Duration	Work	Cost
Current	501.5d	11,212h	\$77,736.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	501.5d	11,212h	\$77,736.00
Percent complete:			
Duration: 0%		Work: 0%	
Close			

- Resource Sheet

Lab report – Project Management

		Resource Name	Type	Material Label	Initials	Group	Max. Units	Std. Rate	Ovt.	Cost/Use	Accrue	Base
1		Architect	Work		Arc	Consultant	100%	\$9.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
2		Draftsperson	Work		Dft	Staff	200%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
3		Building Clerk	Work		BC	Staff	100%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
4		Supervisor	Work		Sup	Staff	100%	\$12.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
5		Rigger	Work		Rig	Wages	600%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
6		Boilermaker	Work		BM	Wages	600%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
7		Welder	Work		Weld	Wages	500%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
8		Carpenter	Work		Car	Wages	800%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
9		Painter	Work		Ptr	Wages	500%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
10		Labourer	Work		Lab	Wages	1,000%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
11		Driver	Work		Drv	Wages	300%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
12		No Barrier Fencing	Work		NBF	Contractor	100%	\$3.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
13		Rock Solid Concrete	Work		RSC	Contractor	100%	\$4.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
14		Listen Ear Audio	Work		LEA	Contractor	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
15		In Focus Video	Work		IFV	Contractor	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
16		Pure Grass Turf	Work		PGT	Contractor	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
17		Building Inspector	Work		BI	Government	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
18		High Jib Crane	Work		HJC	Equipment	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
19		Grader	Work		Grd	Equipment	200%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
20		Air Compressor	Work		AC	Equipment	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
21		Utility	Work		Ute	Equipment	200%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
22		Electrician	Work		Cap	Staff	400%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
23		Plumber	Work		Plu	Staff	400%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
24		Astro Turf	Material	Square Matre	Grass	Material		\$12.00		\$0.00	Prorated	
25		Paint	Material	Ultra	Paint	Ita		\$20.00		\$0.00	Prorated	

- Resource Usage

	Resource Name	Work	Add New Column	Details	H1	2025 H2	H1	2026 H2	H1	2027 H2	H1	2028 H2	H1	2029 H2
	Unassigned	0 hrs		Work										
	Planning Con	0 hrs		Work										
	Site Works Co	0 hrs		Work										
	Building Cons	0 hrs		Work										
	Fit Out Comp	0 hrs		Work										
	Commissioni	0 hrs		Work										
1	Architect	328 hrs		Work			280h			48h				
	Creating arch	120 hrs		Work			120h							
	Submit plans	160 hrs		Work			160h							
	Test control r	40 hrs		Work						40h				
	Obtain offic	8 hrs		Work						8h				
2	Draftsperson	184 hrs		Work			184h							
	Creating arch	120 hrs		Work			120h							
	Order materi	64 hrs		Work			64h							
3	Building Clerk	192 hrs		Work			184h			8h				
	Creating arch	120 hrs		Work			120h							
	Order materi	64 hrs		Work			64h							
	Obtain offic	8 hrs		Work						8h				
4	Supervisor	1,364 hrs		Work			136h	540h	336h	344h	8h			
	Erect site buil	32 hrs		Work			32h							
	Clear and lev	120 hrs		Work			104h	16h						
	Prepare drain	40 hrs		Work				40h						
	Prepare cabli	20 hrs		Work				20h						
	Erect steelwo	480 hrs		Work			464h	16h						

Exercise 5: Resources with the private working time

- Cô không cho làm

Exercise 6: The Engagement planning

- Cô không cho làm
