

LAB REPORT

Software Project Management



Student Name: Nguyễn Văn Minh

ID: 22003405

Class: DHKTPM18

Course: 2025-2026

Contents


Module 1:	3
Exercise 1: Creating a link	3
Exercise 2: Setting duration	3
Exercise 3: Creating phases	4
Exercise 4: Noah - Linking	5
Exercise 5: Pyramid - Multi level grouping.....	6
Exercise 6: Creating a plan for Staff Training	7
Exercise 7: Recurring Tasks	8
Exercise 8: Travelling – tasks calendar.....	9
Module 2:	10
Exercise 1: Part Time - creating new calendar	10
Exercise 2: Changing Working Time	15
Exercise 3: Changing Working Time	20
Exercise 4: Changing Working Time	24
Exercise 5: Create the private Time for a project	27
Exercise 6: My project	31
Module 3: Working with Tasks	33
Exercise 1: Changing Working Time (Start Date Feb 2st 2026)	33
Exercise 2: Changing Working Time (Start Date Feb 2rd 2026)	35
Exercise 3: Scheduling – Task dependencies.....	37
Module 4: Assigning resources to the tasks in Project	41
Exercise 1: Entering Resources.....	41
Exercise 2: Entering resources	42
Exercise 3: Entering resources	43
Exercise 4: Entering resources	44
Exercise 5: Resources with the private working time	46
Exercise 6: The Engagement planning.....	48
Module 5: COST, CONSTRAINS, DEADLINE for TASKs	51
Exercise 1: Entering Cost.....	51
Exercise 2:.....	52

Lab report – Project Management

Exercise 3:.....	53
Exercise 4:.....	54
Module 6:	57
Exercise 1:.....	57


Module 1:

Exercise 1: Creating a link

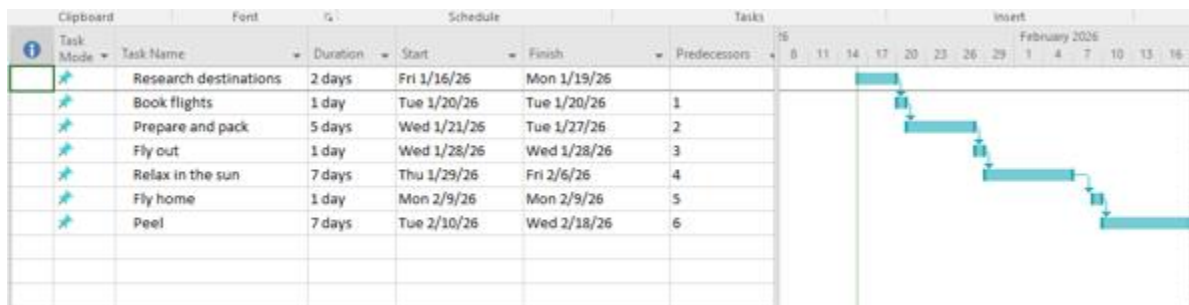


Project Statistics for 'Project1'

	Start	Finish	
Current	Fri 1/16/26	Wed 2/18/26	
Baseline	NA	NA	
Actual	NA	NA	
Variance	0d	0d	
	Duration	Work	Cost
Current	24d?	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	24d?	0h	\$0.00
Percent complete:			
Duration: 0% Work: 0%			
			Close



Exercise 2: Setting duration


Lab report – Project Management

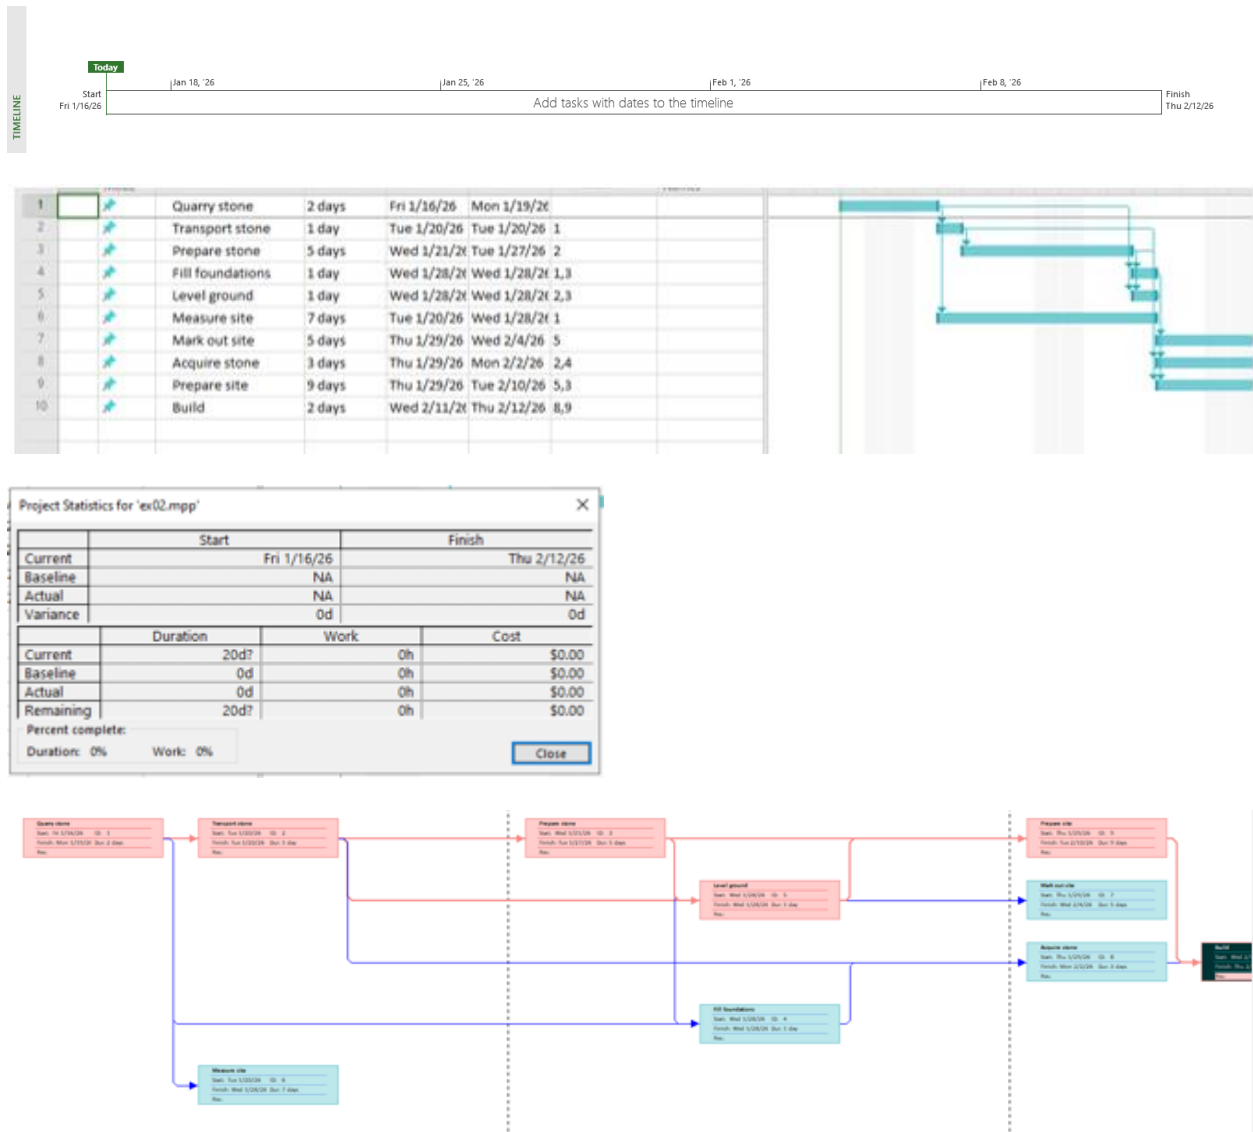

Exercise 3: Creating phases

Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jan 11, '26	S	S	M	T	W	T	F
	Pre-heat oven	5 mins	Fri 1/16/26	Fri 1/16/26										
	Prepare meat	5 mins	Fri 1/16/26	Fri 1/16/26	1									
	Prepare veg	5 mins	Fri 1/16/26	Fri 1/16/26	2									
	Heat pan	5 mins	Fri 1/16/26	Fri 1/16/26	3									
	Fry veg	5 mins	Fri 1/16/26	Fri 1/16/26	4									
	Brown meat	5 mins	Fri 1/16/26	Fri 1/16/26	5									
	Add stock and bring to a simmer	5 mins	Fri 1/16/26	Fri 1/16/26	6									
	Cook in oven	45 mins	Fri 1/16/26	Fri 1/16/26	7									

Lab report – Project Management

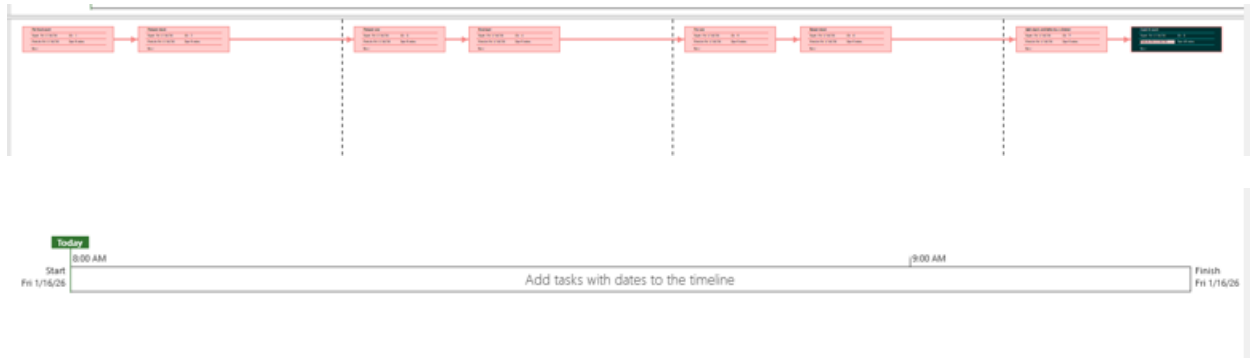

Project Statistics for 'ex03.mpp'

	Start	Finish
Current	Fri 1/16/26	Fri 1/16/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d


	Duration	Work	Cost
Current	0.17d?	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	0.17d?	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%


Close

Exercise 4: Noah - Linking

	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Resource Names
1		Build boat	7 days	Fri 1/16/26	Mon 1/26/26		
2		Load supplies	3 days	Tue 1/27/26	Thu 1/29/26	1	
3		Load family	6 days	Tue 1/27/26	Tue 2/3/26	1	
4		Load animals	7 days	Tue 1/27/26	Wed 2/4/26	1	
5		Collect animals A-M	12 days	Thu 2/5/26	Fri 2/20/26	1,4	
6		Collect animals N-Z	10 days	Thu 2/5/26	Wed 2/18/26	2,4	
7		Float around	7 days	Mon 2/23/26	Tue 3/3/26	5,6	



Lab report – Project Management

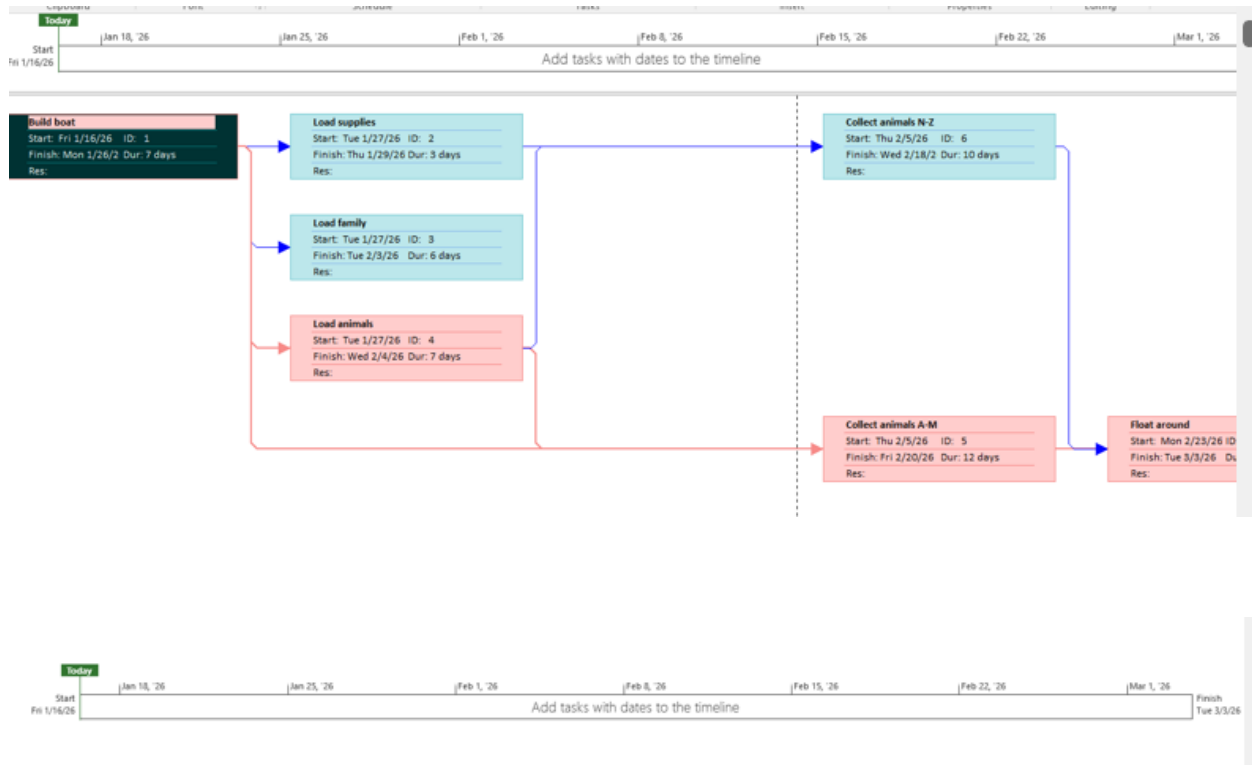

Project Statistics for 'ex04.mpp'


	Start	Finish
Current	Fri 1/16/26	Tue 3/3/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	33d?	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	33d?	0h	\$0.00


Percent complete:
Duration: 0% Work: 0%

Close

Exercise 5: Pyramid - Multi level grouping

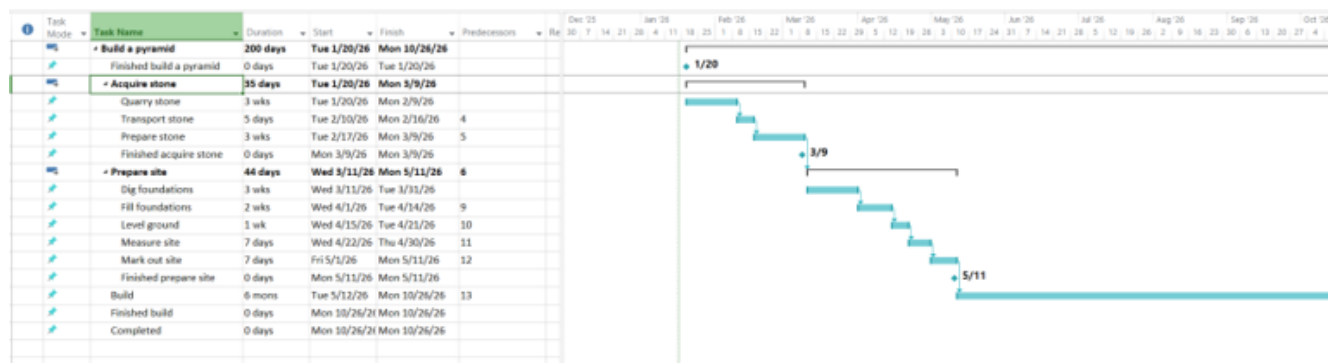

Lab report – Project Management

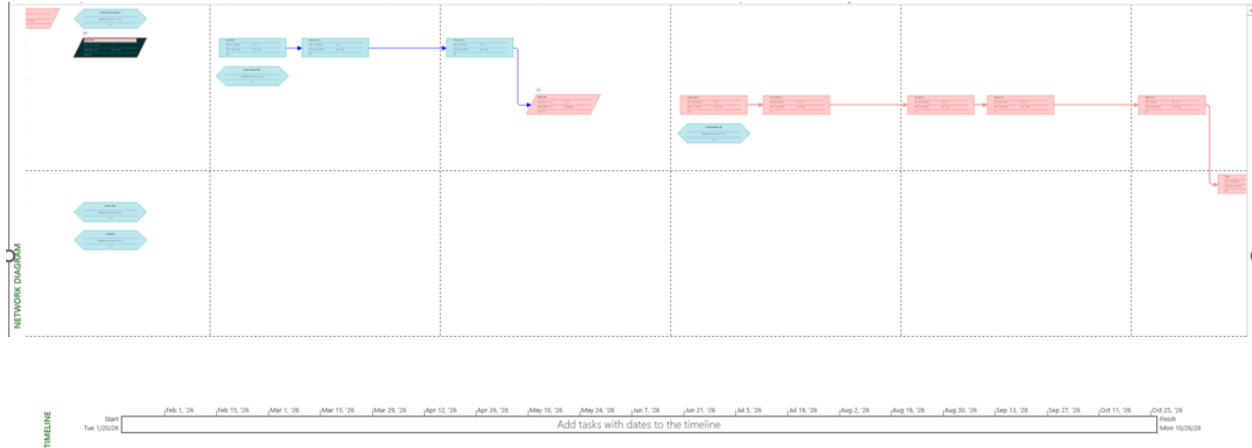

Project Statistics for 'ex05.mpp'

	Start	Finish	
Current	Tue 1/20/26	Mon 10/26/26	
Baseline	NA	NA	
Actual	NA	NA	
Variance	0d	0d	


	Duration	Work	Cost
Current	200d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	200d	0h	\$0.00

Percent complete:

Duration: 0%Work: 0%

Close

Exercise 6: Creating a plan for Staff Training

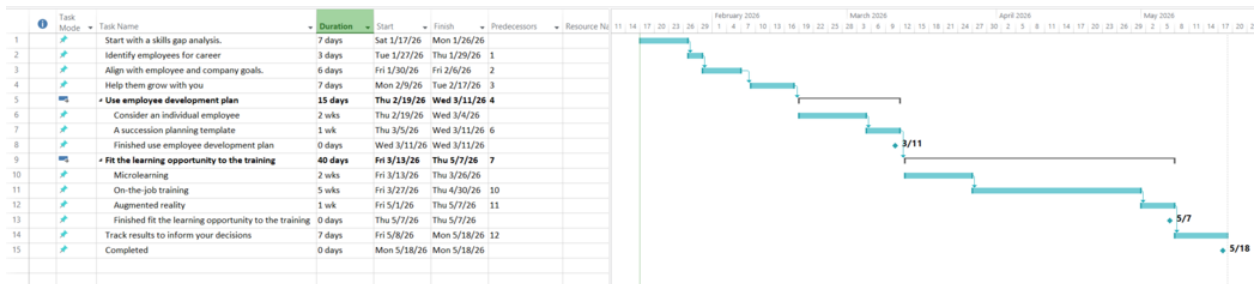

Lab report – Project Management


Project Statistics for 'ex06.mpp'

	Start	Finish
Current	Sat 1/17/26	Mon 5/18/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d


	Duration	Work	Cost
Current	86d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	86d	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%


Close

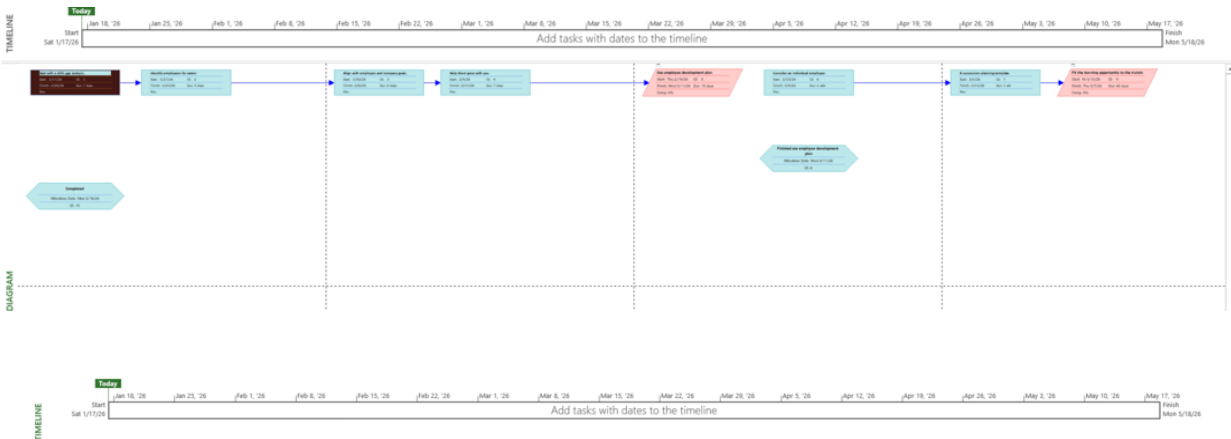

Exercise 7: Recurring Tasks

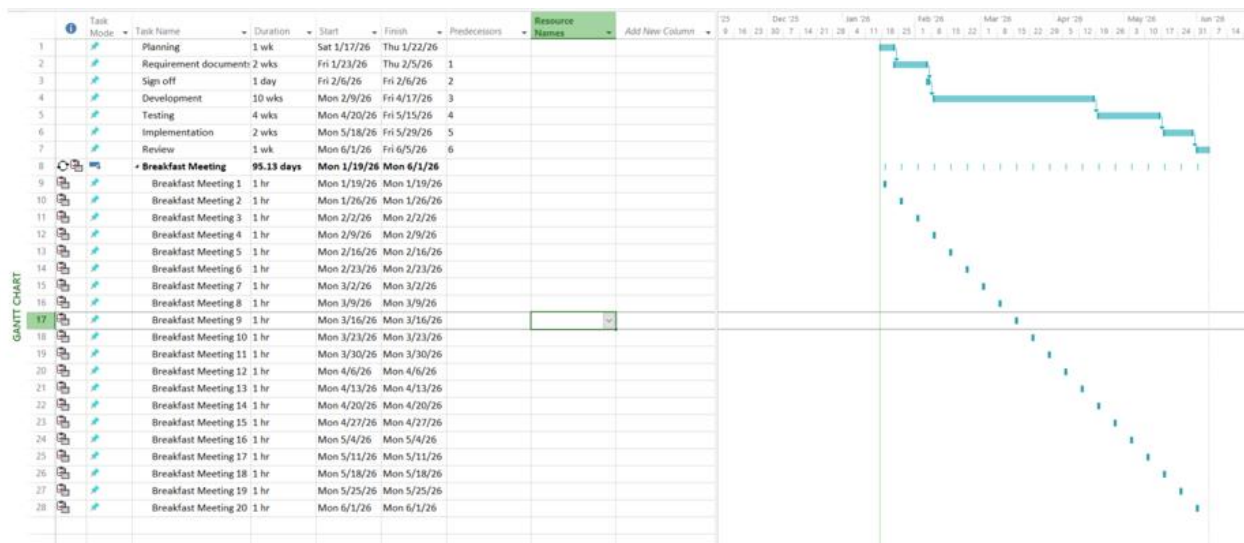

Lab report – Project Management

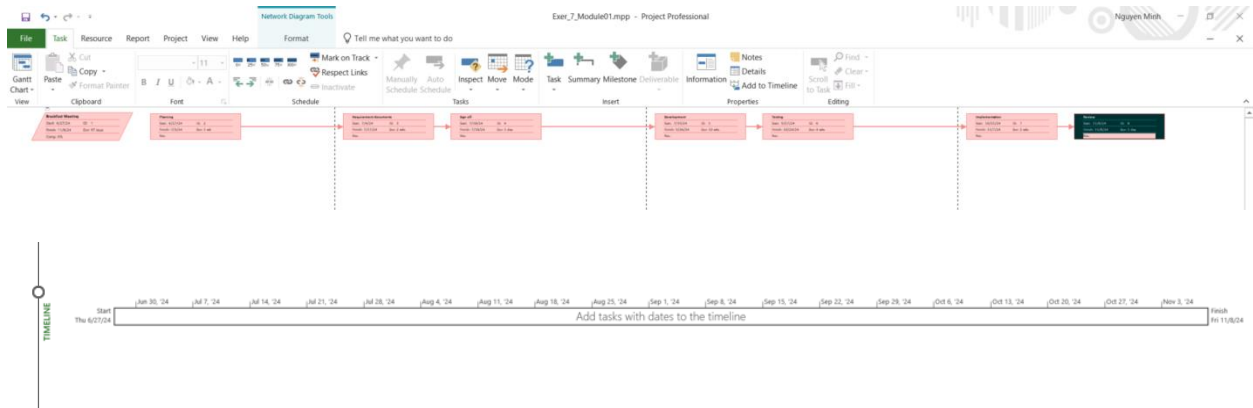

Project Statistics for 'ex07.mpp'

	Start	Finish
Current	Sat 1/17/26	Fri 6/5/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d


	Duration	Work	Cost
Current	100d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	100d	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close

Exercise 8: Travelling – tasks calendar

Travelling – task calendar You intend to travel from HCM to Kuala Lumpur, Bangkok and then, come back to HCM. Creating a plan for your trip.

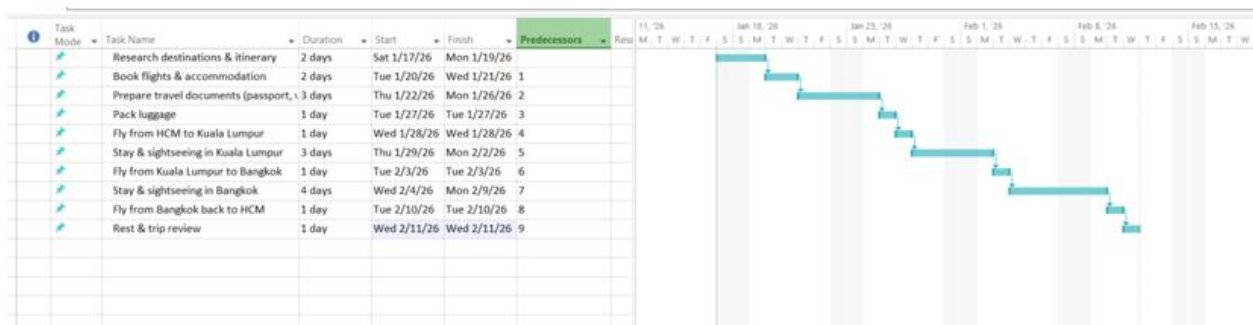

Lab report – Project Management


Project Statistics for 'ex08.mpp'

	Start	Finish
Current	Sat 1/17/26	Wed 2/11/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	18d?	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	18d?	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close

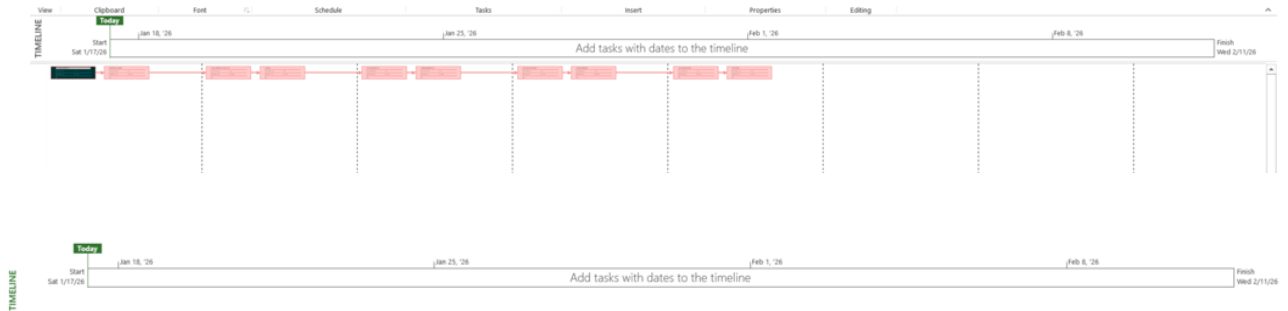

Module 2:


Exercise 1: Part Time - creating new calendar

Part Time - creating new calendar

Open project file Ex2 (Module 1), Use the Project Information dialog box to:

Lab report – Project Management


A part-time worker will be used on this project. Go to the Change Working Time dialog box and create a new copy of the Standard calendar, calling it "Part Time".

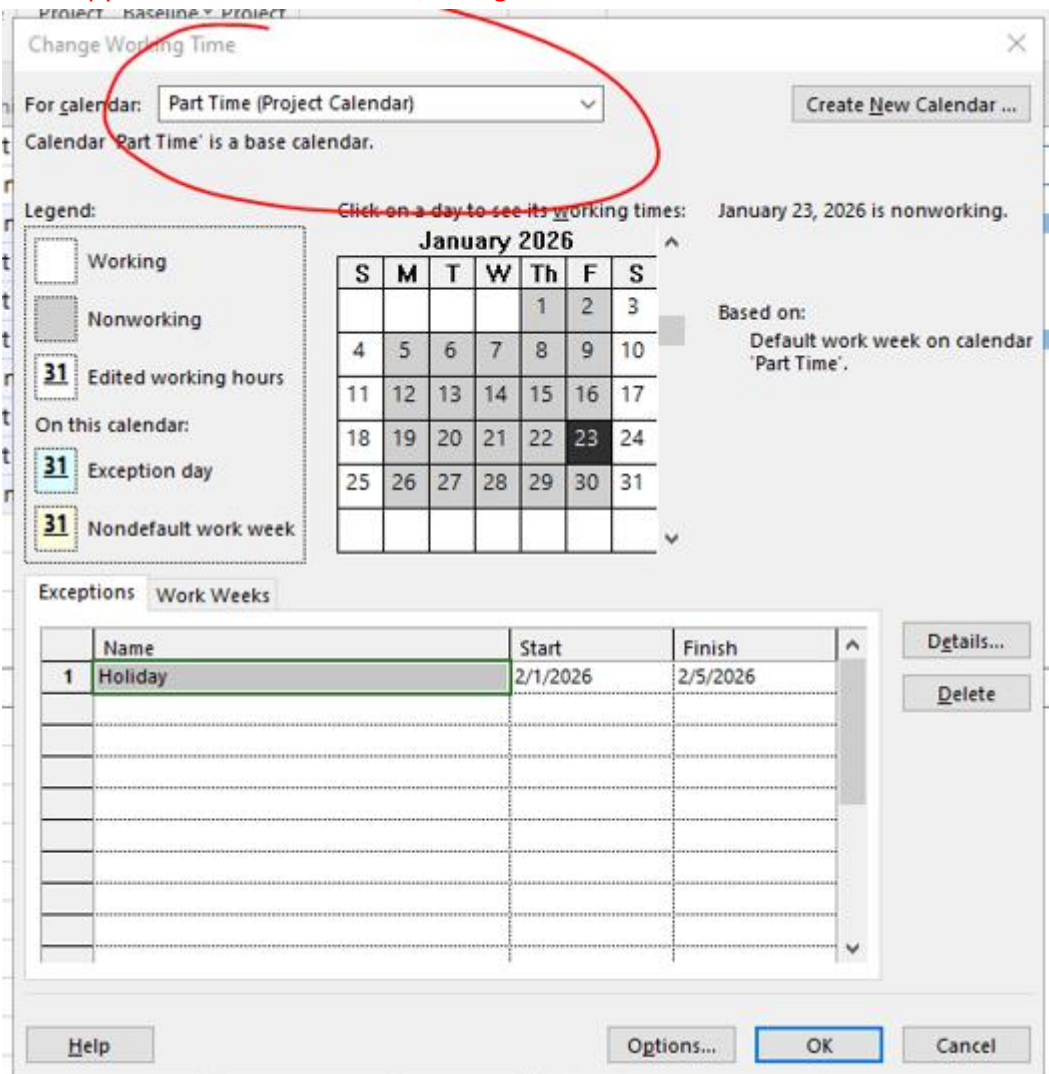


Update the working time of your new calendar so that:

- Mondays to Fridays are nonworking time
- The remaining 2 weekdays have working time of 10:00 to 16:00 (no breaks)

Lab report – Project Management

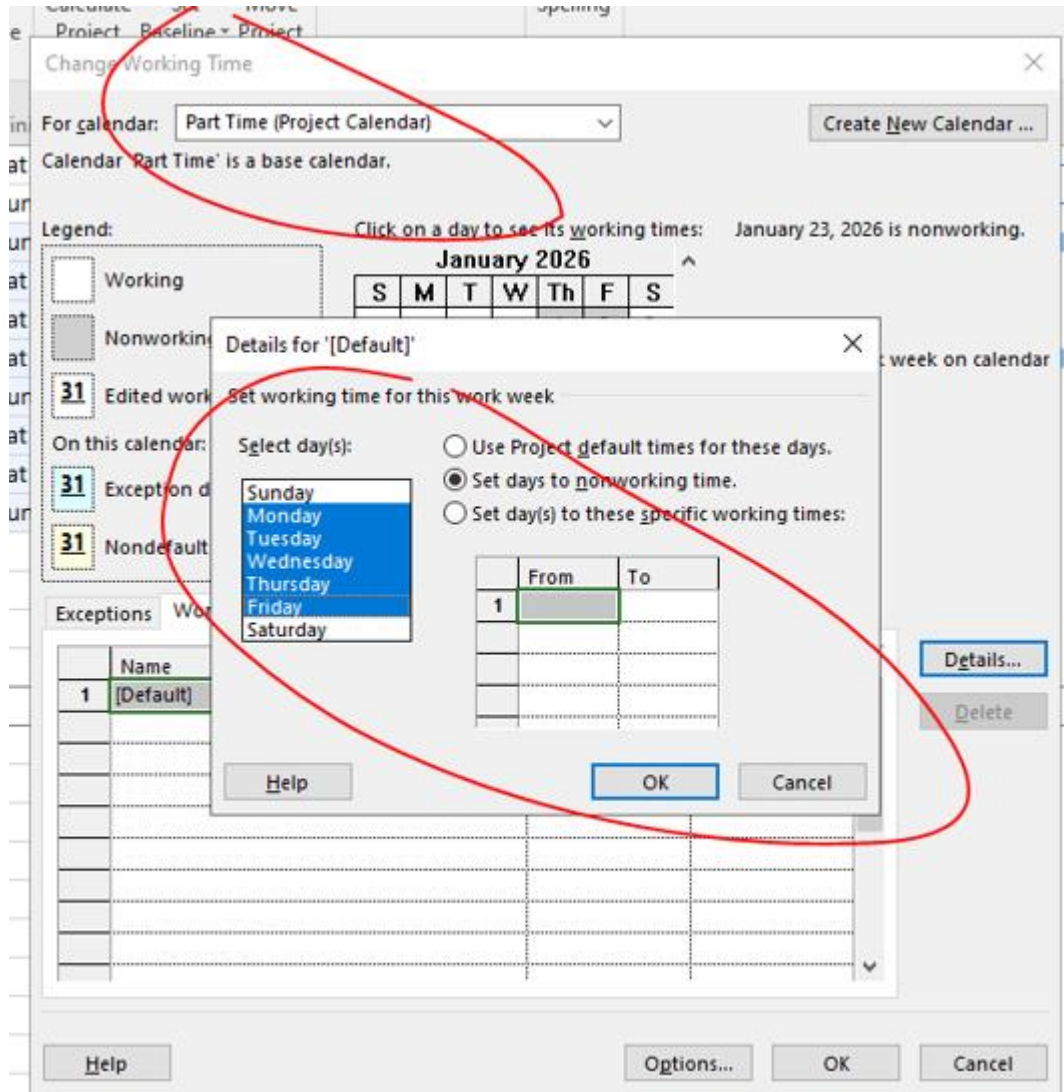

Lab report – Project Management

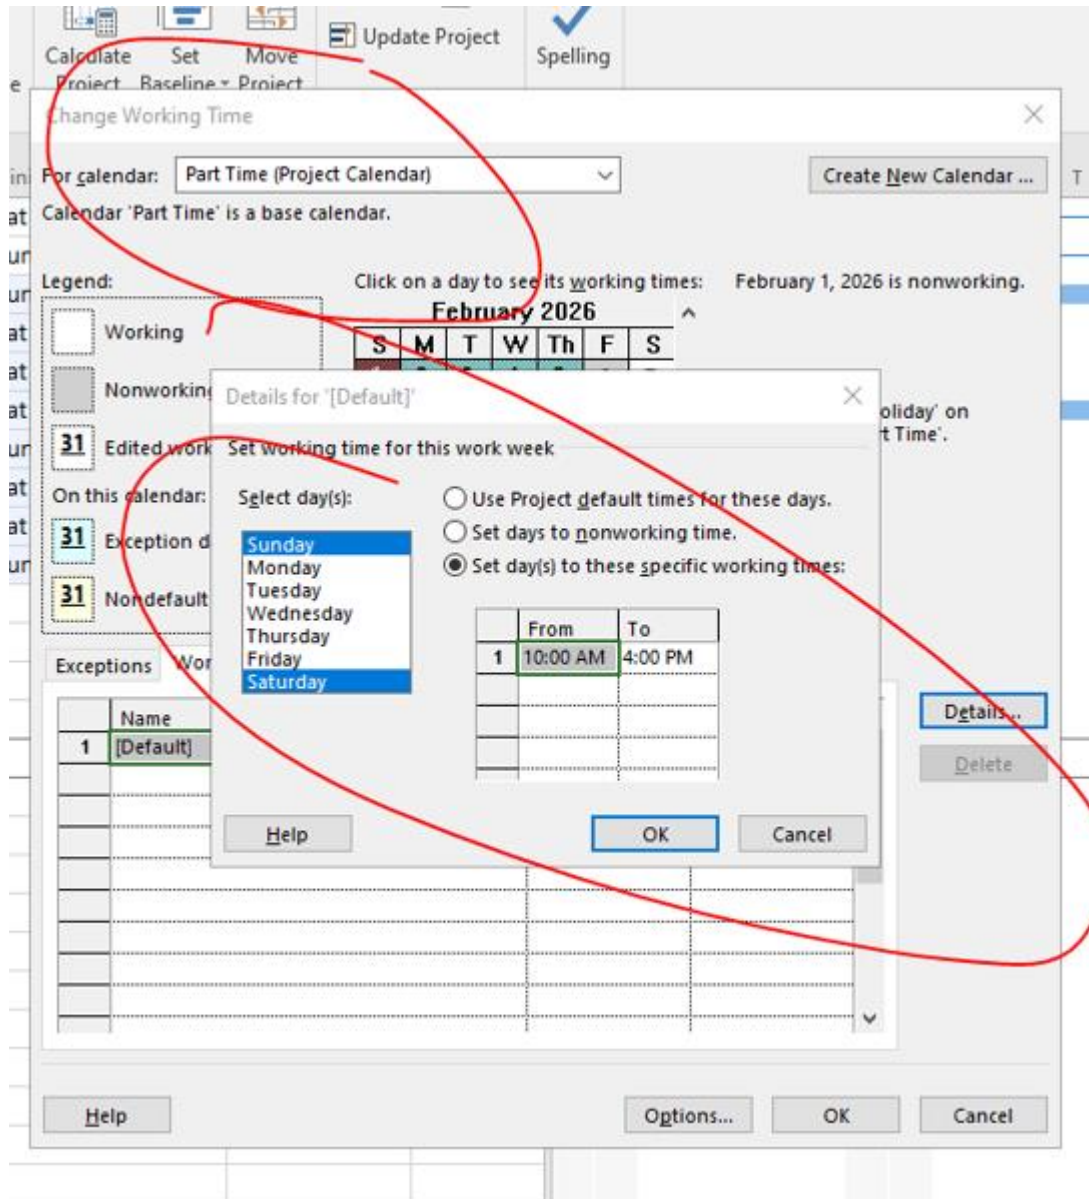

The Part time has also booked a holiday from 1st to Feb 5th . Create an Exception to their calendar with a Holiday name and these days as nonworking

Lab report – Project Management

Change Working Time

For calendar: **Part Time (Project Calendar)** Create New Calendar ...

Calendar 'Part Time' is a base calendar.

Legend:

- ☐ Working
- ☐ Nonworking
- 31** Edited working hours

On this calendar:

- 31** Exception day
- 31** Nondefault work week

Click on a day to see its working times: February 1, 2026 is nonworking.

February 2026

S	M	T	W	Th	F	S
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28

Based on:
Exception 'Holiday' on calendar 'Part Time'.

Exceptions **Work Weeks**

	Name	Start	Finish
1	Holiday	2/1/2026	2/5/2026

Details...
Delete

Help Options... OK Cancel

Display the Project Information.

Project Statistics for 'module02_ex01.mpp'

	Start	Finish
Current	Sat 1/17/26	Sun 4/19/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	20d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	20d	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close

Exercise 2: Changing Working Time

Changing Working Time

Open project file Ex4 (Module 1) Use the Project Information dialog box to:

Start Date: Nov 20th 2025

Project Information for 'module02_ex02'

Start date: Thu 11/20/25 Current date: Fri 1/23/26

Finish date: Mon 1/5/26 Status date: NA

Schedule from: Project Start Date Calendar: Standard

All tasks begin as soon as possible. Priority: 500

Enterprise Custom Fields


Department:

Custom Field Name	Value
-------------------	-------

Help Statistics... OK Cancel

Go to the Change Working Time dialog box and create an Exception called "Tet Holidays" during from Dec 24th 2026 to Jan 5th 2026 into nonworking time.


Lab report – Project Management

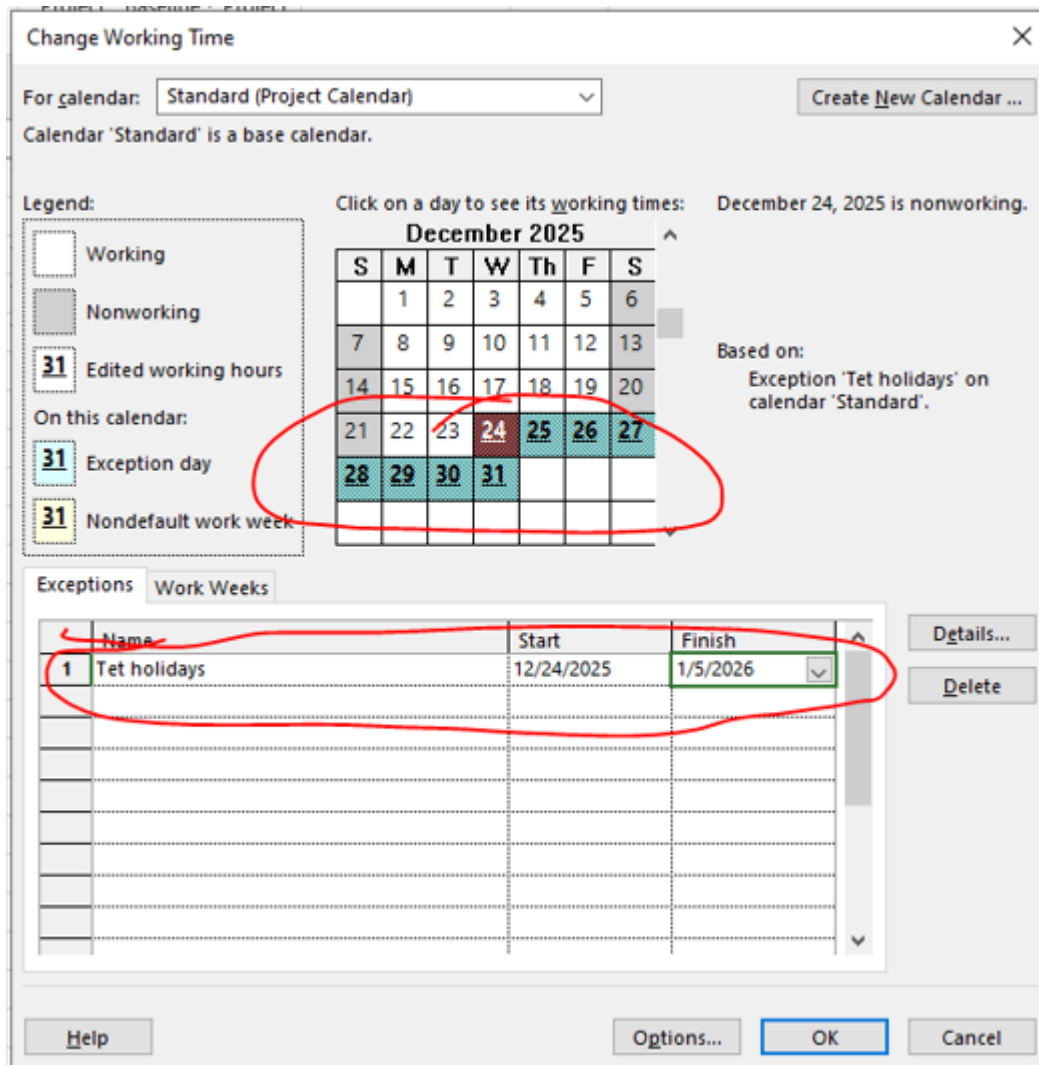


Change Work Weeks time of Standard calendar's default working week. This project's standard working time are:

- 08:30 to 17:30 Monday to Thursday (no lunch break)
- 08:30 to 16:00 on Fridays (no lunch break)
- Add a new Work Week to the Standard calendar named "Xmas Slowdown". Use this to model a 12:30 finish on every weekday from Dec 10th 2025 to Dec 23rd 2025.
- Capture the Work weeks time

Lab report – Project Management

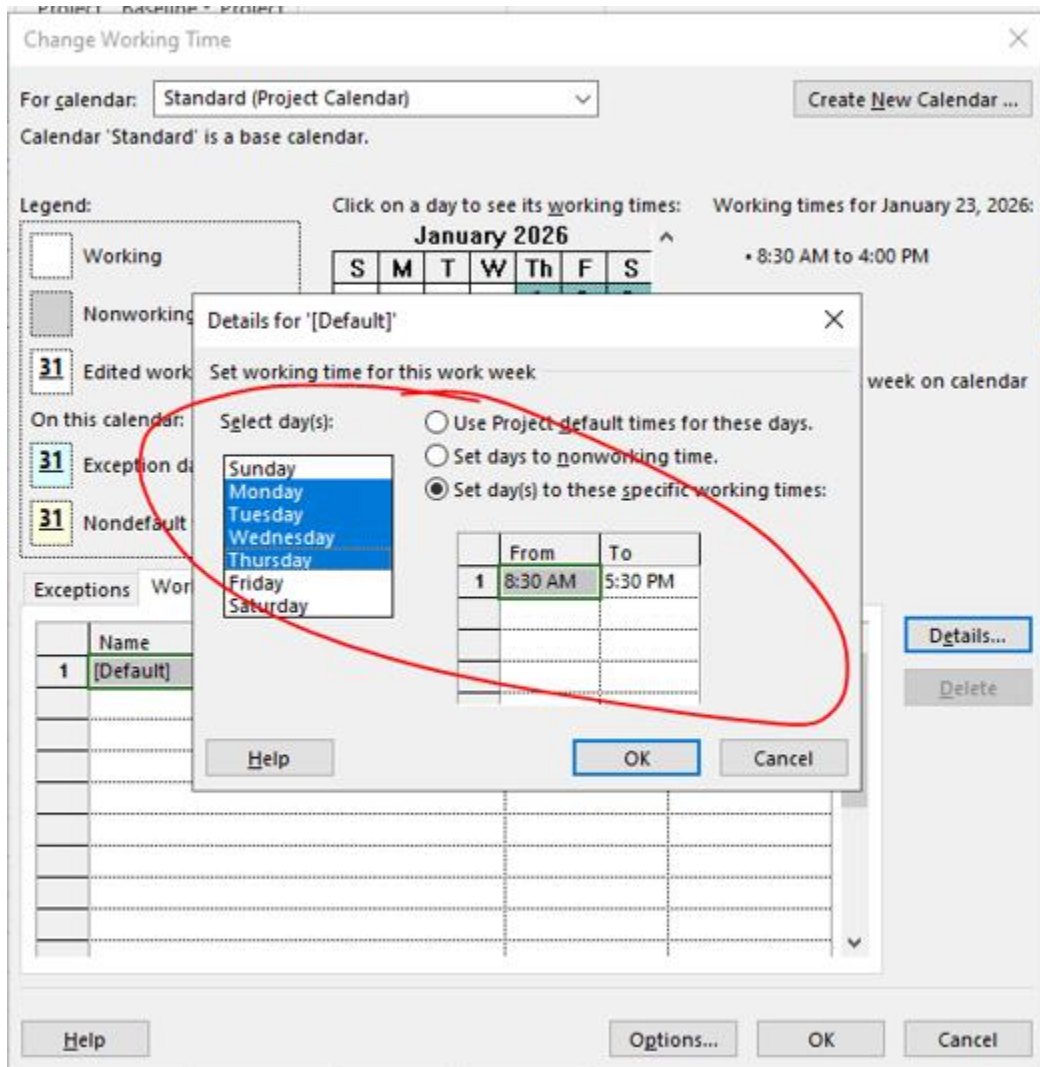

Lab report – Project Management

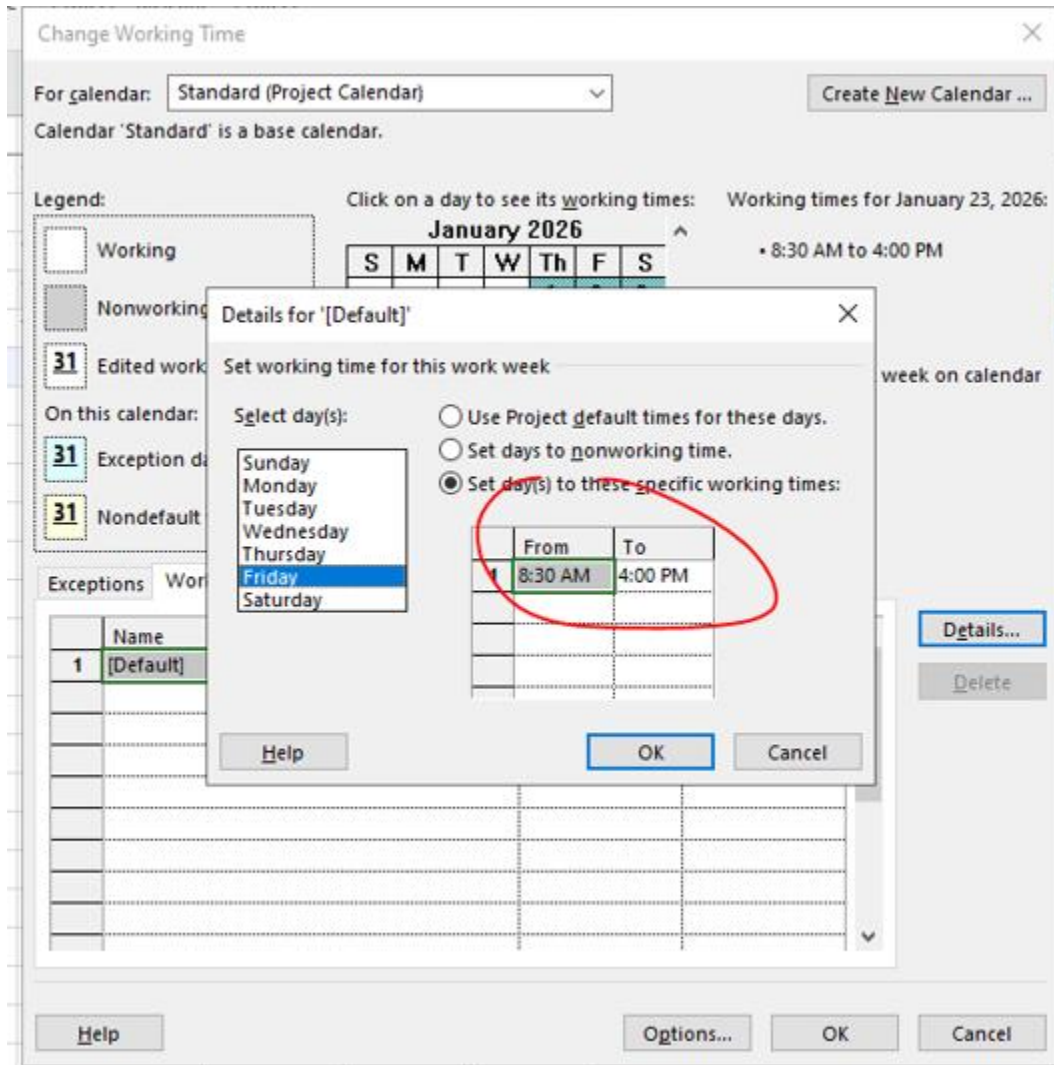

Lab report – Project Management

Change Working Time

For calendar: Standard (Project Calendar) Create New Calendar ...

Calendar 'Standard' is a base calendar.

Legend:

- Working
- Nonworking
- 31 Edited working hours
- 31 Exception day
- 31 Nondefault work week

On this calendar:

Exceptions Work Weeks

Click on a day to

Details for 'Xmas slowdown'

Set working time for this work week

Select day(s):

- Sunday
- Monday
- Tuesday
- Wednesday
- Thursday
- Friday
- Saturday

From To

1 8:30 AM 12:00 PM

OK Cancel

Help Options... OK Cancel

Project Statistics for 'module02_ex02.mpp'

	Start	Finish
Current	Thu 11/20/25	Thu 1/22/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d


	Duration	Work	Cost
Current	33d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	33d	0h	\$0.00

Percent complete:

Duration: 0% Work: 0%

Close

Lab report – Project Management



Exercise 3: Changing Working Time

Open project file **Ex5 (Module 1)**, Use the Project Information dialog box to:

Star Date: Apr 5th 2026

Project Statistics for 'module02_ex03.mpp'

	Start	Finish
Current	Sun 4/5/26	Thu 1/7/27
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d


	Duration	Work	Cost
Current	199d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	199d	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close


The office will shut down for 2 weeks in the summer. Use the Change Working Time dialog box to create an Exception called "Summer Shutdown" and make the first 14 workdays of August nonworking time

Lab report – Project Management

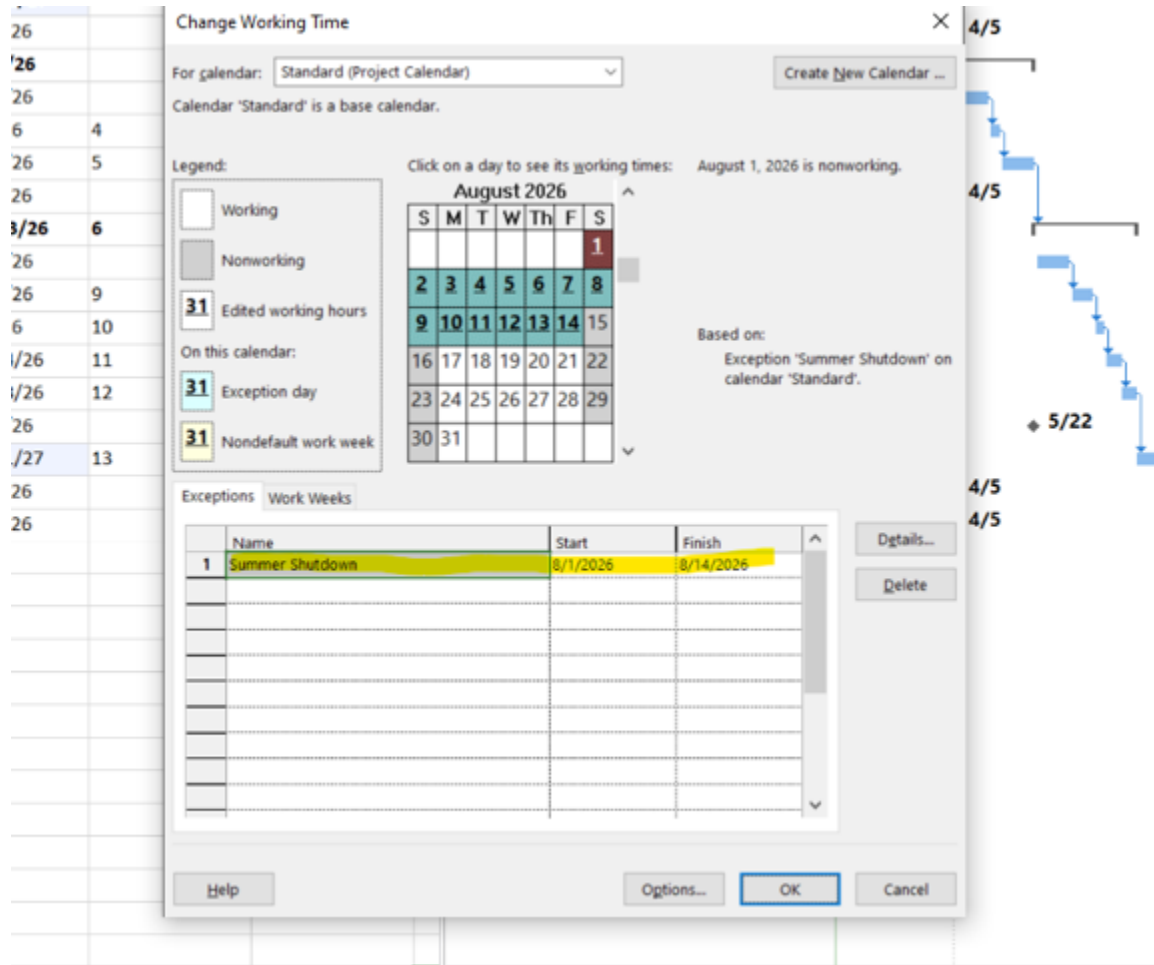


Create an Exception called “Independence Days” is 2 Sep nonworking time.

Lab report – Project Management

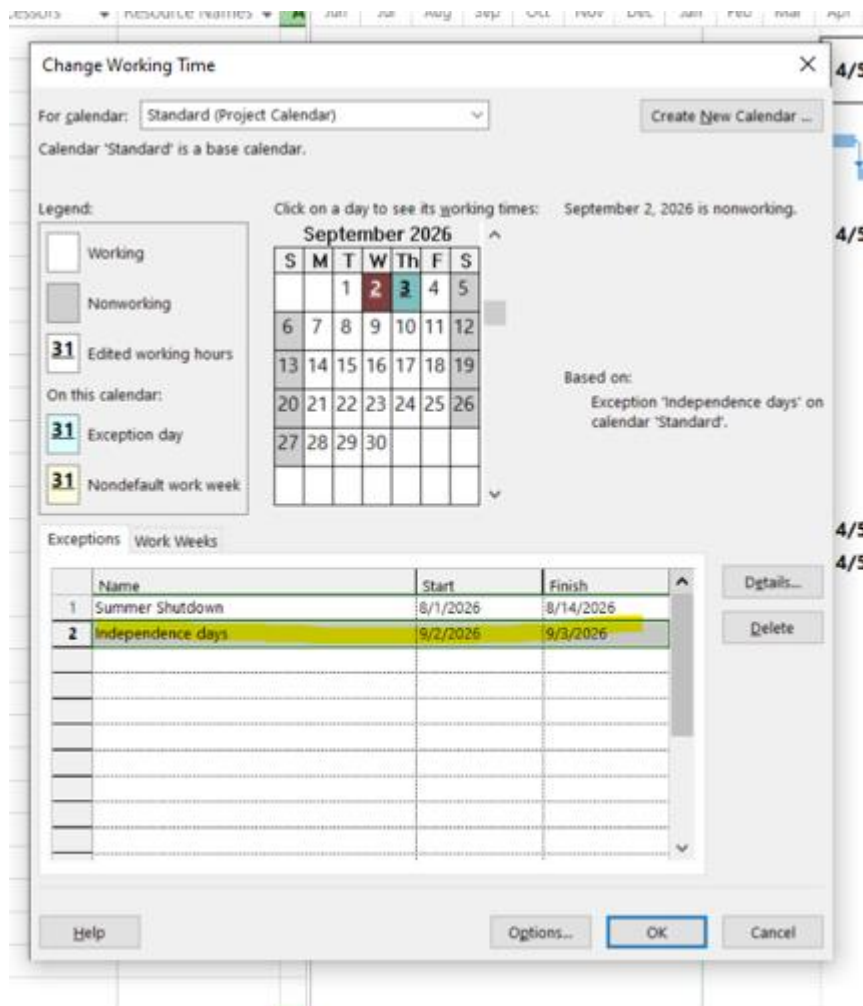


Create an Exception called “International Labor days” is Apr 30th and May 1st nonworking time

Lab report – Project Management

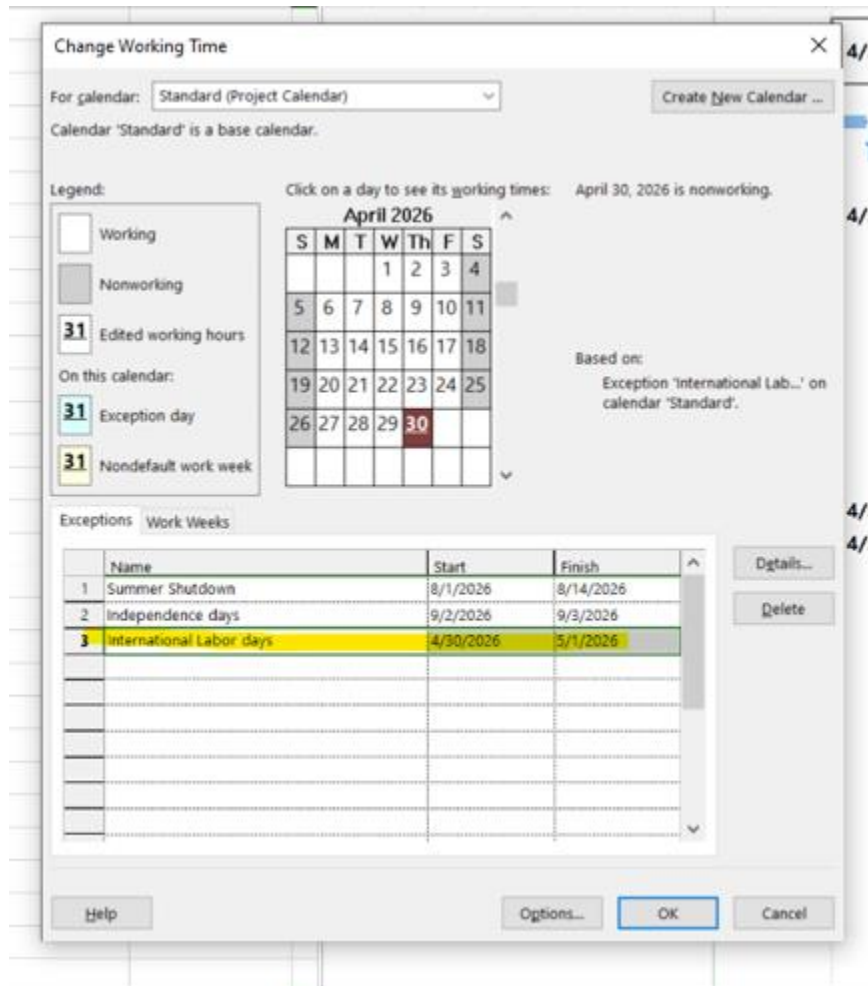


Display the Project Information

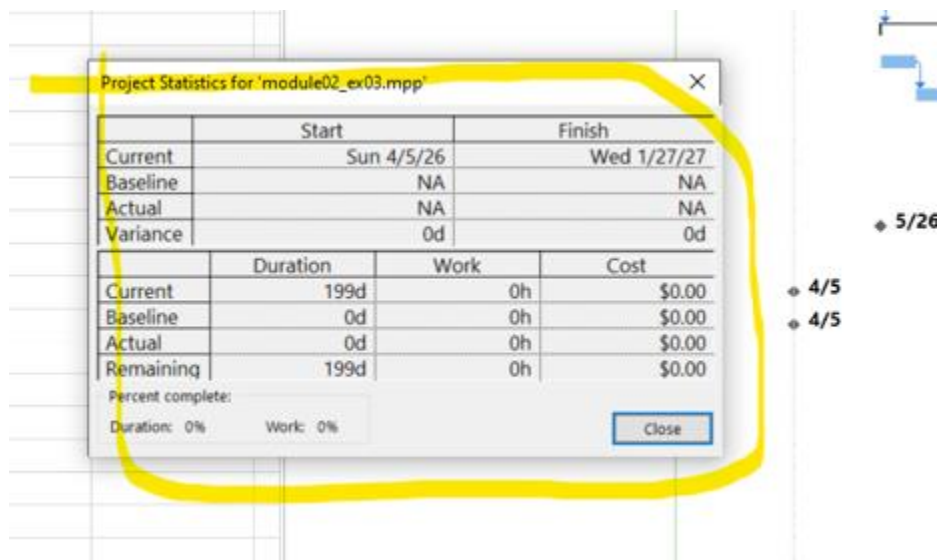

Lab report – Project Management


Exercise 4: Changing Working Time

Open project file Ex6 (Module 1), Use the Project Information dialog box to:

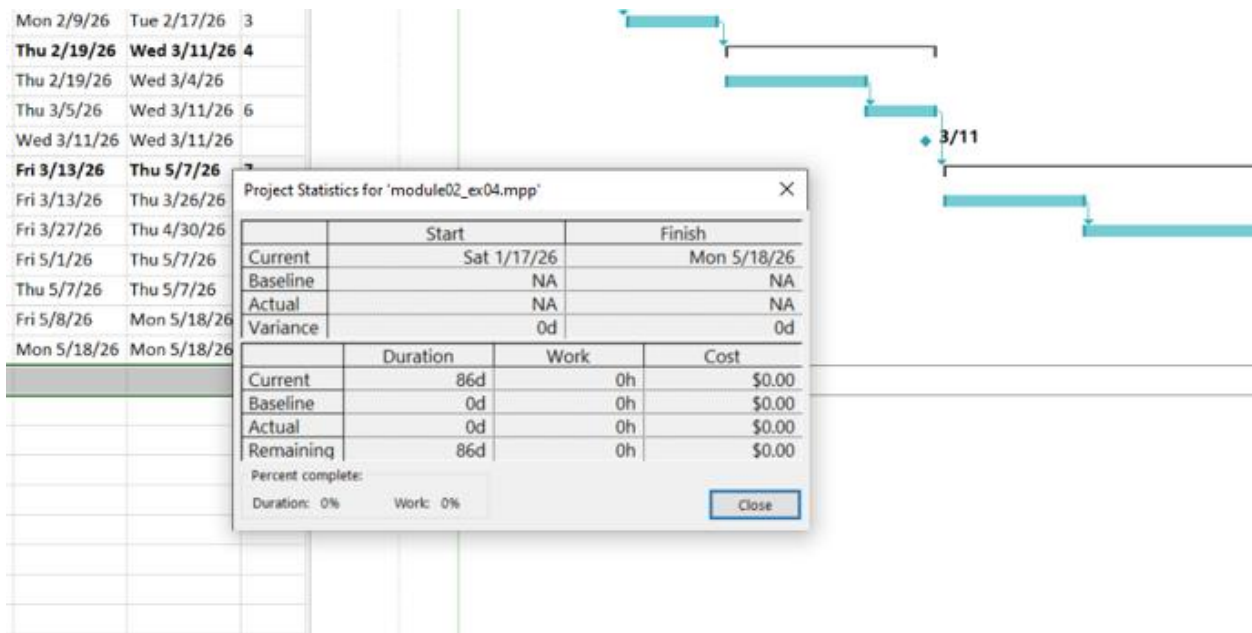


Modify the Standard calendar and change the [Default] work week to use the hours shown below:

Lab report – Project Management

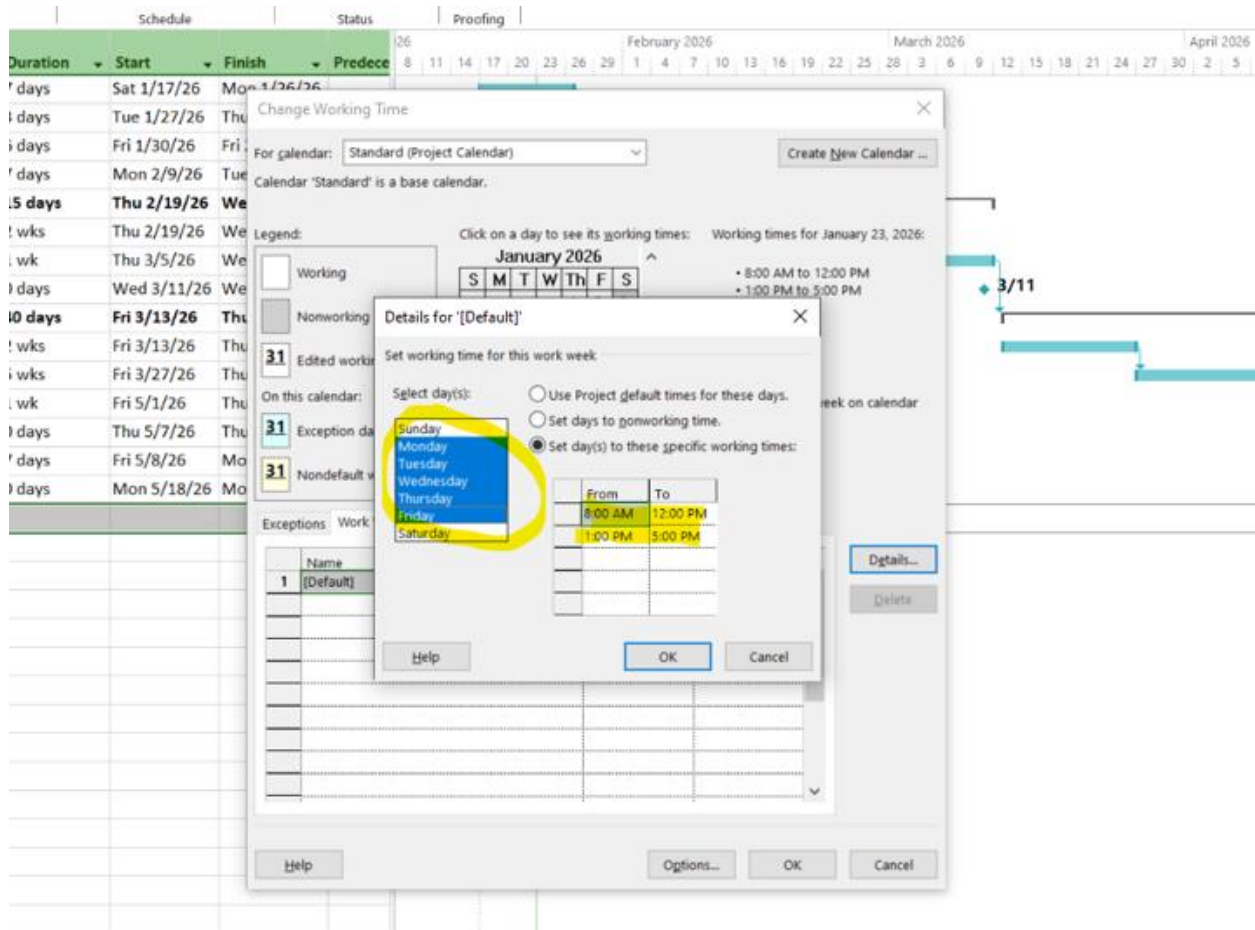


Add an exception in the Standard calendar called Recovery with in 7 lates workdays of March is non-working days.

Lab report – Project Management

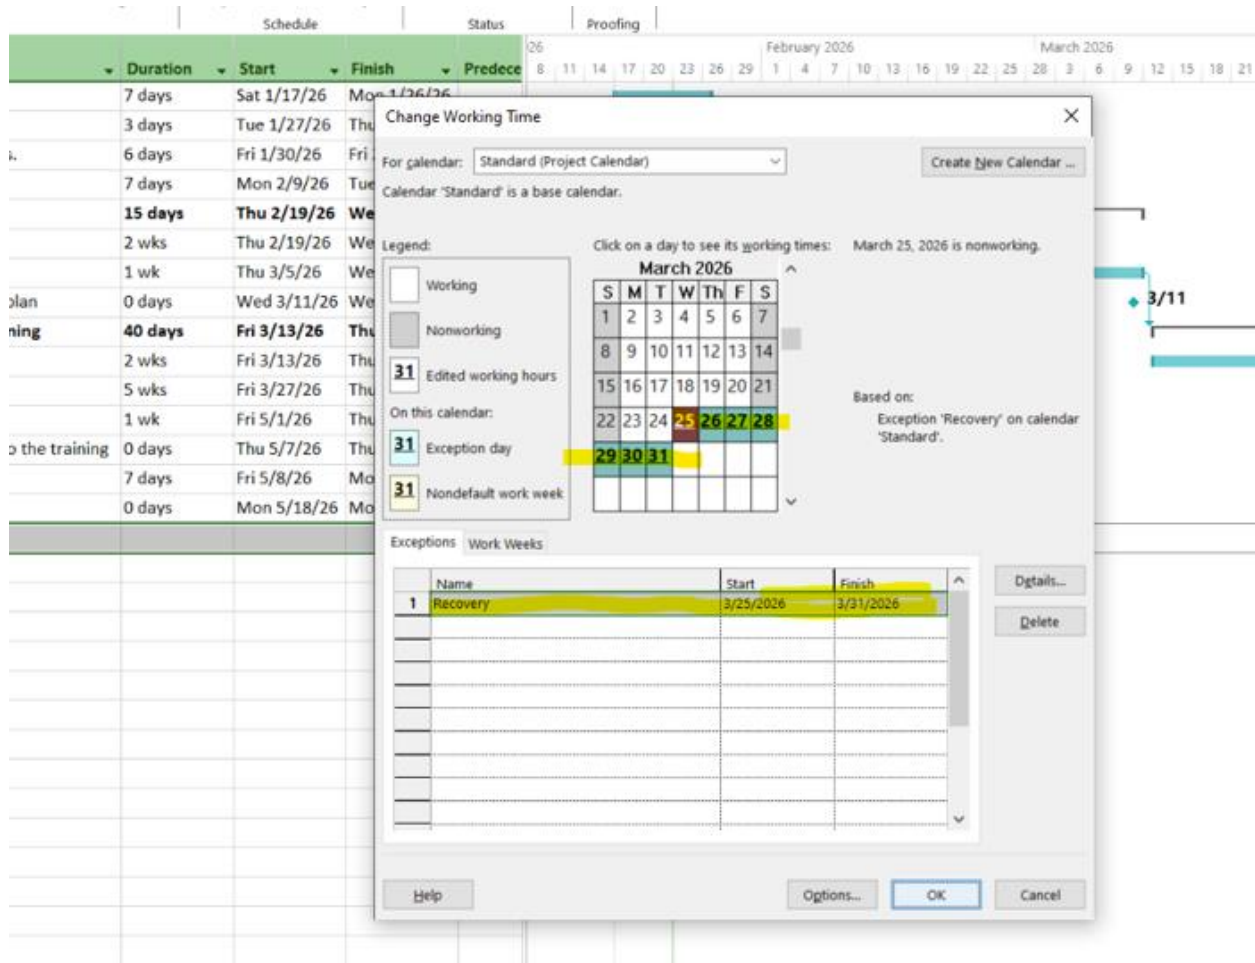

Display the Project Information.

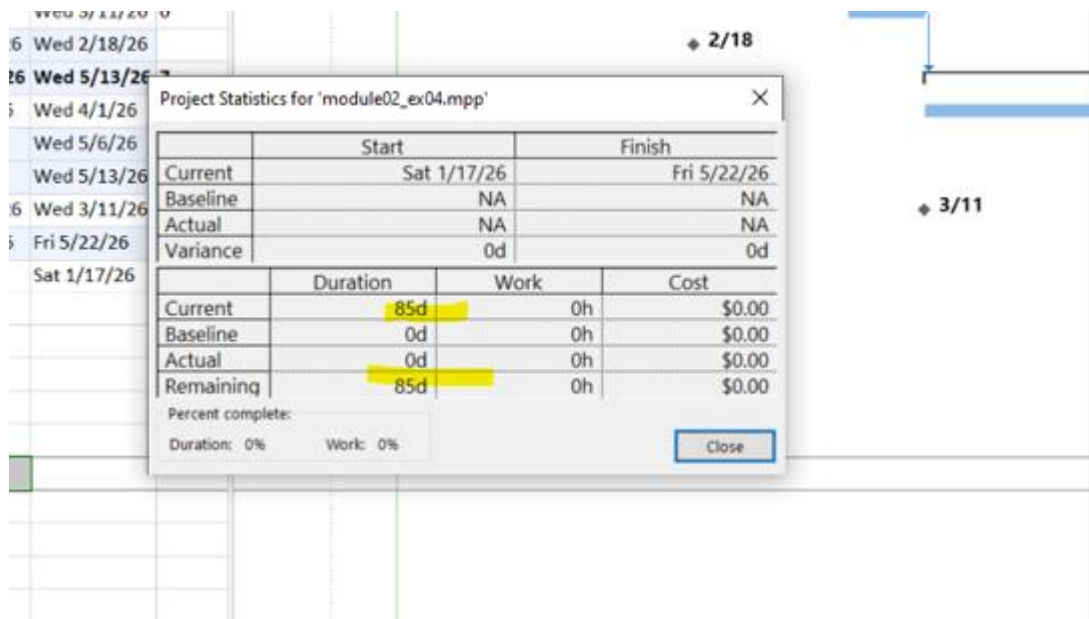


Lab report – Project Management

Exercise 5: Create the private Time for a project

Open project file Ex7 (Module 1), Use the Project Information dialog box to:

Create the new Time Work for your project.


[NameTimeProject] {Name: Your Name - Ex: MinhTimeProject}

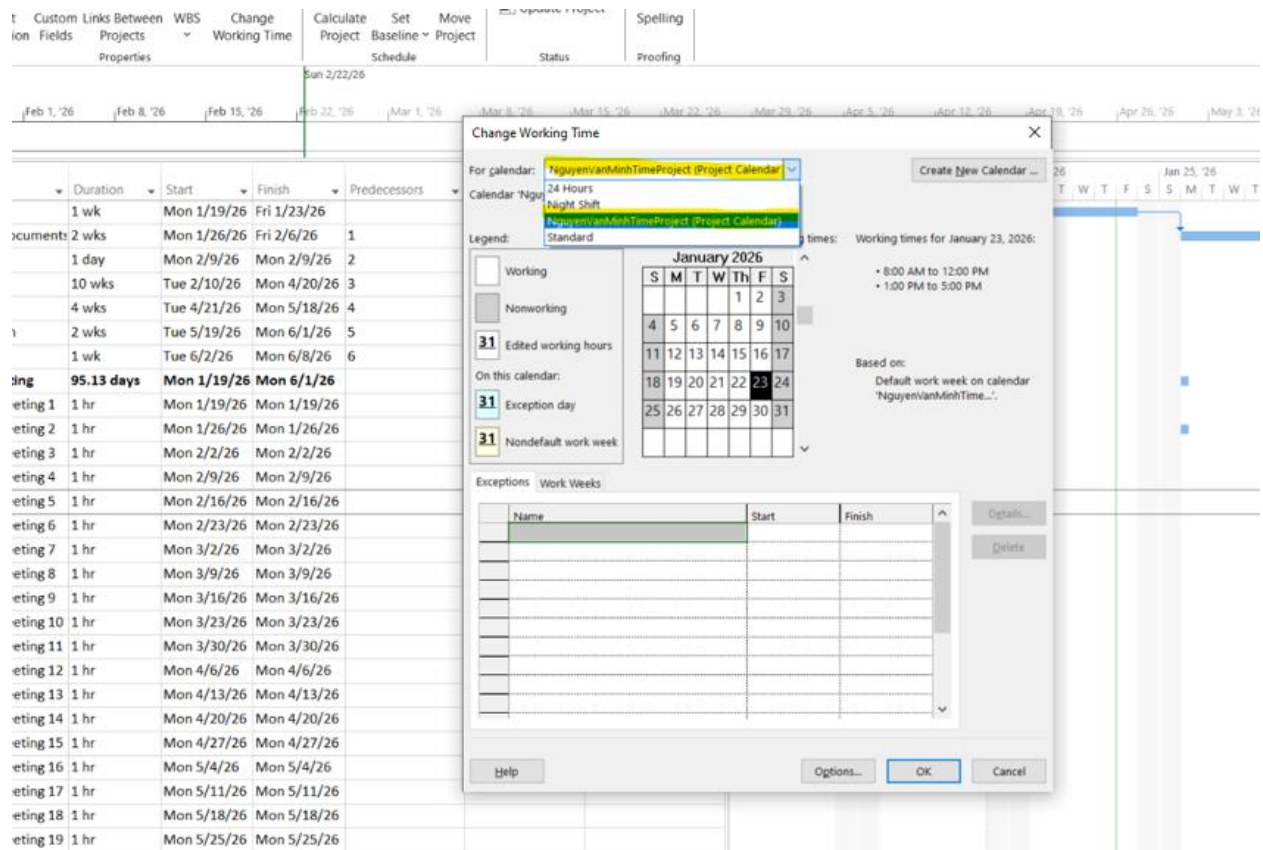

Change Work Weeks time of Standard calendar's default working week. This project's standard working time are:


08:00 to 12:00 on Mon, Wed, Fri

Lab report – Project Management

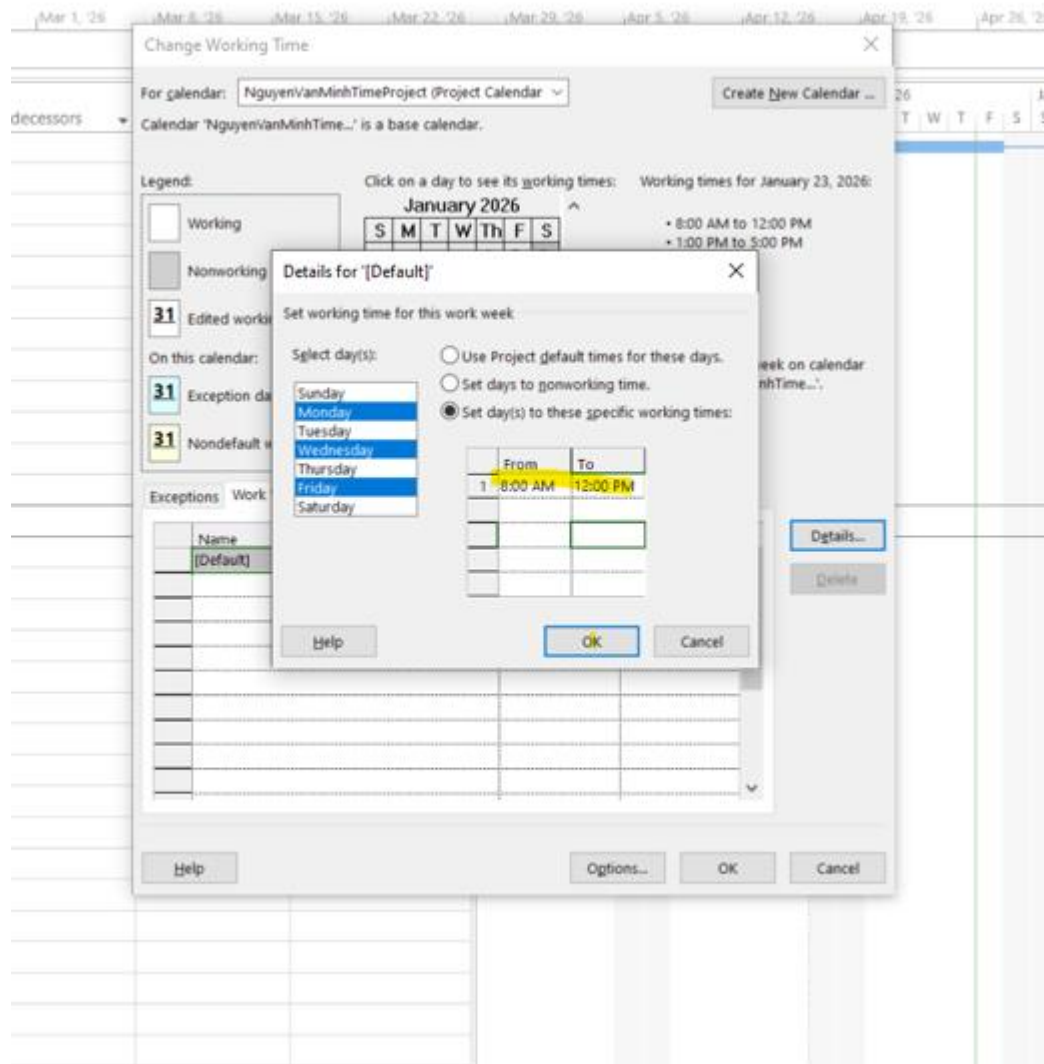


13:00 to 16:00 on Tue, Thu, Sat

Lab report – Project Management

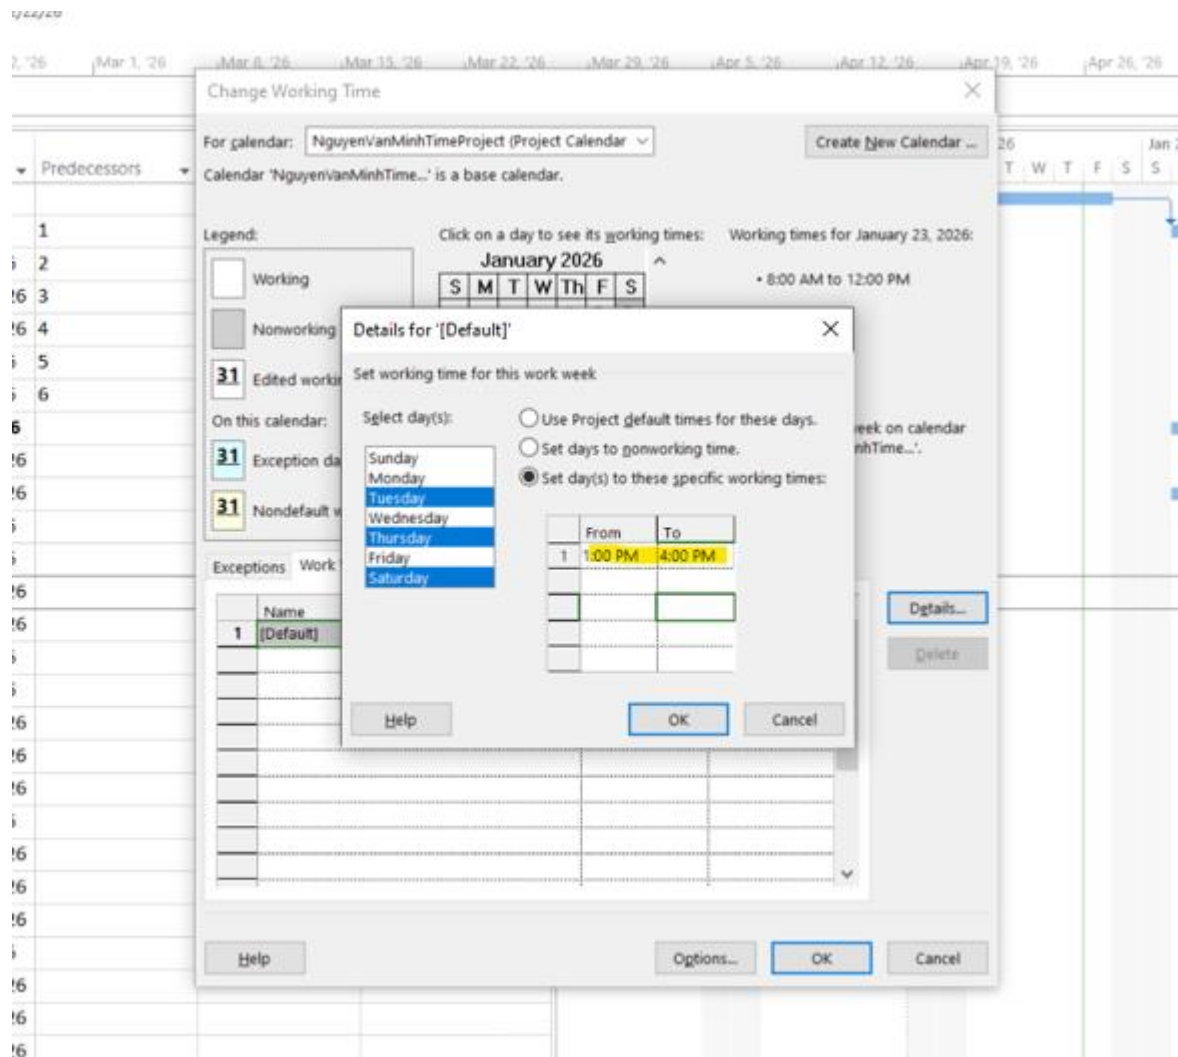

Create an Exception called “International Labor days” is Apr 30th and May 1st nonworking time

Lab report – Project Management

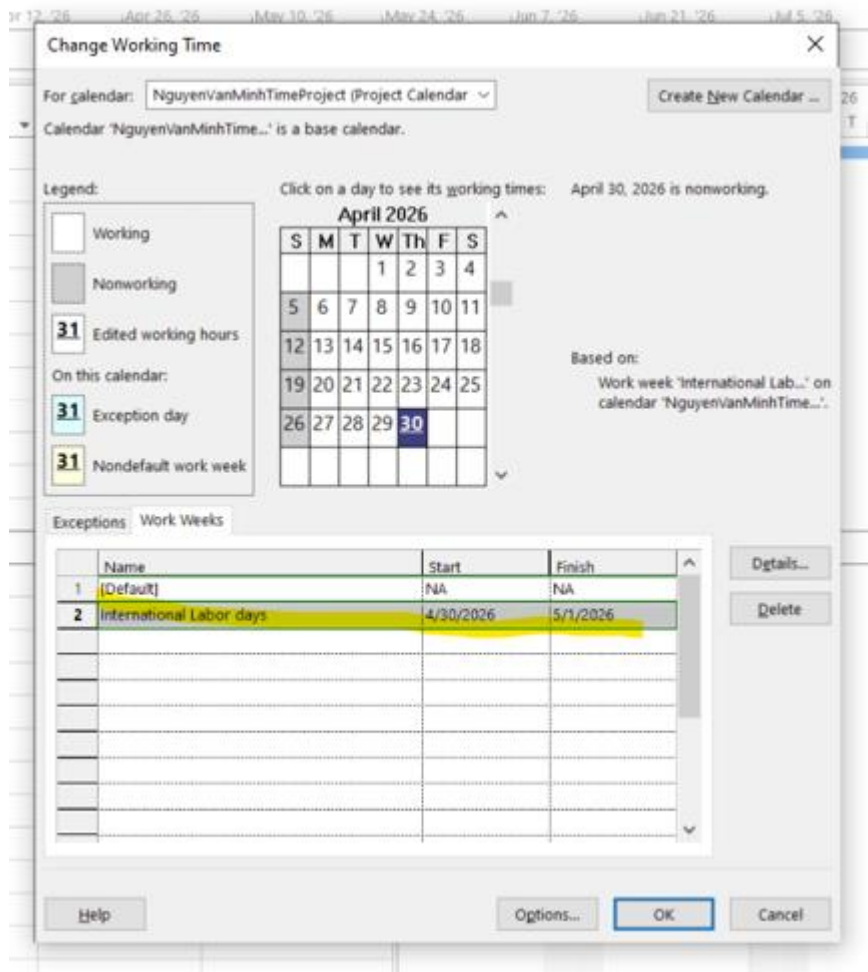

Capture the Work weeks time



Lab report – Project Management

Project Statistics for 'module02_ex05.mpp'

	Start	Finish
Current	Sat 1/17/26	Tue 10/13/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	101d	0h	\$0.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	101d	0h	\$0.00

Percent complete:
Duration: 0% Work: 0%

Close

Exercise 6: My project

Create your plan from Monday to Sunday. It will list all of your activities, your time you spend and resources joining in each task.

Create a new calendar called Student based on the Standard calendar.

Change the [Default] work week so that the hours match to your calendar everyday



Using Note function in MP 2010 to take note for important tasks in your plan.

The screenshot displays the Microsoft Project 2010 interface. On the left, a Gantt chart shows a project plan starting on Jan 25, '26. The task list on the right includes:

- Task Name: Kế hoạch công việc tháng phát triển dự án phần mềm job freelancer của Nguyễn Văn Minh (Duration: 24 days, Start: Fri 1/23/26)
- Task Name: Phân tích yêu cầu hệ thống (Duration: 2 days, Start: Fri 1/23/26)
- Task Name: Thiết kế kiến trúc phần mềm (Duration: 2 days, Start: Tue 1/27/26)
- Task Name: Thiết kế cơ sở dữ liệu (Duration: 2 days, Start: Thu 1/29/26)
- Task Name: Lập trình Backend (Duration: 5 days, Start: Mon 2/2/26)
- Task Name: Lập trình Frontend (Duration: 4 days, Start: Mon 2/9/26)
- Task Name: Tích hợp Frontend & Backend (Duration: 2 days, Start: Fri 2/13/26)
- Task Name: Kiểm thử chức năng (Testing) (Duration: 3 days, Start: Tue 2/17/26)
- Task Name: Sửa lỗi & tối ưu code (Duration: 2 days, Start: Fri 2/20/26)
- Task Name: Viết tài liệu kỹ thuật (Duration: 1 day, Start: Tue 2/24/26)
- Task Name: Triển khai hệ thống (Deployment) (Duration: 1 day, Start: Wed 2/25/26)

Overlaid on the right is the 'Change Working Time' dialog box. It shows the 'Student (Project Calendar)' selected. The legend indicates 'Working' (blue) and 'Nonworking' (grey). The calendar grid for January 2026 shows the current working times. The 'Based on' dropdown is set to 'Default work week on calendar "Student"'. The 'Exceptions' and 'Work Weeks' tables are empty.


Lab report – Project Management

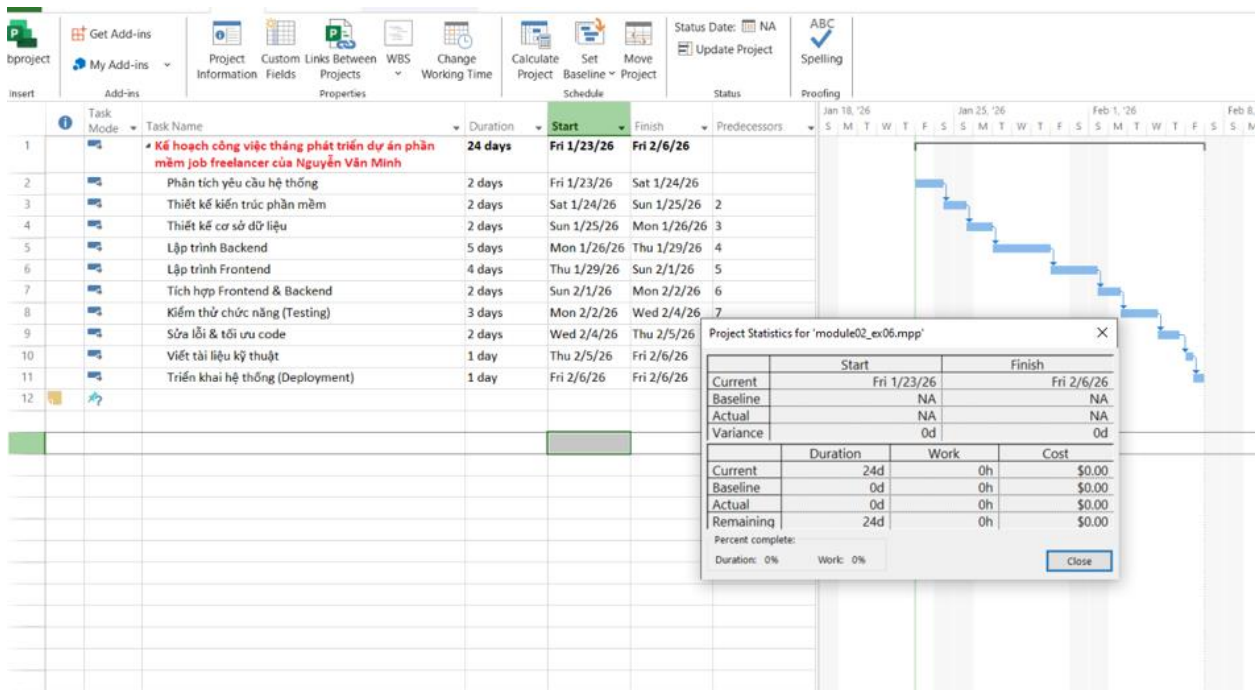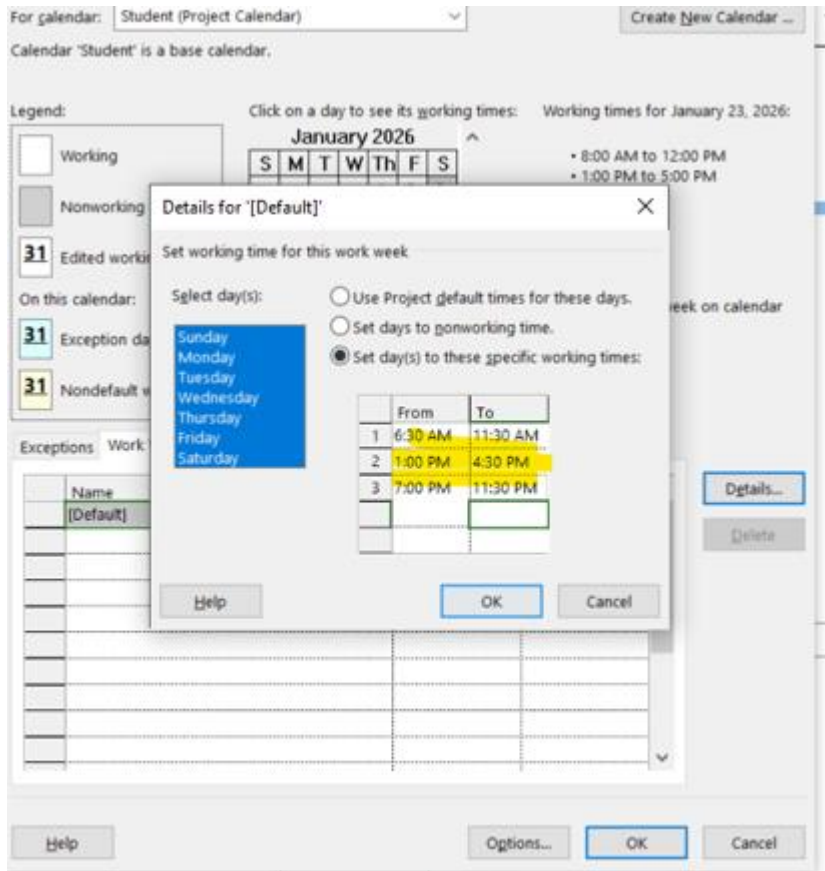


Module 3: Working with Tasks

Exercise 1: Changing Working Time (Start Date Feb 2st 2026)

Display the Project Information.

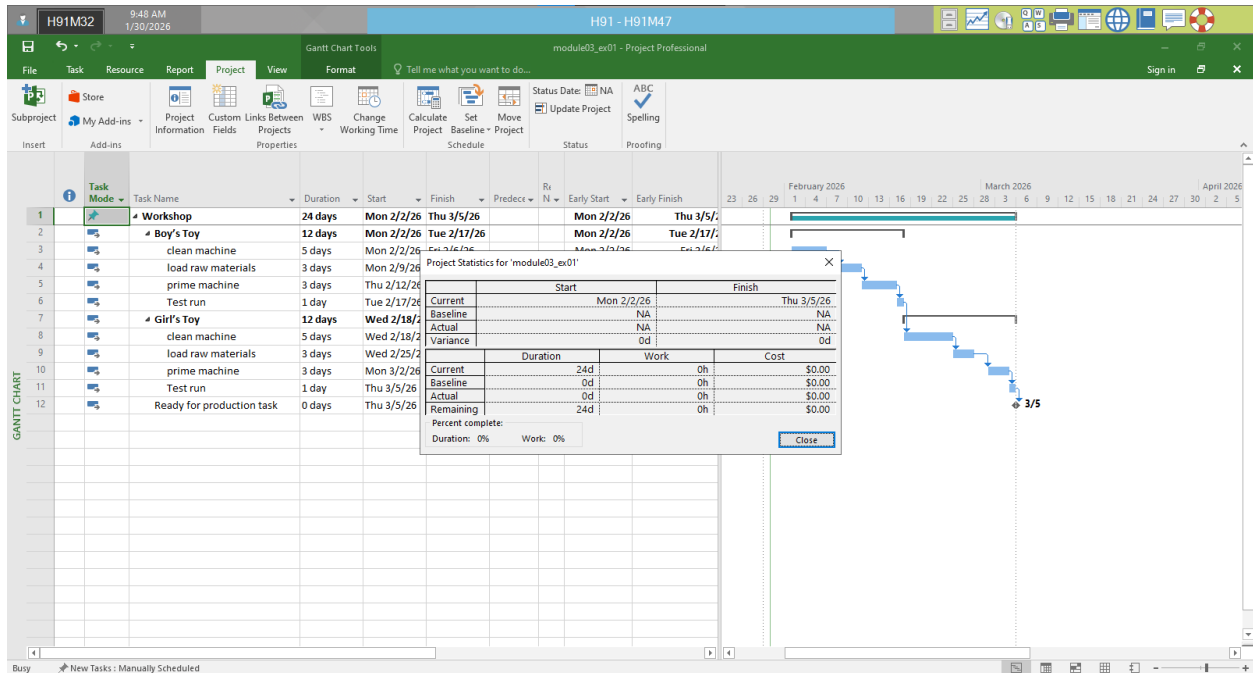


View Project Timeline

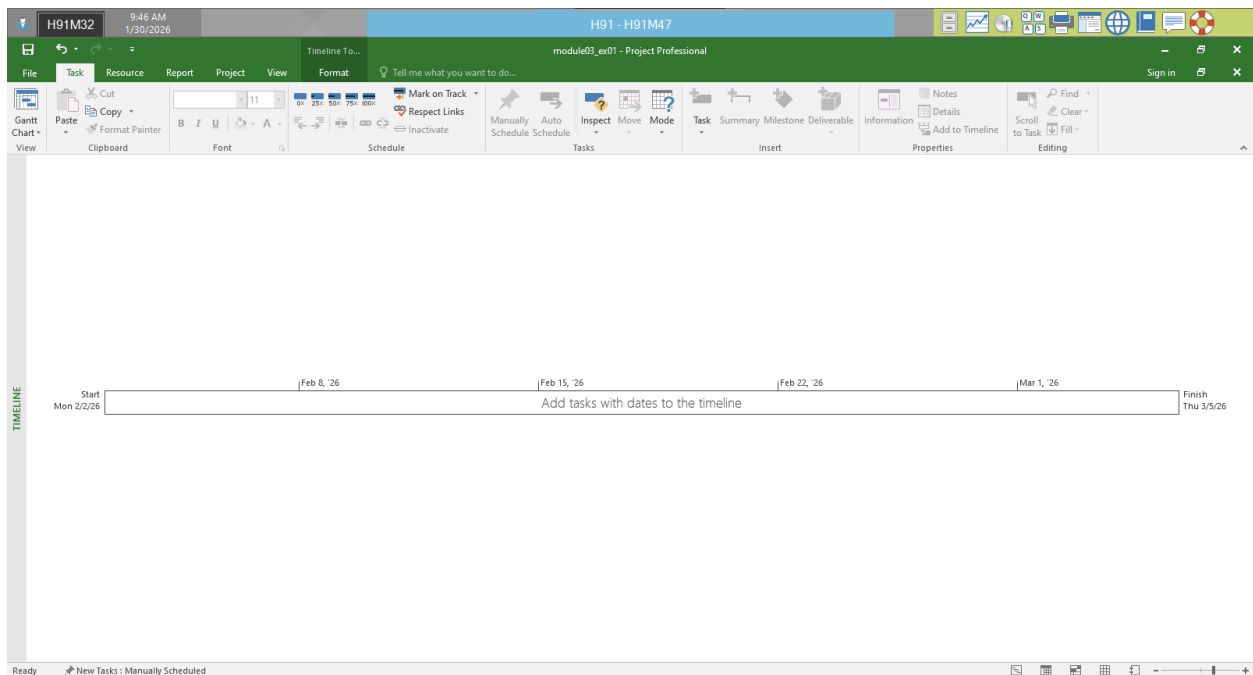


Lab report – Project Management

Gantt Chart

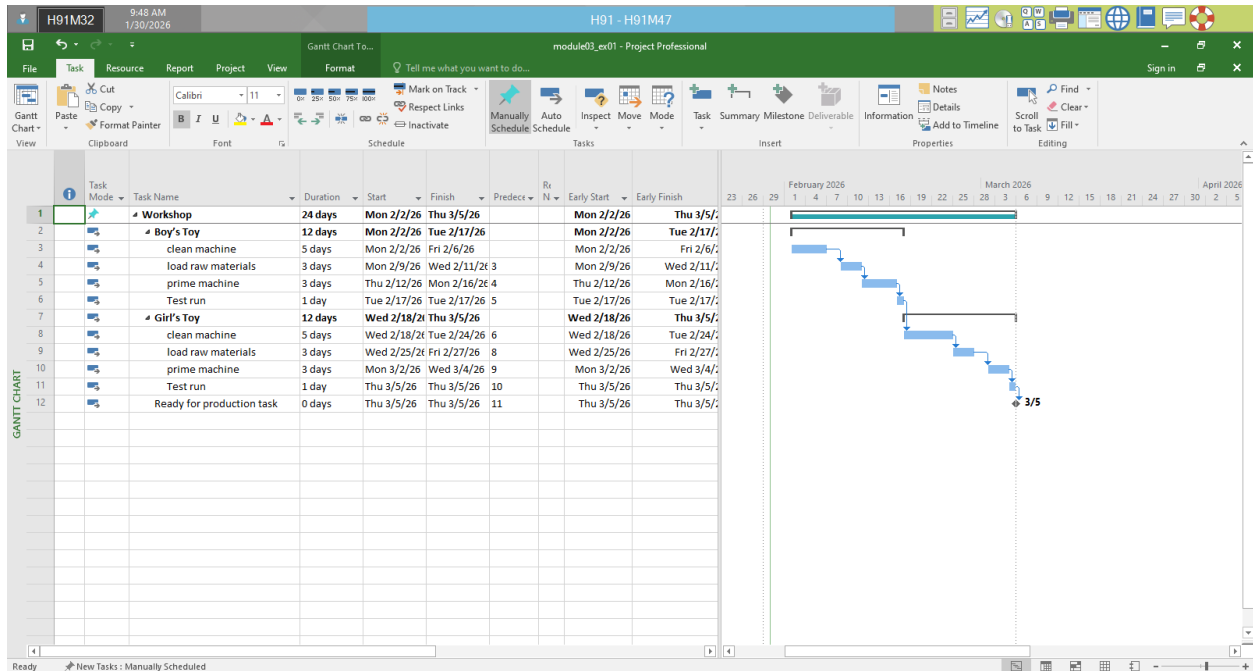


view CP

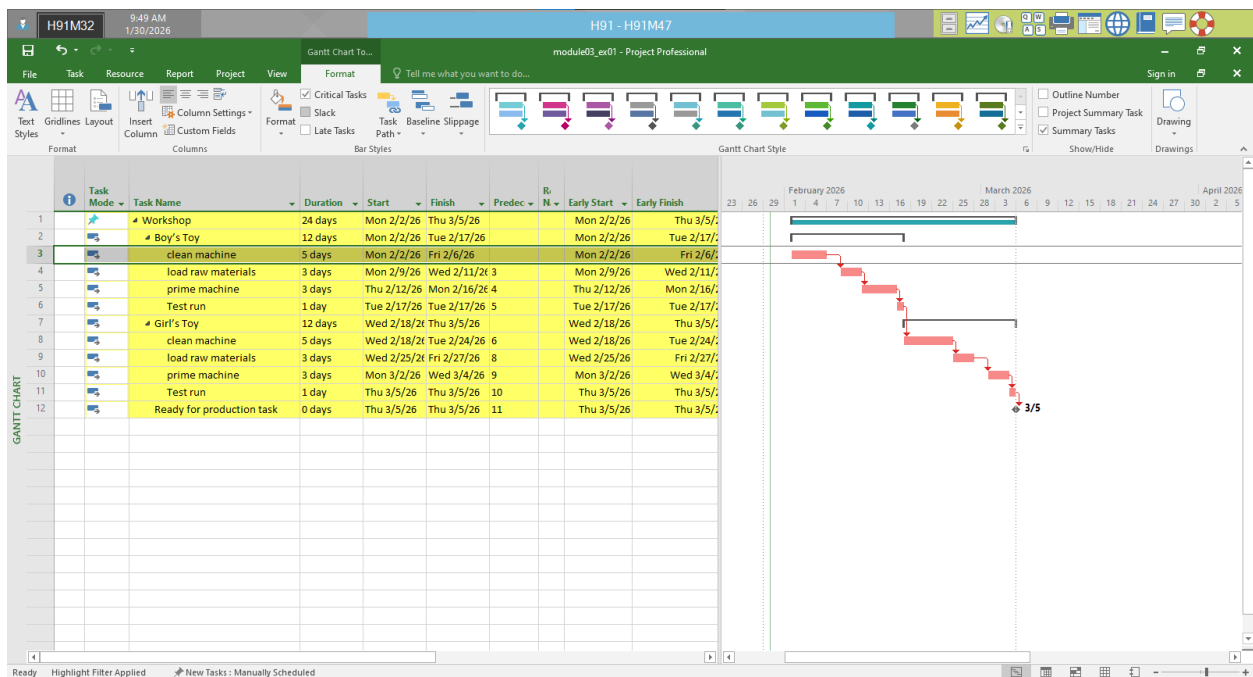


Total Slack

Lab report – Project Management

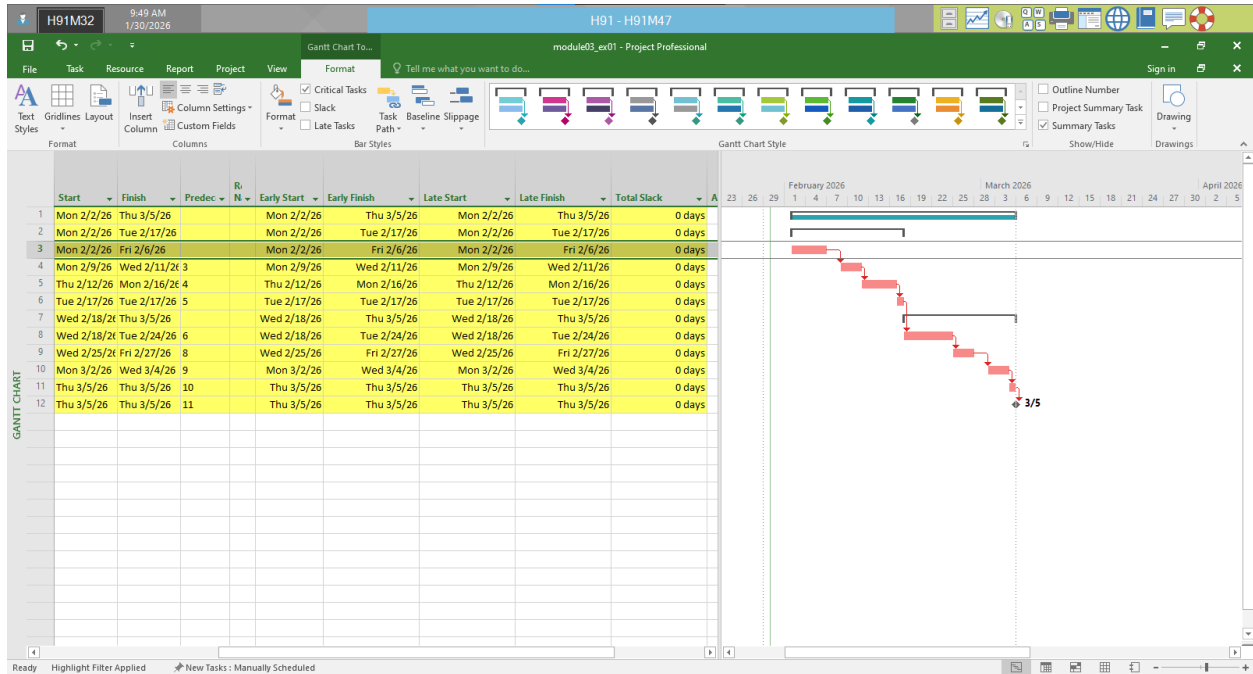


Exercise 2: Changing Working Time (Start Date Feb 2nd 2026)

Timeline

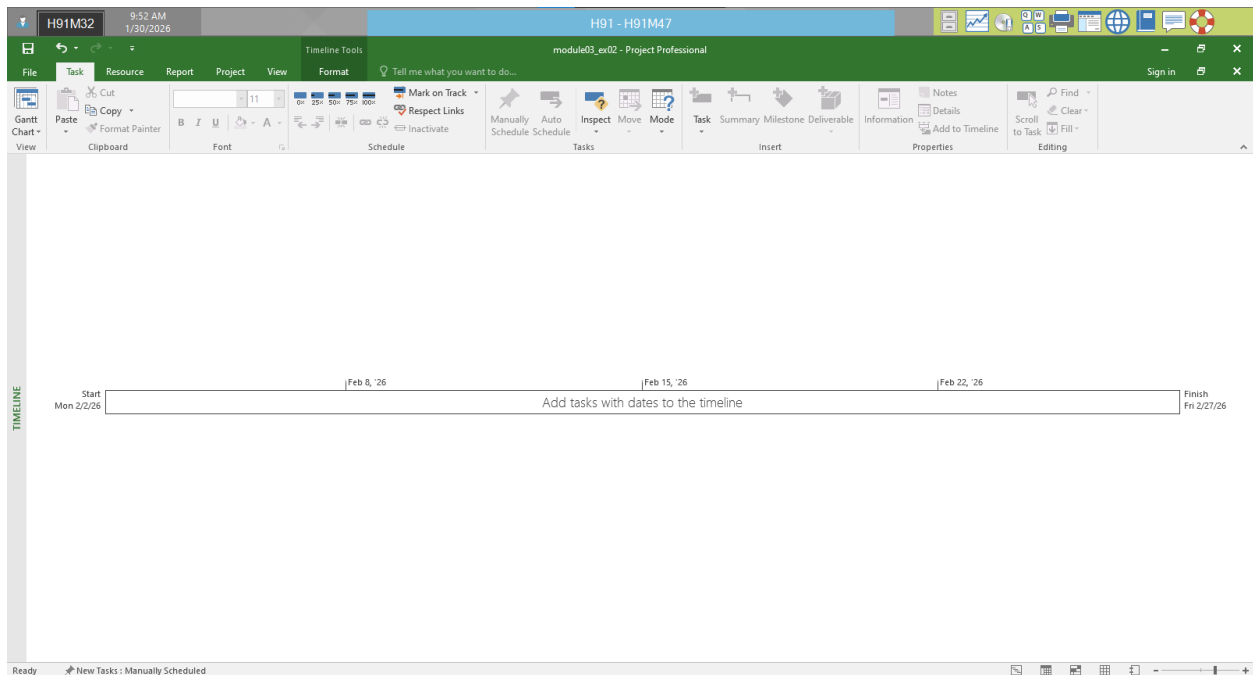


Gantt Chart

Lab report – Project Management

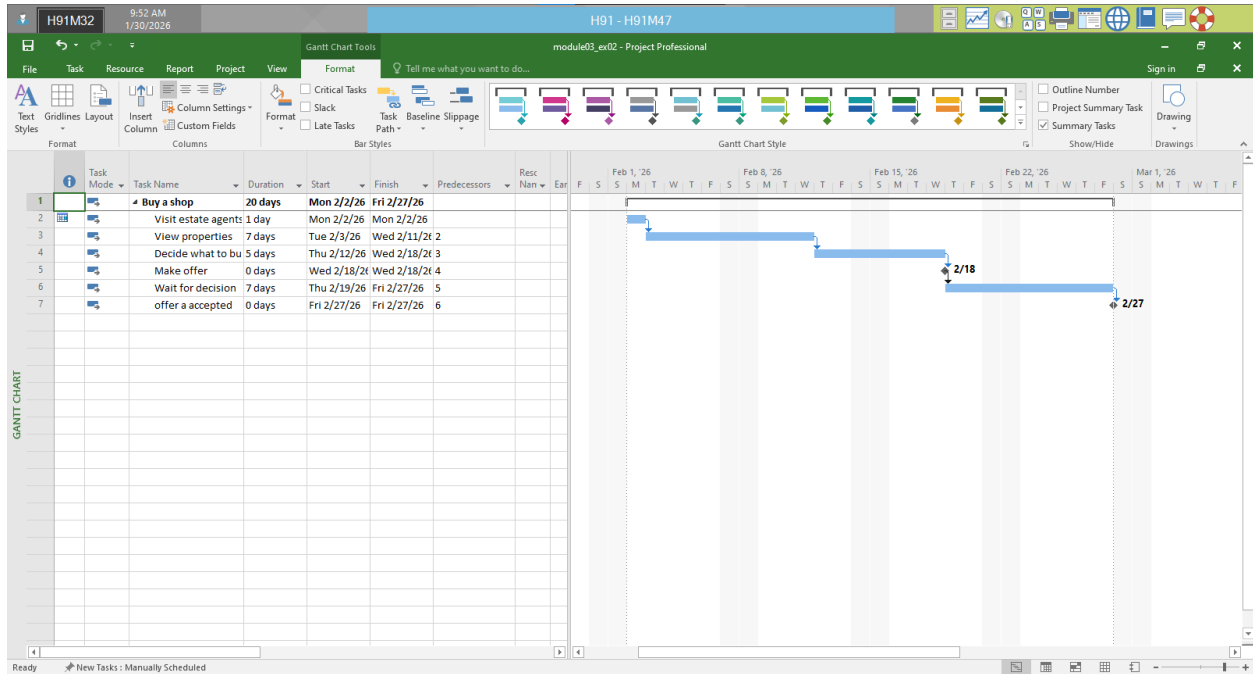


view CP

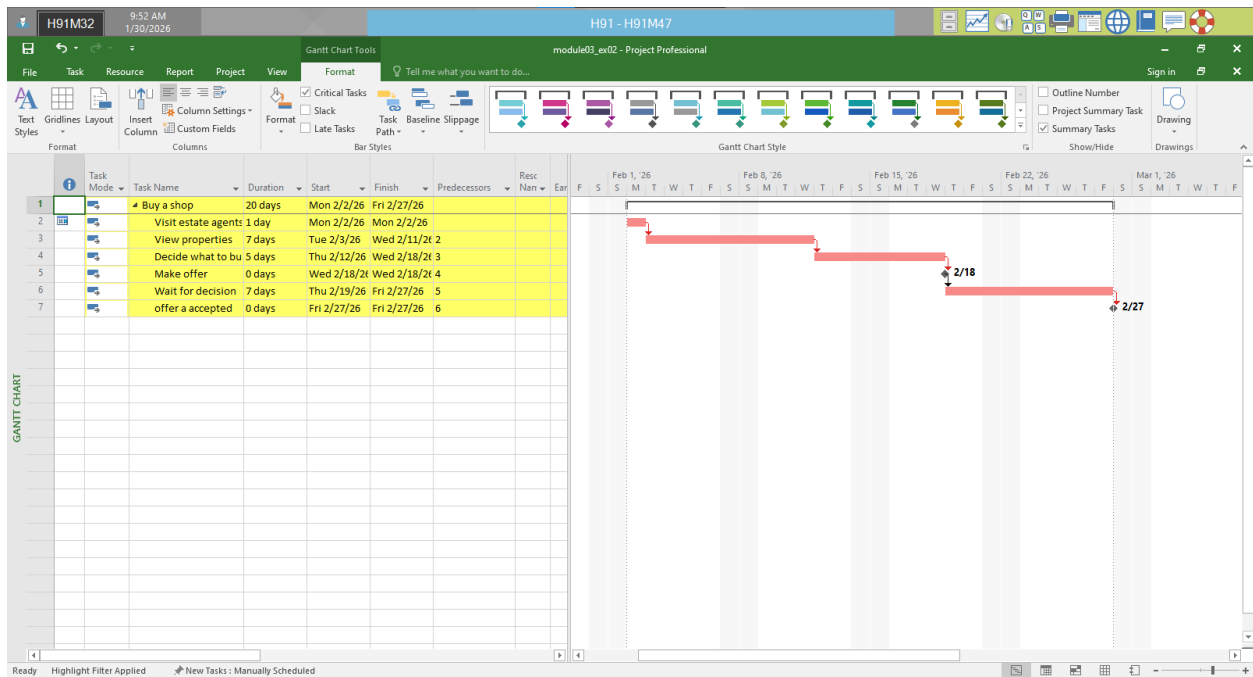


Total Slack

Lab report – Project Management

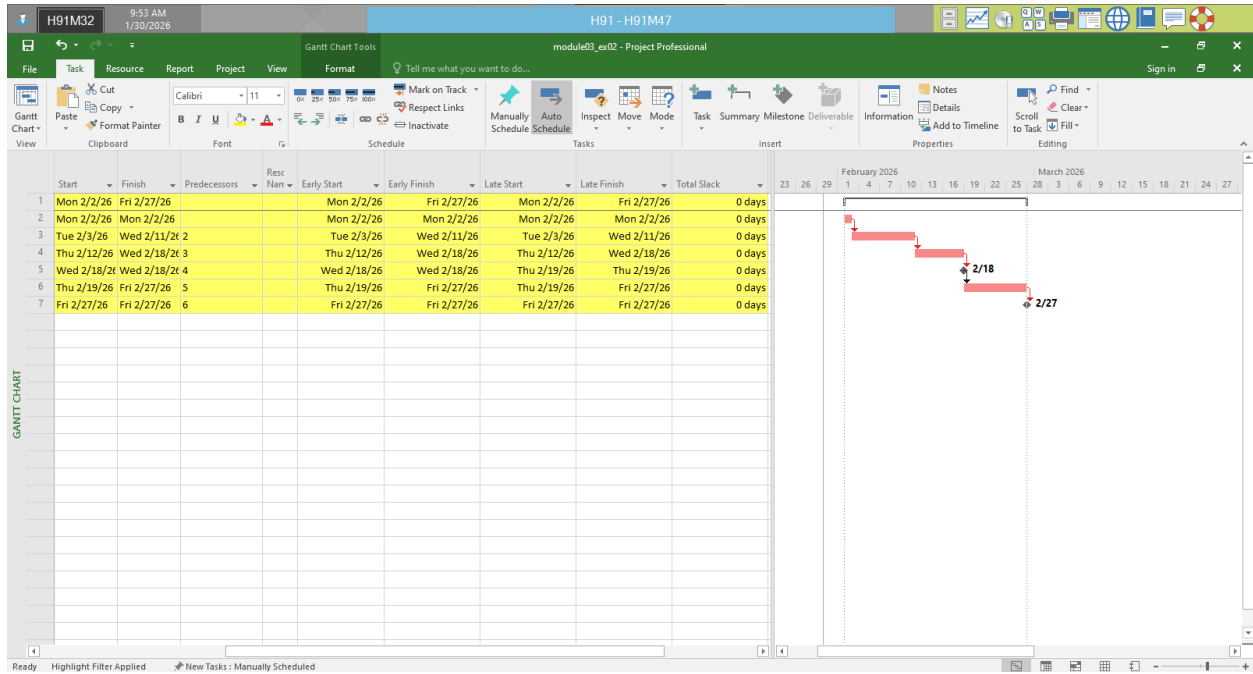



Exercise 3: Scheduling – Task dependencies

Display the Project Information.

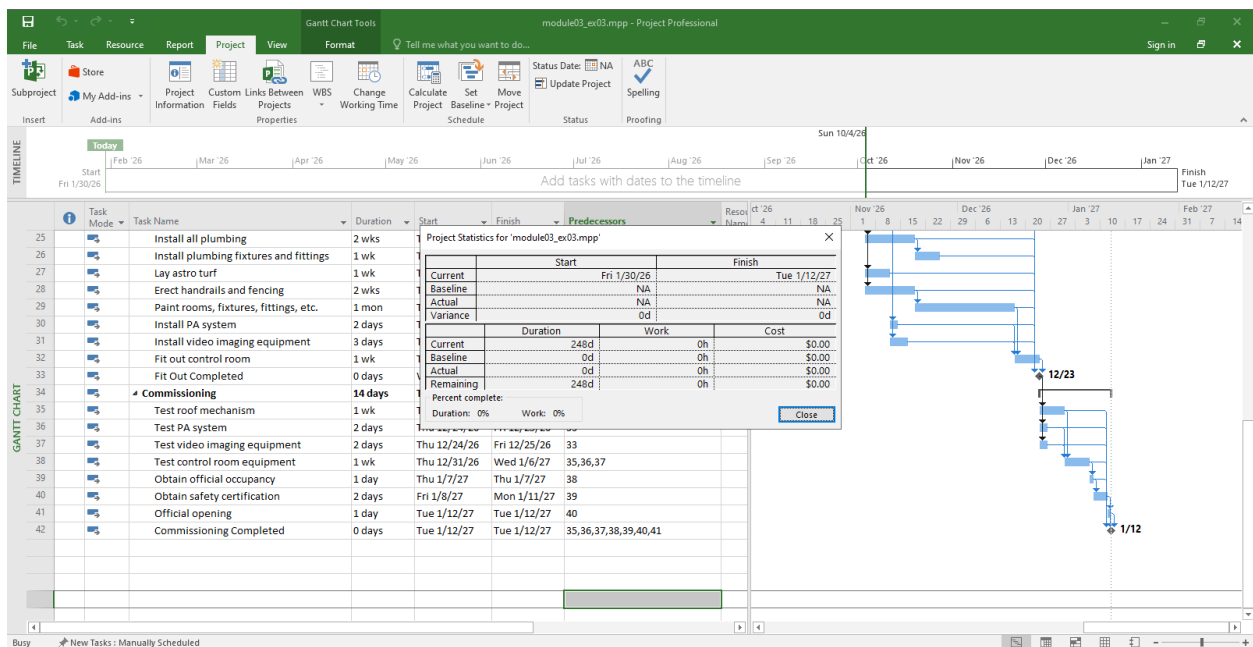


View the project in Gantt Chart and define CP and Project Slack


Lab report – Project Management

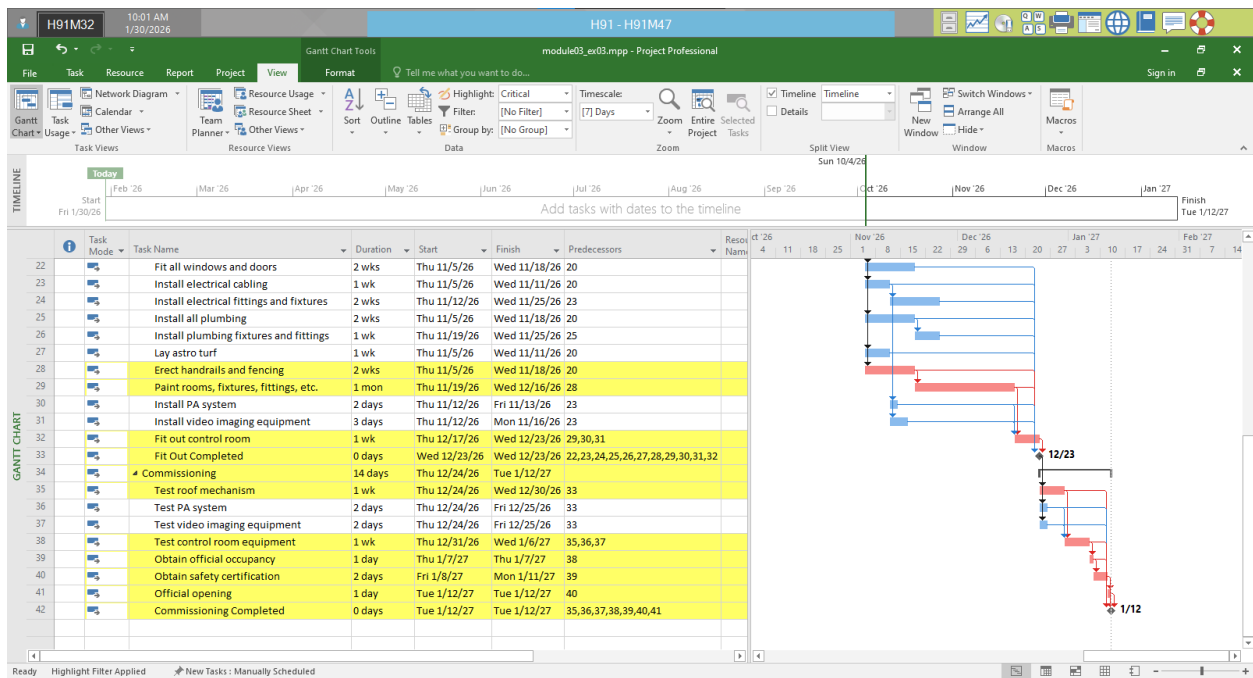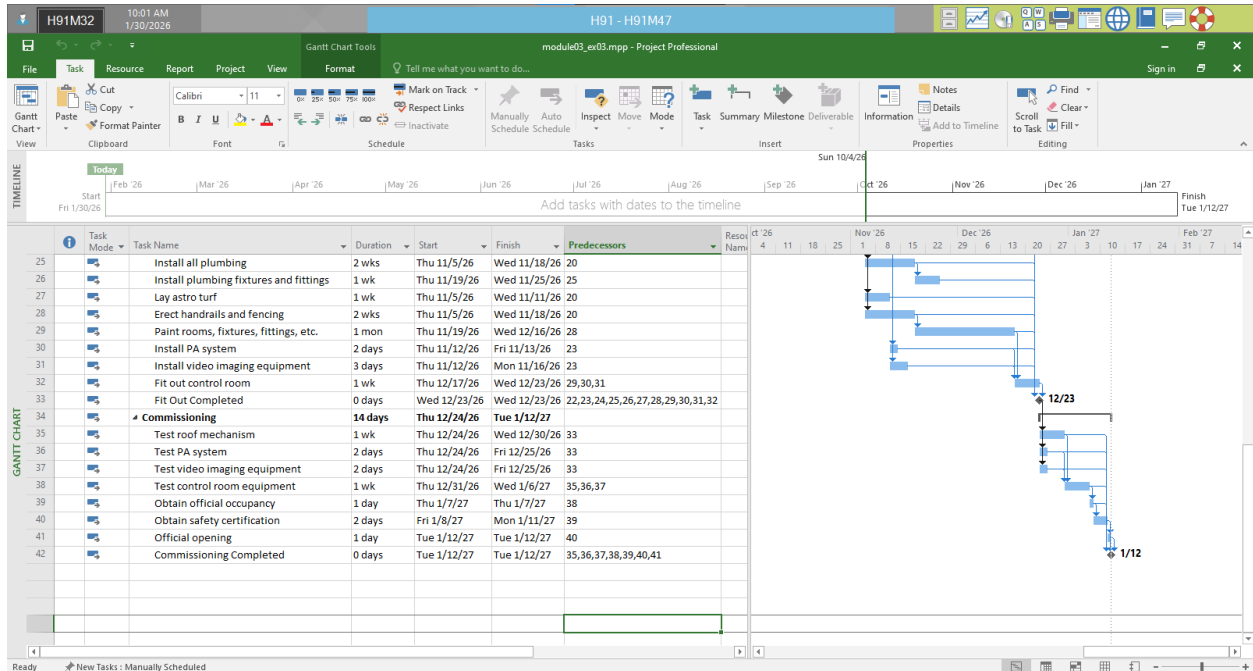

Lab report – Project Management


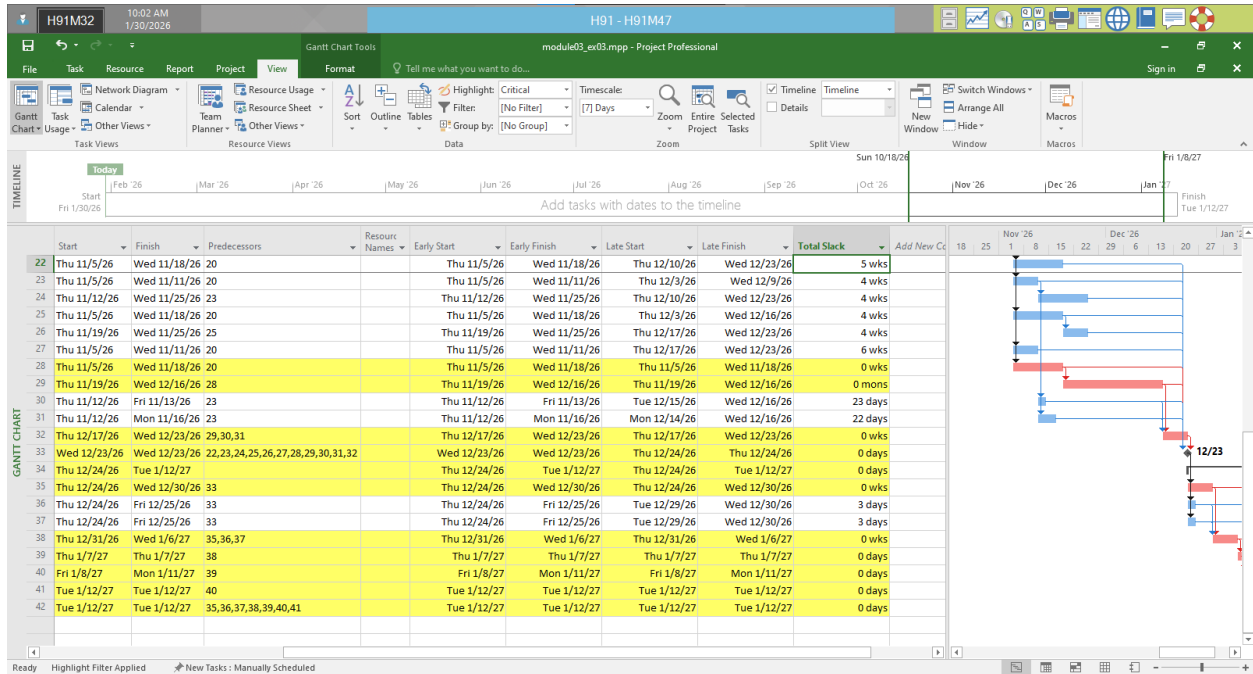


Choose Gantt Chart Format tab ◊ check on Critical Tasks in Bar Styles.

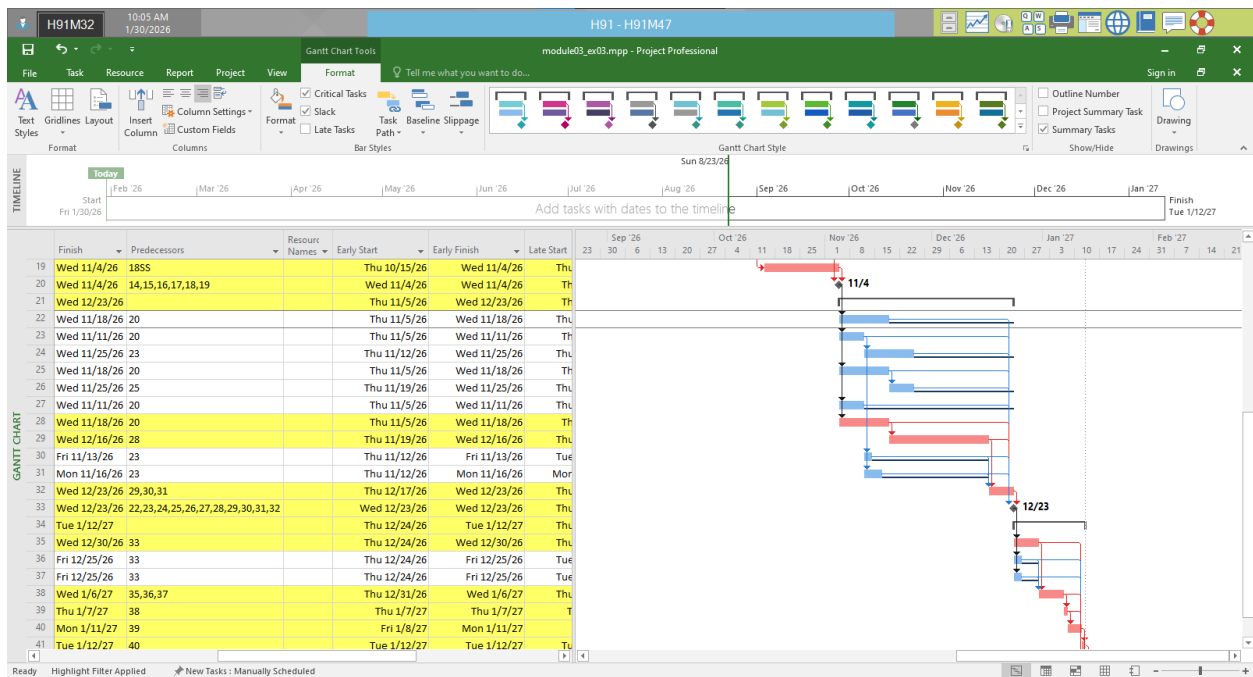

On the table data Add column Late Start, Late Finish, Total Slack


Lab report – Project Management

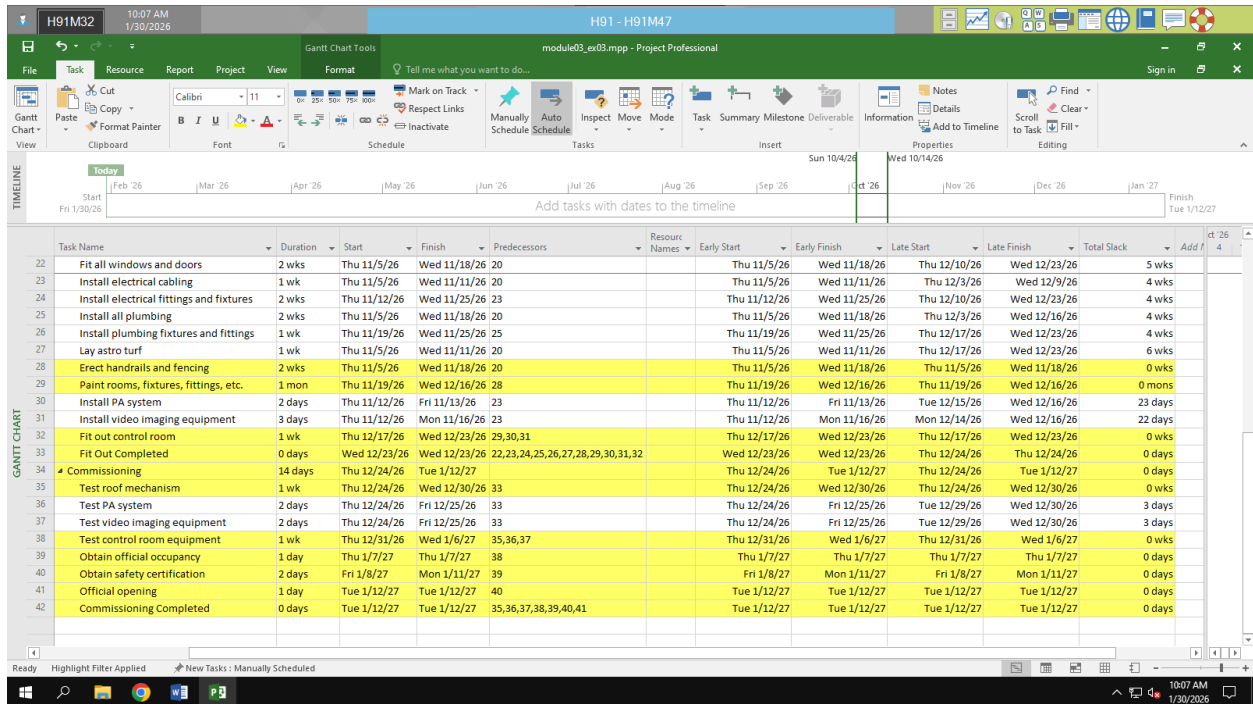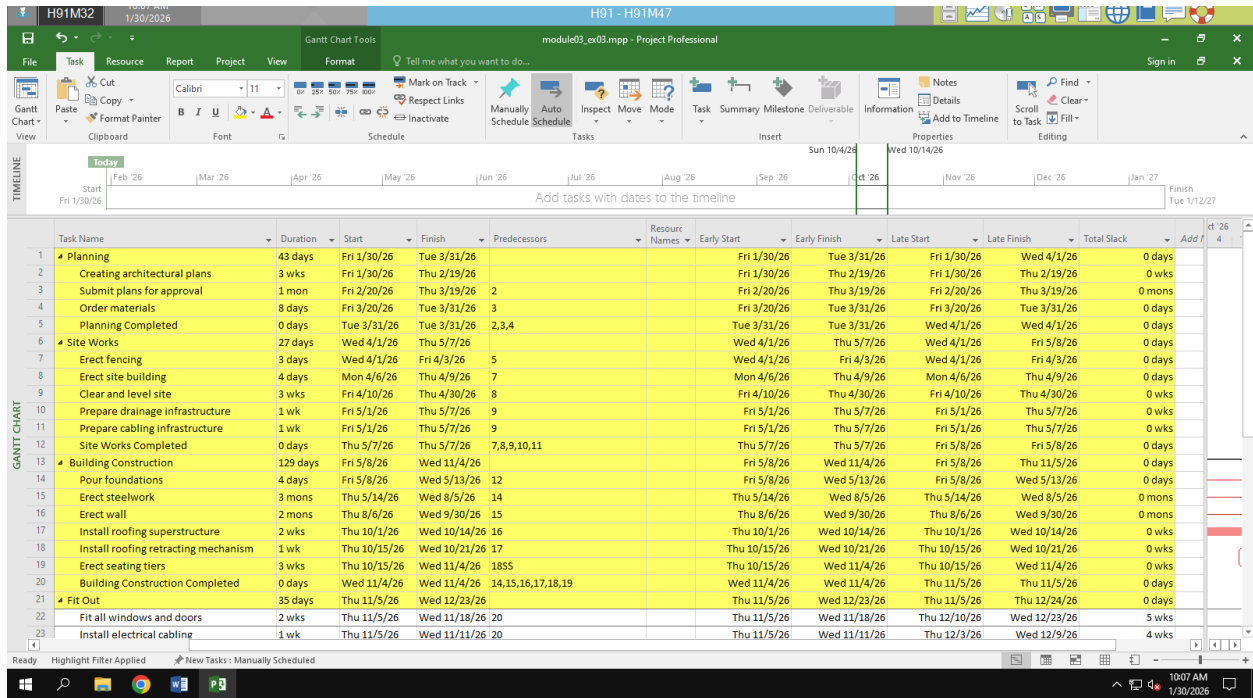

Module 4: Assigning resources to the tasks in Project

Exercise 1: Entering Resources

- Gantt Chart

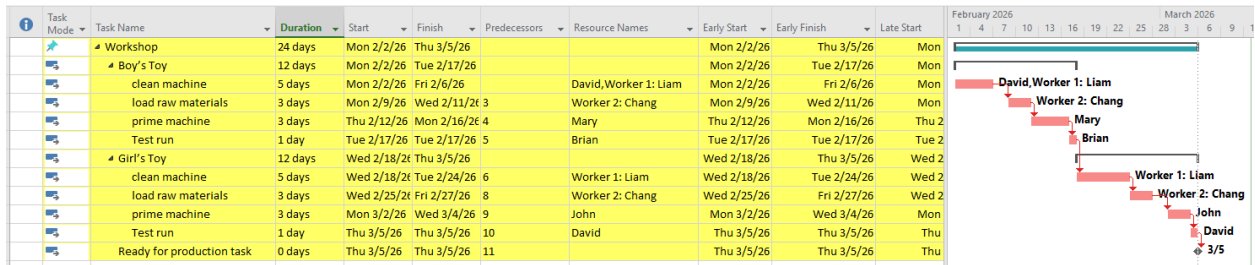

- Display the Project Information (Statics): Duration, Hours, Cost

Project Statistics for 'module04_ex01'

	Start	Finish
Current	Mon 2/2/26	Thu 3/5/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	24d	232h	\$1,544.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	24d	232h	\$1,544.00

Percent complete:

Duration: 0%Work: 0%

Close

- Resource Sheet

Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt.	Cost/Use	Accrue	Base
David	Work		D	Consultar	100%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Brian	Work		B	Staff	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Mary	Work		M	Staff	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
John	Work		J	Staff	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Worker 1: Liam	Work		W	Worker	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
Worker 2: Chang	Work		W	Worker	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard

- Resource Usage

[illegible]

Lab report – Project Management

- Resource Sheet

ew		Clipboard	Font	Font	Schedule		Tasks					
		Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt.	Cost/Use	Accrue	Base
1		MDF	Material	Sheet	M	Material		\$20.00		\$0.00	Prorated	
2		Flooring	Material	Pack	F	Material		\$80.00		\$0.00	Prorated	
3		Purple Material	Material	Roll	P	Material		\$30.00		\$0.00	Prorated	
4		Orange Material	Material	Roll	O	Material		\$120.00		\$0.00	Prorated	

- Resource Usage

iantt hart		Paste Format Painter	B I U	Font	Schedule	Manually Schedule	Auto Schedule	Inspect	
Clipboard		Font		Schedule		Tasks			
		Resource Name	Work	Add New Column	Details	M	T	W	T
1		MDF	2 Sheet		Work (Sheet)				
		Visit estate agent	2 Sheet		Work (Sheet)				
2		Flooring	4 Pack		Work (Pack)				
		View property	2 Pack		Work (Pack)				
		Make offer	1 Pack		Work (Pack)				
		Wait for decision	1 Pack		Work (Pack)				
3		Purple Material	2 Roll		Work (Roll)				
		Decide what to do	1 Roll		Work (Roll)				
		Make offer	1 Roll		Work (Roll)				
4		Orange Material	3 Roll		Work (Roll)				
		Wait for decision	1 Roll		Work (Roll)				
		offer a acceptance	2 Roll		Work (Roll)				
					Work				
					Work				
					Work				

Exercise 3: Entering resources

- Gantt Chart (Resource Name, Cost Column)

	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost	
1		Planning	1 wk	Fri 3/13/26	Thu 3/19/26		PM	\$400.00	
2		Requirement documents	2 wks	Fri 3/20/26	Thu 4/2/26	1	Designer, PM	\$1,280.00	
3		Sign off	1 day	Fri 4/3/26	Fri 4/3/26	2	PM	\$80.00	
4		Development	10 wks	Mon 4/6/26	Fri 6/12/26	3	Developer, Operating System[1 Unit], Visual Studio[1 Unit]	\$3,322.00	
5		Testing	4 wks	Mon 6/15/26	Fri 7/10/26	4	Tester	\$960.00	
6		Implementation	2 wks	Mon 7/13/26	Fri 7/24/26	5	Maintainer, Cable[100 M], Operating System[1 Unit], Visual Studio[1 Unit]	\$622.00	
7		Review	1 wk	Mon 7/27/26	Fri 7/31/26	6	Maintainer, PM	\$600.00	

- Display the Project Information (Statics): Duration, Hours, Cost

Lab report – Project Management

	Start	Finish
Current	Fri 3/13/26	Fri 7/31/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	101d	928h	\$7,264.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	101d	928h	\$7,264.00

Percent complete:

Duration: 0% Work: 0%

Close

- Resource Sheet

	Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt.	Cost/Use	Accrue	Base	Code	Add New Column
1	PM	Work		P	Sponsor	100%	\$10.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
2	Designer	Work		D	Staff	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
3	Developer	Work		D	Staff	100%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
4	Tester	Work		T	Staff	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
5	Maintainer	Work		M	Staff	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard		
6	Operating System	Material	Unit	O	Material		\$120.00		\$0.00	Prorated			
7	Internet Provider	Material	Unit	I	Material		\$100.00		\$0.00	Prorated			
8	Cable	Material	M	C	Material		\$1.00		\$0.00	Prorated			
9	Visual Studio	Material	Unit	V	Material		\$2.00		\$0.00	Prorated			

- Resource Usage

	Resource Name	Work	Add New Column	Details	M	T	W	T	F	S	Mar 15, '26	M	T	W	T	F	S	Mar 22, '26	M	T	W	T
1	PM	168 hrs		Work					8h													
	Planning	40 hrs		Work					8h													
	Requirement	80 hrs		Work							8h	8h	8h	8h	8h							
	Sign off	8 hrs		Work												8h						
	Review	40 hrs		Work																		
2	Designer	80 hrs		Work												8h			8h	8h	8h	
	Requirement	80 hrs		Work															8h	8h	8h	
3	Developer	400 hrs		Work												8h						
	Development	400 hrs		Work																		
4	Tester	160 hrs		Work																		
	Testing	160 hrs		Work																		
5	Maintainer	120 hrs		Work																		
	Implementat	80 hrs		Work																		
	Review	40 hrs		Work																		
6	Operating System	2 Unit		Work																		
	Development	1 Unit		Work																		
	Implementat	1 Unit		Work																		
7	Internet Provider	0 Unit		Work																		
8	Cable	100 M		Work																		
	Implementat	100 M		Work																		
9	Visual Studio	2 Unit		Work																		
	Development	1 Unit		Work																		
	Implementat	1 Unit		Work																		

Exercise 4: Entering resources

- Gantt Chart (Resource Name, Cost Column)

Lab report – Project Management

Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Ear	Ear	L	L	T	T	Cost	2027	2028	2029	2030	2031
1	Planning	88 days	Fri 1/30/26	Tue 6/2/26									\$5,280.00					
2	Creating architectural plans	12 wks	Fri 1/30/26	Thu 4/23/26		Architect, Building Clerk[25%							\$2,880.00					
3	Submit plans for approval	1 mon	Fri 4/24/26	Thu 5/21/26	2	Architect							\$1,440.00					
4	Order materials	8 days	Fri 5/22/26	Tue 6/2/26	3	Building Clerk, Draftsperson							\$960.00					
5	Planning Completed	0 days	Tue 6/2/26	Tue 6/2/26	2,3,4								\$0.00					
6	Site Works	32 days	Wed 6/3/26	Thu 7/16/26									\$5,288.00					
7	Erect fencing	3 days	Wed 6/3/26	Fri 6/5/26	5	No Barrier Fencing							\$72.00					
8	Erect site building	4 days	Mon 6/8/26	Thu 6/11/26	7	Carpenter[400%], Labourer, N							\$896.00					
9	Clear and level site	3 wks	Fri 6/12/26	Thu 7/2/26	8	Supervisor, Driver[200%], Gra							\$3,120.00					
10	Prepare drainage infrastructure	2 wks	Fri 7/3/26	Thu 7/16/26	9	Plumber[200%], Supervisor[5							\$680.00					
11	Prepare cabling infrastructure	1 wk	Fri 7/3/26	Thu 7/9/26	9	Electrician[300%], Supervisor							\$520.00					
12	Site Works Completed	0 days	Thu 7/16/26	Thu 7/16/26	7,8,9,10,11								\$0.00					
13	Building Construction	334 days	Fri 7/17/26	Wed 10/27/27									\$57,888.00					
14	Pour foundations	4 days	Fri 7/17/26	Wed 7/22/26	12	Rock Solid Concrete							\$128.00					
15	Erect steelwork	6 mons	Thu 7/23/26	Wed 6/6/27	14	Boilermaker[600%], Driver[20							\$25,920.00					
16	Erect wall	8 mons	Thu 7/23/26	Wed 8/18/27	15	Supervisor[50%], Carpenter[7							\$18,560.00					
17	Install roofing superstructure	4 wks	Thu 8/19/27	Wed 9/15/27	16	Supervisor[50%], Rigger[500%							\$5,280.00					
18	Install roofing retracting mechanism	2 wks	Thu 9/16/27	Wed 9/29/27	17	Supervisor[50%], Welder, Boile							\$2,000.00					
19	Erect seating tiers	6 wks	Thu 9/16/27	Wed 10/27/27	1855	Supervisor[50%], Carpenter[8							\$6,000.00					
20	Building Construction Completed	0 days	Wed 10/27/27	Wed 10/27/27	14,15,16,17								\$0.00					
21	Fit Out	14 days	Thu 10/28/27	Tue 11/16/27									\$6,120.00					
22	Fit all windows and doors	1 wk	Thu 10/28/27	Wed 11/3/27	20	Carpenter[500%], Labourer[2							\$1,040.00					
23	Install electrical cabling	0.5 wks	Thu 10/28/27	Mon 11/1/27	20	Electrician[300%], Labourer[2							\$520.00					

Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Ear	Ear	L	L	T	T	Cost	2027	2028	2029	2030	2031
22	Fit all windows and doors	1 wk	Thu 10/28/27	Wed 11/3/27	20	Carpenter[500%], Labourer[2							\$1,040.00					
23	Install electrical cabling	0.5 wks	Thu 10/28/27	Mon 11/1/27	20	Electrician[300%], Labourer[2							\$520.00					
24	Install electrical fittings and fixtures	0.67 wks	Mon 11/1/27	Thu 11/4/27	23	Electrician[300%]							\$560.00					
25	Install all plumbing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Plumber[200%], Labourer[200							\$880.00					
26	Install plumbing fixtures and fittings	0.5 wks	Thu 11/4/27	Mon 11/8/27	25	Plumber[200%]							\$200.00					
27	Lay astro turf	1 wk	Thu 10/28/27	Wed 11/3/27	20	Pure Grass Turf							\$200.00					
28	Erect handrails and fencing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Welder[400%], Boilermaker[2							\$880.00					
29	Paint rooms, fixtures, fittings, etc.	0.2 mons	Thu 11/4/27	Tue 11/9/27	28	Painter[500%]							\$960.00					
30	Install PA system	2 days	Mon 11/1/27	Thu 11/3/27	23	Listen Ear Audio							\$80.00					
31	Install video imaging equipment	3 days	Mon 11/1/27	Thu 11/4/27	23	In Focus Video							\$120.00					
32	Fit out control room	1 wk	Wed 11/10/27	Tue 11/16/27	29,30,31	Electrician[200%], Listen Ear							\$680.00					
33	Fit Out Completed	0 days	Tue 11/16/27	Tue 11/16/27	22,23,24,25								\$0.00					
34	Commissioning	33.5 days	Wed 11/17/27	Mon 1/3/28									\$3,160.00					
35	Test roof mechanism	1 wk	Wed 11/17/27	Tue 11/23/27	33	Supervisor, Electrician[200%]							\$960.00					
36	Test PA system	2 days	Wed 11/17/27	Thu 11/18/27	33	Listen Ear Audio							\$80.00					
37	Test video imaging equipment	2 days	Wed 11/17/27	Thu 11/18/27	33	In Focus Video							\$80.00					
38	Test control room equipment	5 wks	Wed 11/24/27	Tue 12/28/27	35,36,37	Supervisor, Listen Ear Audio							\$1,520.00					
39	Obtain official occupancy	1 day	Wed 12/29/27	Wed 12/29/27	38	Architect, Building Clerk, Supe							\$232.00					
40	Obtain safety certification	2 days	Thu 12/30/27	Fri 12/31/27	39	Supervisor							\$192.00					
41	Official opening	0.5 days	Mon 1/3/28	Mon 1/3/28	40	Supervisor[200%]							\$96.00					
42	Commissioning Completed	0 days	Mon 1/3/28	Mon 1/3/28	35,36,37,38								\$0.00					

- Display the Project Information (Statics): Duration, Hours, Cost

Project Statistics for 'module04_ex04'			
	Start	Finish	
Current	Fri 1/30/26	Mon 1/3/28	
Baseline	NA	NA	
Actual	NA	NA	
Variance	0d	0d	
	Duration	Work	Cost
Current	501.5d	11,212h	\$77,736.00
Baseline	0d	0h	\$0.00
Actual	0d	0h	\$0.00
Remaining	501.5d	11,212h	\$77,736.00
Percent complete:			
Duration: 0%		Work: 0%	
Close			

- Resource Sheet

Lab report – Project Management

		Resource Name	Type	Material Label	Initials	Group	Max. Units	Std. Rate	Ovt.	Cost/Use	Accrue	Base
1		Architect	Work		Arc	Consultant	100%	\$9.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
2		Draftsperson	Work		Dft	Staff	200%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
3		Building Clerk	Work		BC	Staff	100%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
4		Supervisor	Work		Sup	Staff	100%	\$12.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
5		Rigger	Work		Rig	Wages	600%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
6		Boilermaker	Work		BM	Wages	600%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
7		Welder	Work		Weld	Wages	500%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
8		Carpenter	Work		Car	Wages	800%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
9		Painter	Work		Ptr	Wages	500%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
10		Labourer	Work		Lab	Wages	1,000%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
11		Driver	Work		Drv	Wages	300%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
12		No Barrier Fencing	Work		NBF	Contractor	100%	\$3.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
13		Rock Solid Concrete	Work		RSC	Contractor	100%	\$4.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
14		Listen Ear Audio	Work		LEA	Contractor	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
15		In Focus Video	Work		IFV	Contractor	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
16		Pure Grass Turf	Work		PGT	Contractor	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
17		Building Inspector	Work		BI	Government	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
18		High Jib Crane	Work		HJC	Equipment	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
19		Grader	Work		Grd	Equipment	200%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
20		Air Compressor	Work		AC	Equipment	100%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
21		Utility	Work		Ute	Equipment	200%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
22		Electrician	Work		Cap	Staff	400%	\$7.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
23		Plumber	Work		Plu	Staff	400%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
24		Astro Turf	Material	Square Matre	Grass	Material		\$12.00		\$0.00	Prorated	
25		Paint	Material	Ultra	Paint	Ita		\$20.00		\$0.00	Prorated	

- Resource Usage


	Resource Name	Work	Add New Column	Details	H1	2025 H2	H1	2026 H2	H1	2027 H2	H1	2028 H2	H1	2029 H2
	Unassigned	0 hrs		Work										
	Planning Con	0 hrs		Work										
	Site Works Co	0 hrs		Work										
	Building Cons	0 hrs		Work										
	Fit Out Comp	0 hrs		Work										
	Commissioni	0 hrs		Work										
1	Architect	328 hrs		Work			280h			48h				
	Creating arch	120 hrs		Work			120h							
	Submit plans	160 hrs		Work			160h							
	Test control r	40 hrs		Work						40h				
	Obtain offic	8 hrs		Work						8h				
2	Draftsperson	184 hrs		Work			184h							
	Creating arch	120 hrs		Work			120h							
	Order materi	64 hrs		Work			64h							
3	Building Clerk	192 hrs		Work			184h			8h				
	Creating arch	120 hrs		Work			120h							
	Order materi	64 hrs		Work			64h							
	Obtain offic	8 hrs		Work						8h				
4	Supervisor	1,364 hrs		Work			136h	540h	336h	344h	8h			
	Erect site buil	32 hrs		Work			32h							
	Clear and lev	120 hrs		Work			104h	16h						
	Prepare drain	40 hrs		Work				40h						
	Prepare cabli	20 hrs		Work				20h						
	Erect steelwo	480 hrs		Work			464h	16h						

Exercise 5: Resources with the private working time


Capture images:

- Gantt Chart (Resource Name, Cost Column)


Lab report – Project Management

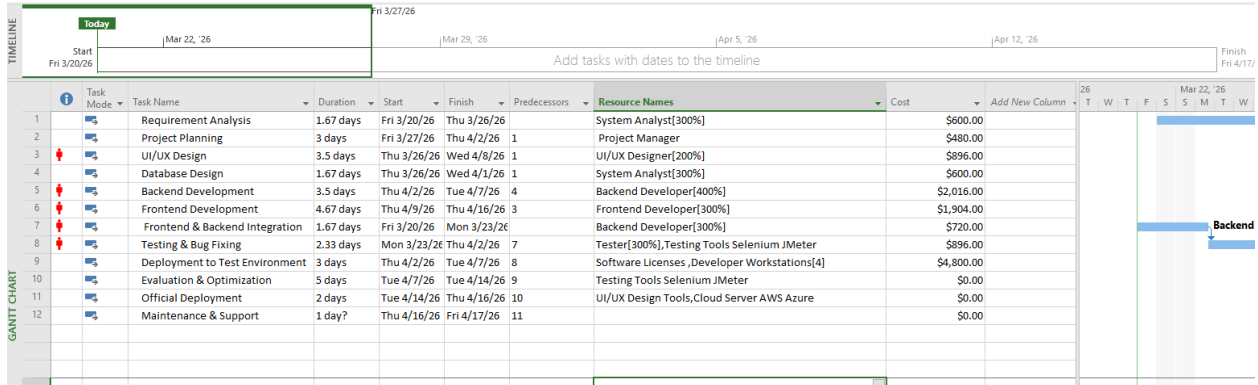

- Display the Project Information (Statics): Duration, Hours, Cost

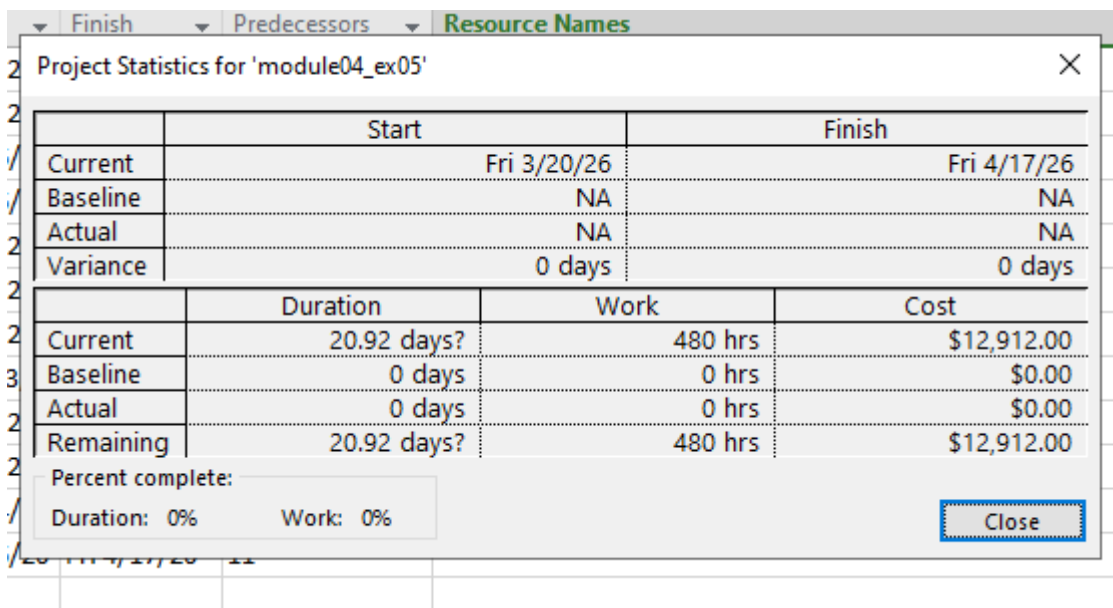


- Resource Sheet

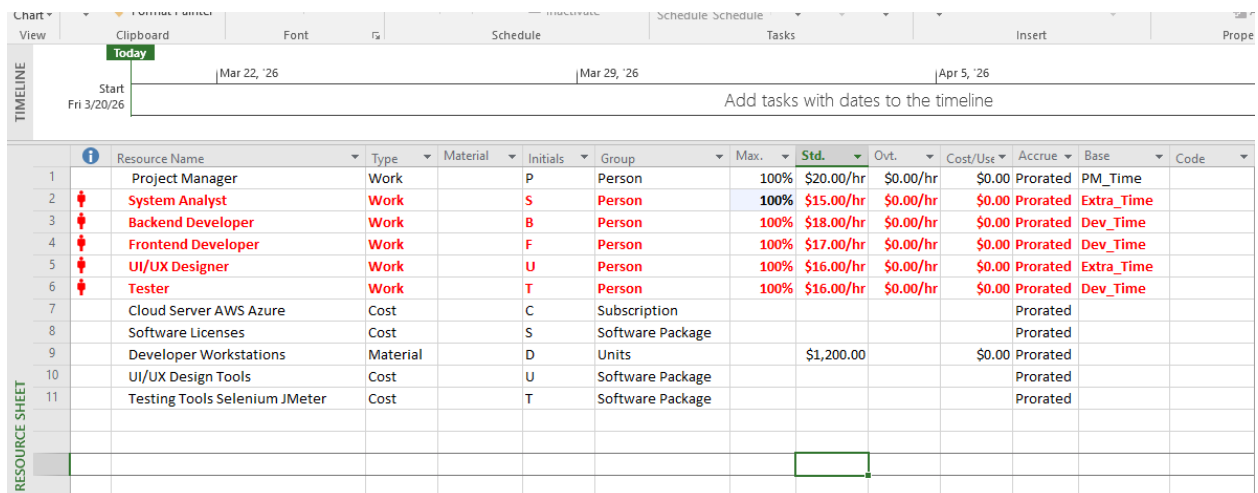

Lab report – Project Management

- Resource Usage

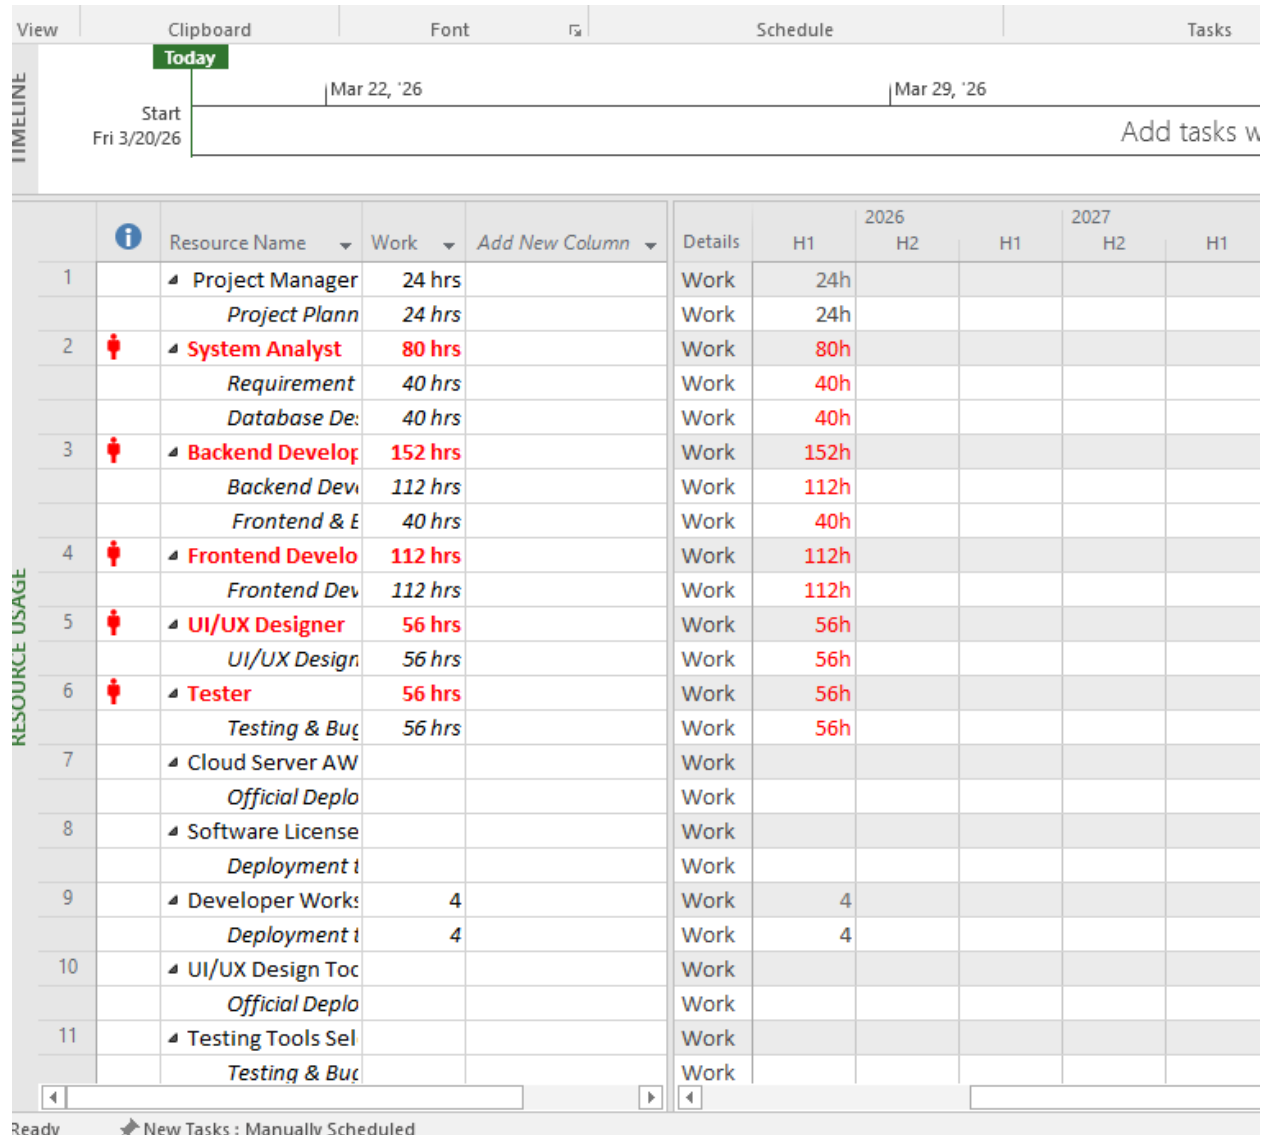


Exercise 6: The Engagement planning


Capture images:

- Gantt Chart (Resource Name, Cost Column)

Lab report – Project Management

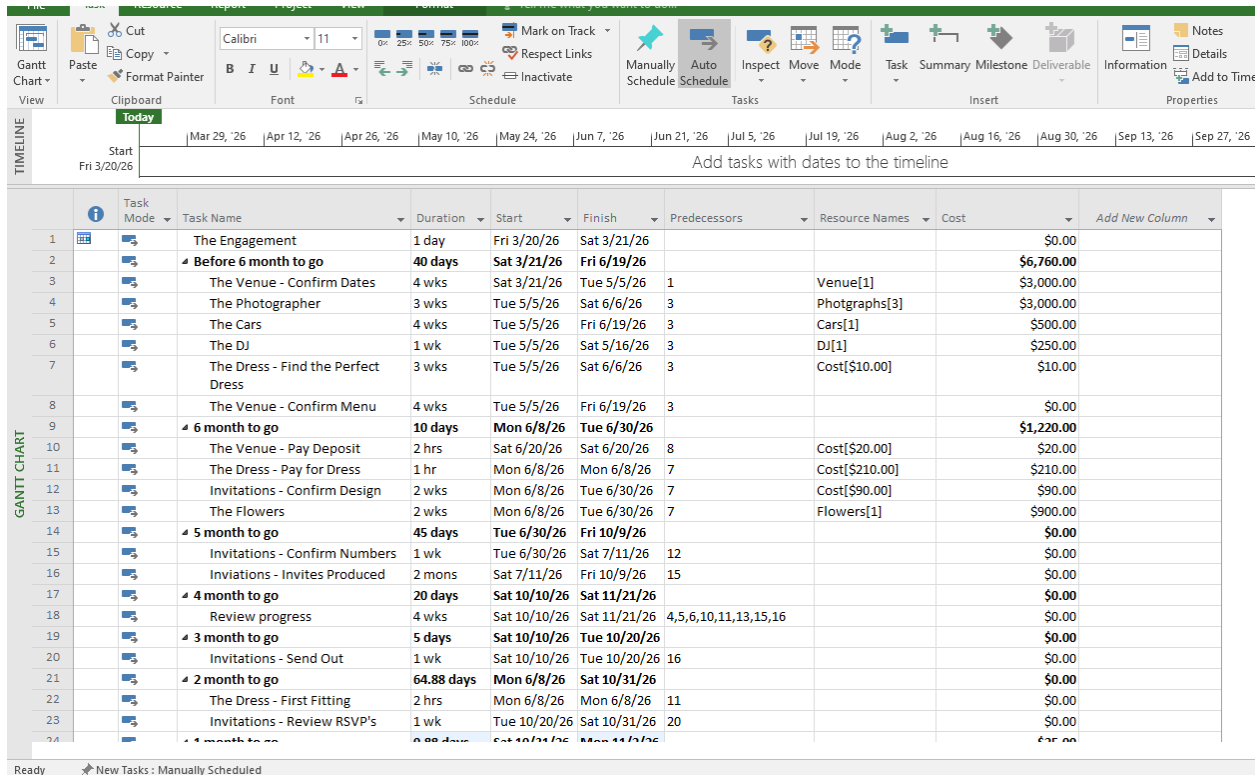

- Display the Project Information (Statics): Duration, Hours, Cost

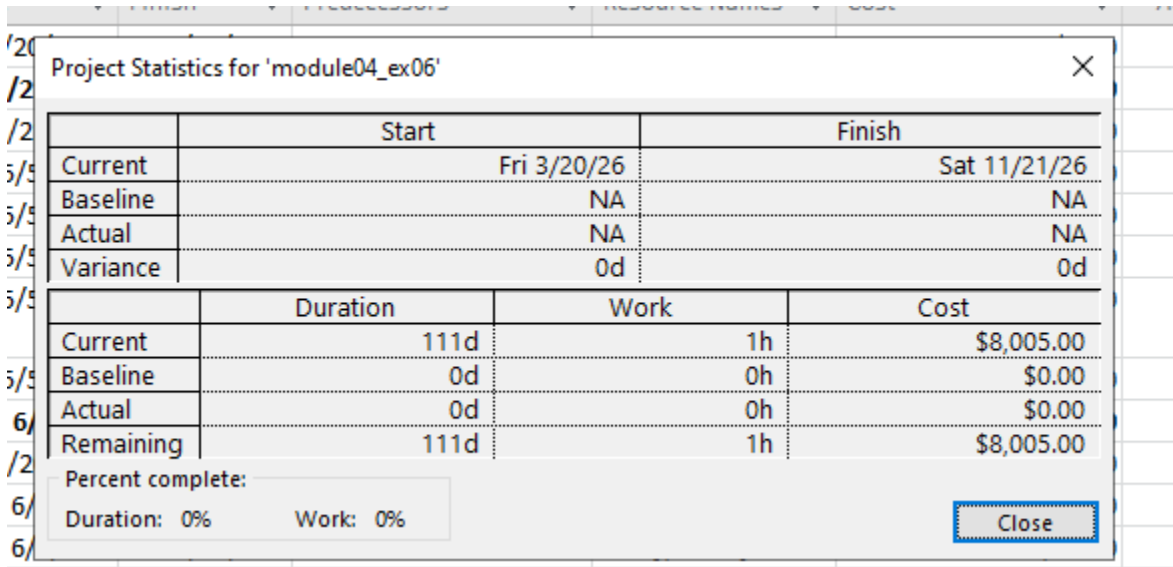

- Resource Sheet - Resource Usage

Lab report – Project Management

module04_ex06 - Project Professional

File Task Resource Report Project View Format Tell me what you want to do...

Gantt Chart View Paste Copy Format Painter Clipboard Font Calibri 11 Bold Italic Underline Color Font Background Color Schedule 0% 25% 50% 75% 100% Mark on Track Respect Links Inactivate Manually Schedule Auto Schedule Inspect Move Mode Task Summary

TIMELINE Today Start Fri 3/20/26 Mar 29, '26 Apr 12, '26 Apr 26, '26 May 10, '26 May 24, '26 Jun 7, '26 Jun 21, '26 Jul 5, '26 Jul 19, '26 Aug 2, '26 Add tasks with dates to the timeline

	Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt.	Cost/Use	Accrue	Code	Ad
1	Venue	Material		Initials			\$3,000.00		\$0.00	Prorated		
2	Photographs	Material		V			\$1,000.00		\$0.00	Prorated		
3	Flowers	Material		P			\$900.00		\$0.00	Prorated		
4	Cars	Material		F			\$500.00		\$0.00	Prorated		
5	DJ	Material		C			\$250.00		\$0.00	Prorated		
6	Guest	Work		D		8,000%	\$25.00/hr	\$0.00/hr	\$0.00	Prorated		
7	Cost	Cost		C						Prorated		

TIMELINE Mon 3/16/26 Today Start Fri 3/20/26 Fri 4/3/26 Mar 29, '26 Apr 12, '26 Apr 26, '26 May 10, '26 May 24, '26 Jun 7, '26 Jun 21, '26 Jul 5, '26 Jul 19, '26 Aug 2, '26 Aug 16, '26 Aug 30, '26 Add tasks with dates to the timeline

RESOURCE USAGE


Resource Name	Work	Add New Column	Details	M	T	W	T	F	S	S	M	T	W
Unassigned	0 hrs		Work										
The Engagem	0 hrs		Work										
The Venue - C	0 hrs		Work										
Invitations - C	0 hrs		Work										
Invitations - Ir	0 hrs		Work										
Review progr	0 hrs		Work										
Invitations - S	0 hrs		Work										
The Dress - Fi	0 hrs		Work										
Invitations - F	0 hrs		Work										
The Venue - C	0 hrs		Work										
The Venue - C	0 hrs		Work										
The Dress - Fir	0 hrs		Work										
The Big day (	0 hrs		Work										
1 Venue	1		Work						0.03		0.02	0.02	0.02
The Venue - C	1		Work						0.03		0.02	0.02	0.02
2 Photographs	3		Work										
The Photogrc	3		Work										
3 Flowers	1		Work										
The Flowers	1		Work										
4 Cars	1		Work										
The Cars	1		Work										
5 DJ	1		Work										
The DJ	1		Work										
6 Guest	1 hr		Work										
The Venue - C	1 hr		Work										

Dashboard New Tasks - Manually Scheduled

Lab report – Project Management

Module 5: COST, CONSTRAINS, DEADLINE for TASKs

Exercise 1: Entering Cost

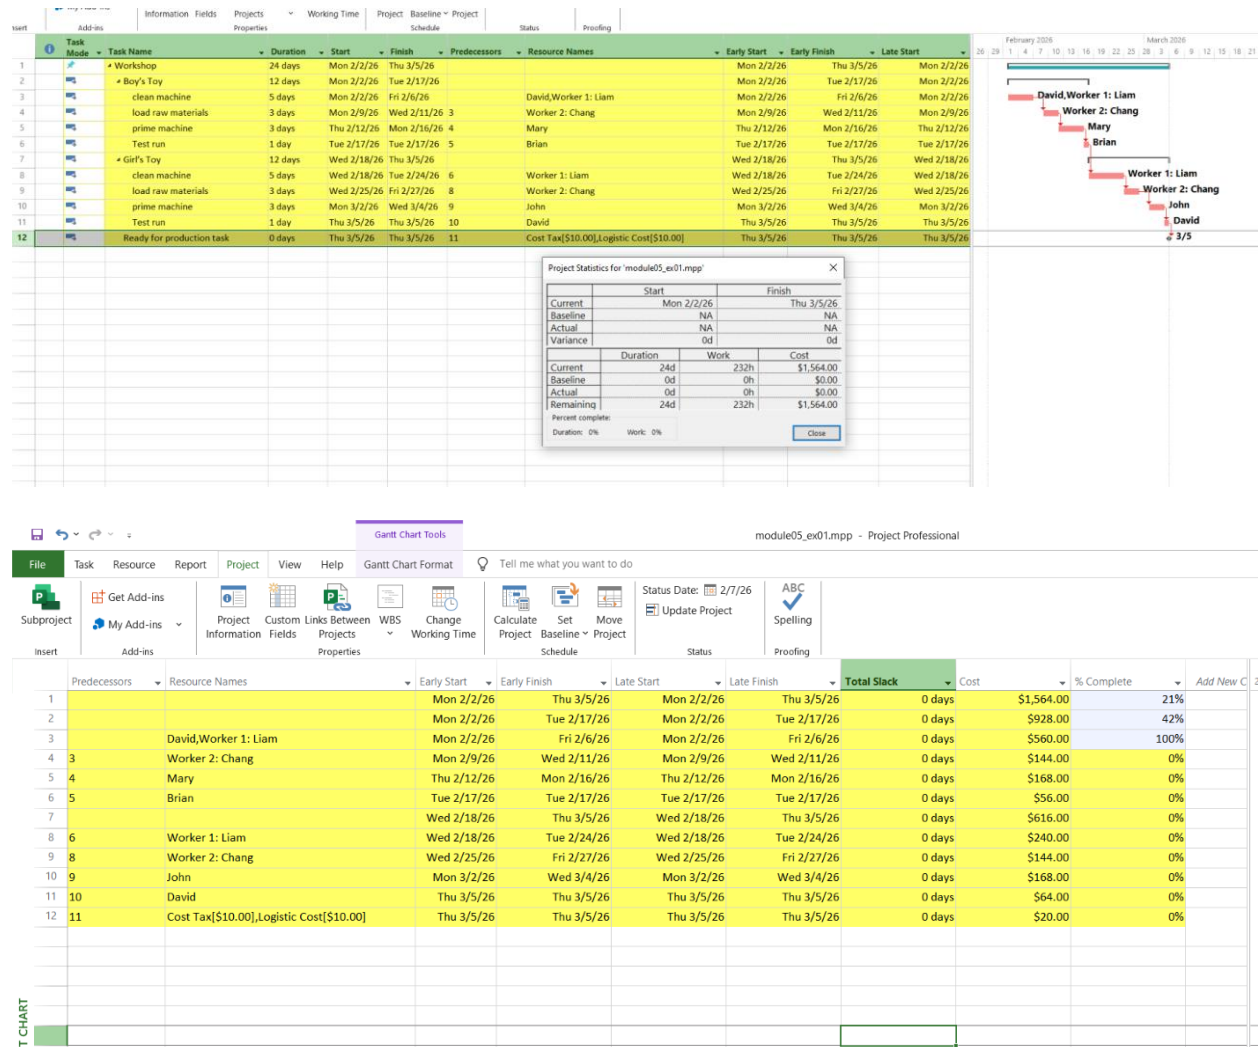

Lab report – Project Management

Exercise 2:

Resource Sheet Tools

module05_ex02.mpp - Project Professional

File Task Resource Report Project View Help Resource Sheet Format Tell me what you want to do

Calibri 11

Mark on Track Respect Links Inactivate

Manually Schedule Auto Schedule

Inspect Move Mode

Task Summary Milestone Deliverable

GET GENUINE OFFICE Your license isn't genuine, and you may be a victim of software counterfeiting. Avoid interruption and keep your files safe with genuine Office today. Get genuine Office Learn more

	Resource Name	Type	Material	Initials	Group	Max.	Std. Rate	Ovt. Rate	Cost/Use	Accrue	Base	Code	Add New Column
1	MDF	Material	Sheet	M	Material		\$20.00		\$0.00	Prorated			
2	Flooring	Material	Pack	F	Material		\$80.00		\$0.00	Prorated			
3	Purple Material	Material	Roll	P	Material		\$30.00		\$0.00	Prorated			
4	Orange Material	Material	Roll	O	Material		\$120.00		\$0.00	Prorated			
5	Cost Tax	Cost		C						Prorated			
6	Logistic Cost	Cost		L						Prorated			
7	OT Cost	Cost		O						Prorated			
8	Bonus	Cost		B						Prorated			
9	Punishment	Cost		P						Prorated			

RESOURCE SHEET

Gantt Chart Tools

module05_ex02.mpp - Project Professional

File Task Resource Report Project View Help Gantt Chart Format Tell me what you want to do

Calibri 11

Mark on Track Respect Links Inactivate

Manually Schedule Auto Schedule

Inspect Move Mode

Task Summary Milestone Deliverable

Information Details Add to Timeline

Find Clear Fill

GET GENUINE OFFICE Your license isn't genuine, and you may be a victim of software counterfeiting. Avoid interruption and keep your files safe with genuine Office today. Get genuine Office Learn more

	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost	% Complete	Add New
1	Buy a shop	22 days	Mon 2/2/26	Tue 3/3/26			\$943.00	0%	
2	Visit estate agents	1 day	Mon 2/2/26	Mon 2/2/26		MDF[2 Sheet],OT Cost [\$50.00]	\$90.00	0%	
3	View properties	7 days	Mon 2/2/26	Wed 2/11/26	2	Flooring[2 Pack],Cost Tax[\$3.00]	\$163.00	0%	
4	Decide what to buy	5 days	Thu 2/12/26	Wed 2/18/26	3	Purple Material[1 Roll],Bonus[\$12.00]	\$42.00	0%	
5	Make offer	1 day	Thu 2/19/26	Thu 2/19/26	4	Flooring[1 Pack],Purple Material[1 Roll],OT Cost [\$8.00],Punishment	\$123.00	0%	
6	Wait for decision	7 days	Fri 2/20/26	Mon 3/2/26	5	Flooring[1 Pack],Orange Material [1 Roll],Logistic Cost[\$75.00]	\$275.00	0%	
7	offer a accepted	1 day	Tue 3/3/26	Tue 3/3/26	6	Orange Material [2 Roll],Bonus[\$10.00]	\$250.00	0%	

GANTT CHART

Lab report – Project Management

module05_ex02.mpp - Project Professional

GET GENUINE OFFICE Your license isn't genuine, and you may be a victim of software counterfeiting. Avoid interruption and keep your files safe with genuine Office today. [Get genuine Office](#) [Learn more](#)

Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost	% Complete	Add New
1	Buy a shop	22 days	Mon 2/2/26	Tue 3/3/26			\$943.00	99%	
2	Visit estate agents	1 day	Mon 2/2/26	Mon 2/2/26		MDF[2 Sheet],OT Cost [\$50.00]	\$90.00	99%	
3	View properties	7 days	Mon 2/2/26	Wed 2/11/26	2	Flooring[2 Pack],Cost Tax[\$3.00]	\$163.00	99%	
4	Decide what to buy	5 days	Thu 2/12/26	Wed 2/18/26	3	Purple Material[1 Roll],Bonus[\$12.00]	\$42.00	99%	
5	Make offer	1 day	Thu 2/19/26	Thu 2/19/26	4	Flooring[1 Pack],Purple Material[1 Roll],OT Cost [\$8.00],Punishment	\$123.00	99%	
6	Wait for decision	7 days	Fri 2/20/26	Mon 3/2/26	5	Flooring[1 Pack],Orange Material[1 Roll],Logistic Cost[\$75.00]	\$275.00	99%	
7	offer a accepted	1 day	Tue 3/3/26	Tue 3/3/26	6	Orange Material [2 Roll],Bonus[\$10.00]	\$250.00	99%	

Exercise 3:

module05_ex03.mpp - Project Professional

GET GENUINE OFFICE Your license isn't genuine, and you may be a victim of software counterfeiting. Avoid interruption and keep your files safe with genuine Office today. [Get genuine Office](#) [Learn more](#)

Timeline


Start: Fri 3/13/26

Today: Mar 15, '26


Add tasks with dates to the timeline

Resource Name	Type	Material	Initials	Group	Max	Std. Rate	Ovt. Rate	Cost/Use	Accrue	Base	Code
PM	Work		P	Sponsor	100%	\$10.00/hr	\$0.00/hr	\$0.00	Prorated	Standard	
Designer	Work		D	Staff	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard	
Developer	Work		D	Staff	100%	\$8.00/hr	\$0.00/hr	\$0.00	Prorated	Standard	
Tester	Work		T	Staff	100%	\$6.00/hr	\$0.00/hr	\$0.00	Prorated	Standard	
Maintainer	Work		M	Staff	100%	\$5.00/hr	\$0.00/hr	\$0.00	Prorated	Standard	
Operating System	Material	Unit	O	Material		\$120.00		\$0.00	Prorated		
Internet Provider	Material	Unit	I	Material		\$100.00		\$0.00	Prorated		
Cable	Material	M	C	Material		\$1.00		\$0.00	Prorated		
Visual Studio	Material	Unit	V	Material		\$2.00		\$0.00	Prorated		
Tax	Cost		T						Prorated		
Upgrade Fee	Cost		U						Prorated		
Maintain Fee	Cost		M						Prorated		
Bonus	Cost		B						Prorated		
Part Time Fee	Cost		P						Prorated		


Lab report – Project Management

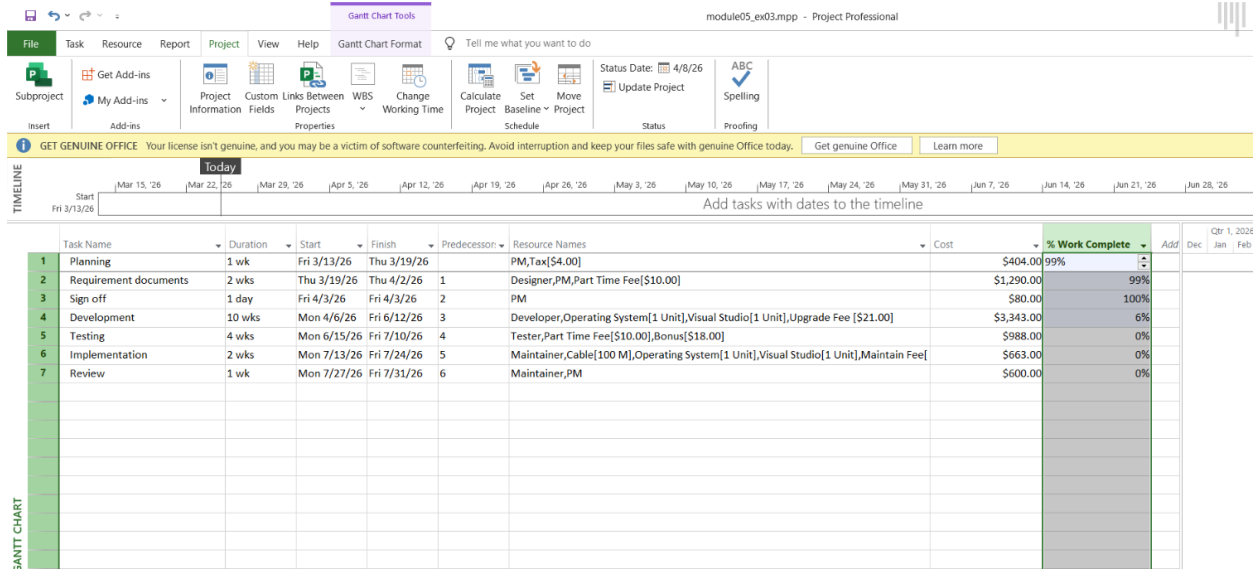

Exercise 4:

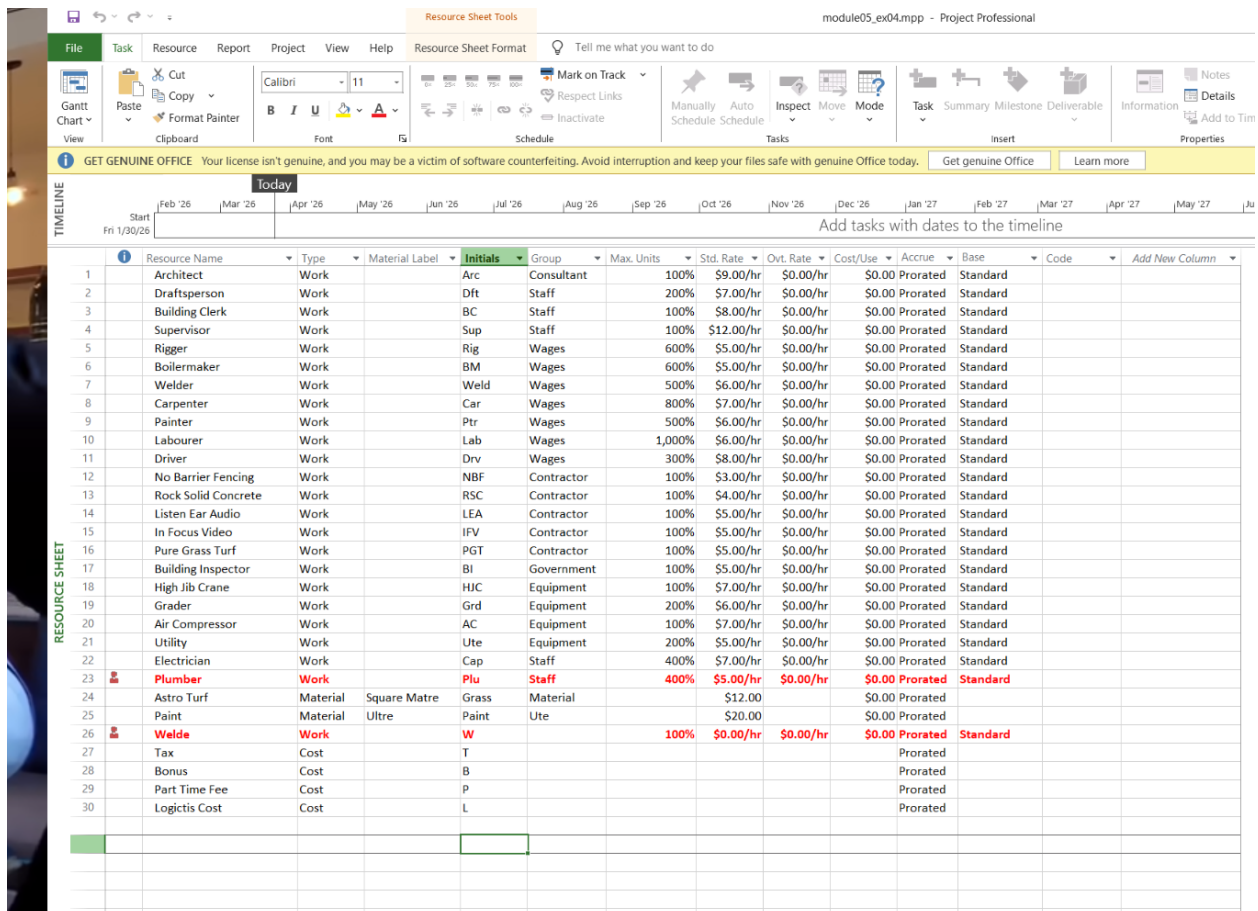

Lab report – Project Management

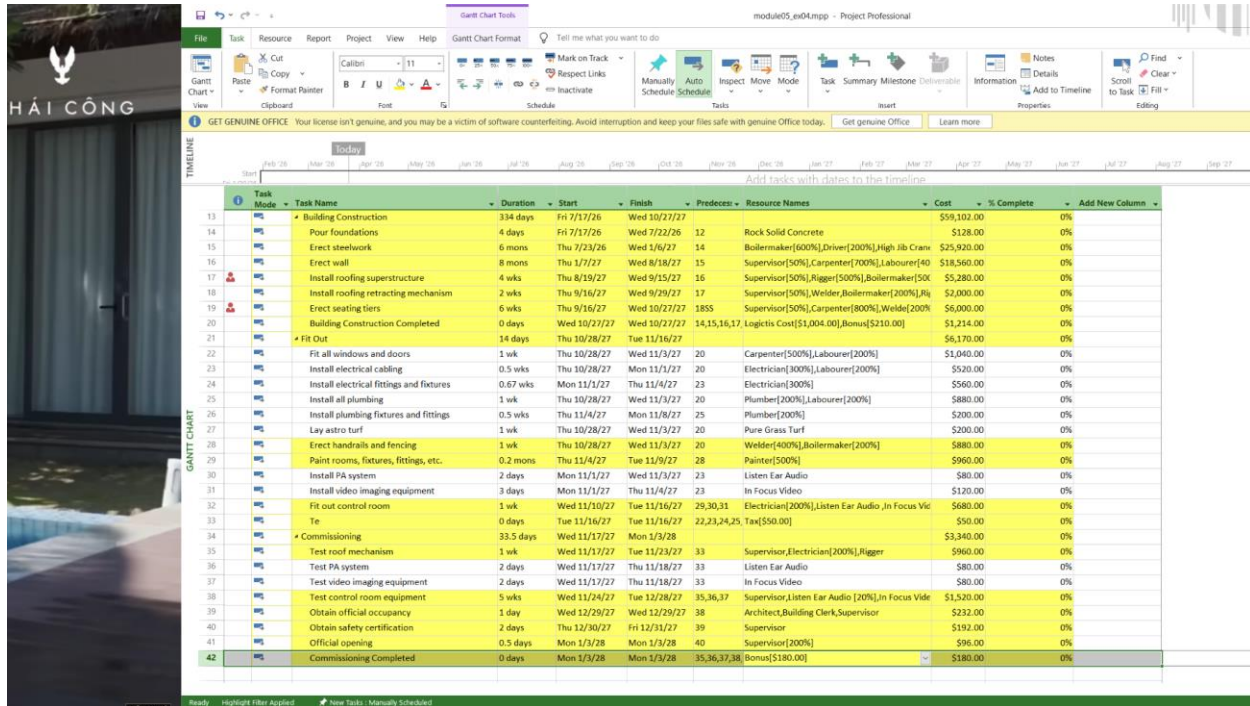

Cost of project? .

Wed 10/27/27			\$59,102.00	0%
Wed 7/22/26	12	Rock Solid Concrete	\$128.00	0%
Wed 1/6/27	14	Boilermaker[600%],Driver[200%],High Jib Crane	\$25,920.00	0%
Wed 8/18/27	15	Supervisor[50%],Carpenter[700%],Labourer[40	\$18,560.00	0%
Wed 9/15/27				0%
Wed 9/29/27				0%
Wed 10/27/27				0%
27 Wed 10/27/27				0%
7 Tue 11/16/27				0%
7 Wed 11/3/27				0%
7 Mon 11/1/27				0%
7 Thu 11/4/27				0%
7 Wed 11/3/27				0%
Mon 11/8/27				0%
7 Wed 11/3/27				0%
7 Tue 11/9/27	28	Painter[500%]	\$960.00	0%
7 Wed 11/3/27	23	Listen Ear Audio	\$80.00	0%
7 Thu 11/4/27	23	In Focus Video	\$120.00	0%
27 Tue 11/16/27	29,30,31	Electrician[200%],Listen Ear Audio ,In Focus Vid	\$680.00	0%
7 Tue 11/16/27	22,23,24,25	Tax[\$50.00]	\$50.00	0%

Update Project after 1 month?

Lab report – Project Management


Insert Add-ins Properties Schedule Status Proofing										
TASK CHART	Timeline									
	Start	Feb '26	Mar '26	Apr '26	May '26	Jun '26	Jul '26	Aug '26	Sep '26	Oct '26
Add tasks with dates to the timeline										
Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost	% Complete	Add New Column	
13	Building Construction	334 days	Fri 7/17/26	Wed 10/27/27	12	Rock Solid Concrete	\$59,102.00	0%		
14	Pour foundations	4 days	Fri 7/17/26	Wed 7/22/26	12	Rock Solid Concrete	\$128.00	0%		
15	Erect steelwork	6 mons	Thu 7/23/26	Wed 1/6/27	14	Boilermaker[600%],Driver[200%],High Jib Crani	\$25,920.00	0%		
16	Erect wall	8 mons	Thu 1/7/27	Wed 8/18/27	15	Supervisor[50%],Carpenter[700%],Labourer[40	\$18,560.00	0%		
17	Install roofing superstructure	4 wks	Thu 8/19/27	Wed 9/15/27	16	Supervisor[50%],Rigger[500%],Boilermaker[500	\$5,280.00	0%		
18	Install roofing retracting mechanism	2 wks	Thu 9/16/27	Wed 9/29/27	17	Supervisor[50%],Welder,Boilermaker[200%],Ri	\$2,000.00	0%		
19	Erect seating tiers	6 wks	Thu 9/16/27	Wed 10/27/27	1855	Supervisor[50%],Carpenter[800%],Welde[200%	\$6,000.00	0%		
20	Building Construction Completed	0 days	Wed 10/27/27	Wed 10/27/27	14,15,16,17	Logictis Cost[\$1,004.00],Bonus[\$210.00]	\$1,214.00	0%		
21	Fit Out	14 days	Thu 10/28/27	Tue 11/16/27			\$6,170.00	0%		
22	Fit all windows and doors	1 wk	Thu 10/28/27	Wed 11/3/27	20	Carpenter[500%],Labourer[200%]	\$1,040.00	0%		
23	Install electrical cabling	0.5 wks	Thu 10/28/27	Mon 11/1/27	20	Electrician[300%],Labourer[200%]	\$520.00	0%		
24	Install electrical fittings and fixtures	0.67 wks	Mon 11/1/27	Thu 11/4/27	23	Electrician[300%]	\$560.00	0%		
25	Install all plumbing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Plumber[200%],Labourer[200%]	\$880.00	0%		
26	Install plumbing fixtures and fittings	0.5 wks	Thu 11/4/27	Mon 11/8/27	25	Plumber[200%]	\$200.00	0%		
27	Lay astro turf	1 wk	Thu 10/28/27	Wed 11/3/27	20	Pure Grass Turf	\$200.00	0%		
28	Erect handrails and fencing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Welder[400%],Boilermaker[200%]	\$880.00	0%		
29	Paint rooms, fixtures, fittings, etc.	0.2 mons	Thu 11/4/27	Tue 11/9/27	28	Painter[500%]	\$960.00	0%		
30	Install PA system	2 days	Mon 11/1/27	Wed 11/3/27	23	Listen Ear Audio	\$80.00	0%		
31	Install video imaging equipment	3 days	Mon 11/1/27	Thu 11/4/27	23	In Focus Video	\$120.00	0%		
32	Fit out control room	1 wk	Wed 11/10/27	Tue 11/16/27	29,30,31	Electrician[200%],Listen Ear Audio ,In Focus Vid	\$680.00	0%		
33	Te	0 days	Tue 11/16/27	Tue 11/16/27	22,23,24,25	Tax[\$50.00]	\$50.00	0%		
34	Commissioning	33.5 days	Wed 11/17/27	Mon 1/3/28			\$3,340.00	0%		
35	Test roof mechanism	1 wk	Wed 11/17/27	Tue 11/23/27	33	Supervisor,Electrician[200%],Rigger	\$960.00	0%		
36	Test PA system	2 days	Wed 11/17/27	Thu 11/18/27	33	Listen Ear Audio	\$80.00	0%		
37	Test video imaging equipment	2 days	Wed 11/17/27	Thu 11/18/27	33	In Focus Video	\$80.00	0%		
38	Test control room equipment	5 wks	Wed 11/24/27	Tue 12/28/27	35,36,37	Supervisor,Listen Ear Audio [20%],In Focus Vide	\$1,520.00	0%		
39	Obtain official occupancy	1 day	Wed 12/29/27	Wed 12/29/27	38	Architect,Building Clerk,Supervisor	\$232.00	0%		
40	Obtain safety certification	2 days	Thu 12/30/27	Fri 12/31/27	39	Supervisor	\$192.00	0%		
41	Official opening	0.5 days	Mon 1/3/28	Mon 1/3/28	40	Supervisor[200%]	\$96.00	0%		
42	Commissioning Completed	0 days	Mon 1/3/28	Mon 1/3/28	35,36,37,38	Bonus[\$180.00]	\$180.00	0%		

Update Project after 4,5 month? Cost of Project? .

Insert Add-ins Properties Schedule Status Proofing										
TASK CHART	Timeline									
	Start	Feb '26	Mar '26	Apr '26	May '26	Jun '26	Jul '26	Aug '26	Sep '26	Oct '26
Add tasks with dates to the timeline										
Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost	% Complete	Add New Column	
13	Building Construction	334 days	Fri 7/17/26	Wed 10/27/27	12	Rock Solid Concrete	\$59,102.00	15%		
14	Pour foundations	4 days	Fri 7/17/26	Wed 7/22/26	12	Rock Solid Concrete	\$128.00	100%		
15	Erect steelwork	6 mons	Thu 7/23/26	Wed 1/6/27	14	Boilermaker[600%],Driver[200%],High Jib Crani	\$25,920.00	39%		
16	Erect wall	8 mons	Thu 1/7/27	Wed 8/18/27	15	Supervisor[50%],Carpenter[700%],Labourer[40	\$18,560.00	0%		
17	Install roofing superstructure	4 wks	Thu 8/19/27	Wed 9/15/27	16	Supervisor[50%],Rigger[500%],Boilermaker[500	\$5,280.00	0%		
18	Install roofing retracting mechanism	2 wks	Thu 9/16/27	Wed 9/29/27	17	Supervisor[50%],Welder,Boilermaker[200%],Ri	\$2,000.00	0%		
19	Erect seating tiers	6 wks	Thu 9/16/27	Wed 10/27/27	1855	Supervisor[50%],Carpenter[800%],Welde[200%	\$6,000.00	0%		
20	Building Construction Completed	0 days	Wed 10/27/27	Wed 10/27/27	14,15,16,17	Logictis Cost[\$1,004.00],Bonus[\$210.00]	\$1,214.00	0%		
21	Fit Out	14 days	Thu 10/28/27	Tue 11/16/27			\$6,170.00	0%		
22	Fit all windows and doors	1 wk	Thu 10/28/27	Wed 11/3/27	20	Carpenter[500%],Labourer[200%]	\$1,040.00	0%		
23	Install electrical cabling	0.5 wks	Thu 10/28/27	Mon 11/1/27	20	Electrician[300%],Labourer[200%]	\$520.00	0%		
24	Install electrical fittings and fixtures	0.67 wks	Mon 11/1/27	Thu 11/4/27	23	Electrician[300%]	\$560.00	0%		
25	Install all plumbing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Plumber[200%],Labourer[200%]	\$880.00	0%		
26	Install plumbing fixtures and fittings	0.5 wks	Thu 11/4/27	Mon 11/8/27	25	Plumber[200%]	\$200.00	0%		
27	Lay astro turf	1 wk	Thu 10/28/27	Wed 11/3/27	20	Pure Grass Turf	\$200.00	0%		
28	Erect handrails and fencing	1 wk	Thu 10/28/27	Wed 11/3/27	20	Welder[400%],Boilermaker[200%]	\$880.00	0%		
29	Paint rooms, fixtures, fittings, etc.	0.2 mons	Thu 11/4/27	Tue 11/9/27	28	Painter[500%]	\$960.00	0%		
30	Install PA system	2 days	Mon 11/1/27	Wed 11/3/27	23	Listen Ear Audio	\$80.00	0%		
31	Install video imaging equipment	3 days	Mon 11/1/27	Thu 11/4/27	23	In Focus Video	\$120.00	0%		
32	Fit out control room	1 wk	Wed 11/10/27	Tue 11/16/27	29,30,31	Electrician[200%],Listen Ear Audio ,In Focus Vid	\$680.00	0%		
33	Te	0 days	Tue 11/16/27	Tue 11/16/27	22,23,24,25	Tax[\$50.00]	\$50.00	0%		
34	Commissioning	33.5 days	Wed 11/17/27	Mon 1/3/28			\$3,340.00	0%		
35	Test roof mechanism	1 wk	Wed 11/17/27	Tue 11/23/27	33	Supervisor,Electrician[200%],Rigger	\$960.00	0%		
36	Test PA system	2 days	Wed 11/17/27	Thu 11/18/27	33	Listen Ear Audio	\$80.00	0%		
37	Test video imaging equipment	2 days	Wed 11/17/27	Thu 11/18/27	33	In Focus Video	\$80.00	0%		
38	Test control room equipment	5 wks	Wed 11/24/27	Tue 12/28/27	35,36,37	Supervisor,Listen Ear Audio [20%],In Focus Vide	\$1,520.00	0%		
39	Obtain official occupancy	1 day	Wed 12/29/27	Wed 12/29/27	38	Architect,Building Clerk,Supervisor	\$232.00	0%		
40	Obtain safety certification	2 days	Thu 12/30/27	Fri 12/31/27	39	Supervisor	\$192.00	0%		
41	Official opening	0.5 days	Mon 1/3/28	Mon 1/3/28	40	Supervisor[200%]	\$96.00	0%		
42	Commissioning Completed	0 days	Mon 1/3/28	Mon 1/3/28	35,36,37,38	Bonus[\$180.00]	\$180.00	0%		

Update Project after 6 month? Cost of Project?

Lab report – Project Management

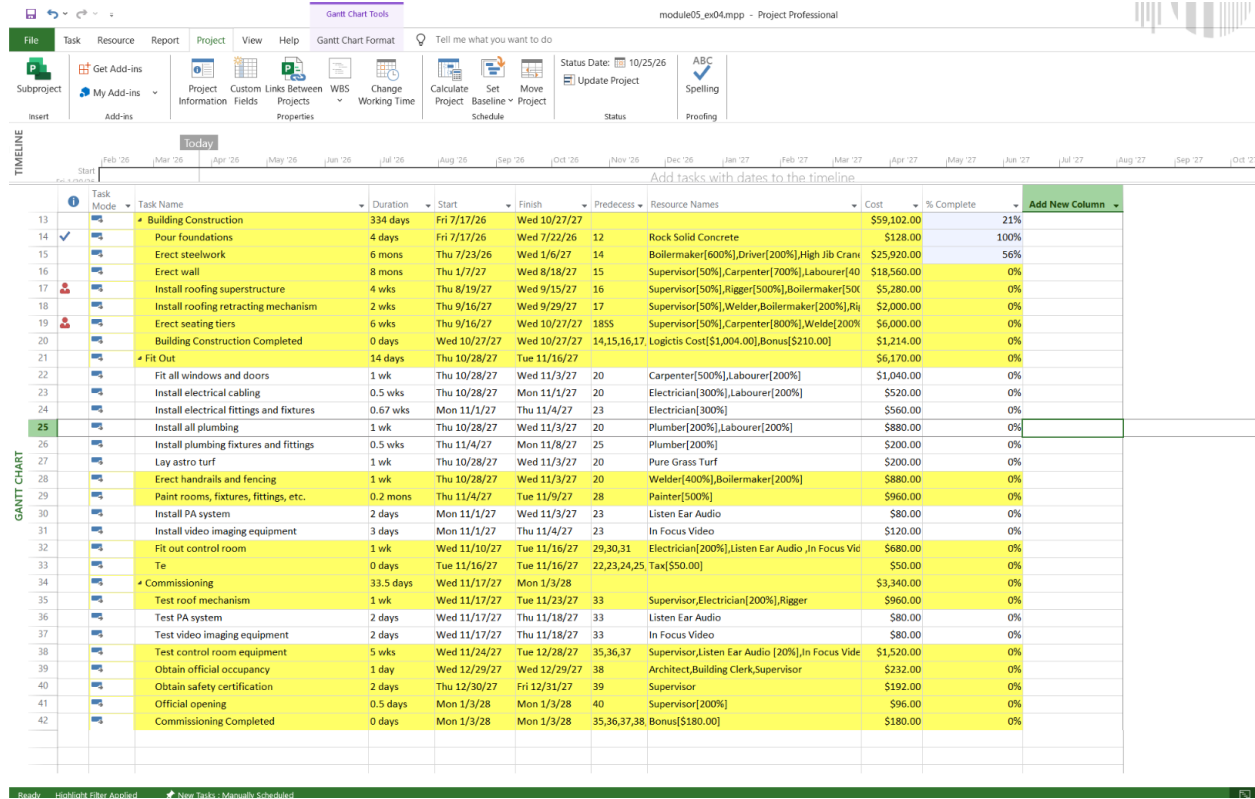

Module 6:

Exercise 1:


	Khảo sát	2 days	Fri 4/3/26	Mon 4/6/26		Bùi Hoàng Quyền, Thuế [\$20.00]
	Phân tchHu	4 days	Tue 4/7/26	Fri 4/10/26	1	Framework[1], Lê Lan Phương [200%], Chi phí đi lại [\$5.00]
	Thiết kế	7 days	Mon 4/13/26	Tue 4/21/26	2	OS[2], Trần Ngọc Hà
	Xây dựng	0.5 mons	Wed 4/22/26	Tue 5/5/26	3	Trần Ngọc Hà, Hardisk[0.5]
	Kiểm thử	1 wk	Wed 5/6/26	Tue 5/12/26	4	Hoàng Mạnh Quân (PM), Thuế [\$10.00]
	Chuyển Giao	4 days	Wed 5/13/26	Mon 5/18/26	5	Lê Hoàng Minh (TV) [50%], Mai Hà Linh, Chi phí công tác[\$100.00]
	Hướng dẫn sử dụng	3 days	Tue 5/19/26	Thu 5/21/26	6	Phạm Minh Vương (TV), Chi phí đi lại [\$10.00]

	Hoàng Mạnh Quân (PM)	Work	H		100%	\$10.00/hr	\$0.00/hr	\$20.00	Prorated	Standard
	Lê Hoàng Minh (TV)	Work	L		50%	\$20.00/hr	\$0.00/hr	\$10.00	Prorated	Standard
	Phạm Minh Vương (TV)	Work	P		200%	\$15.00/hr	\$0.00/hr	\$30.00	Prorated	Standard
	Lê Lan Phương	Work	L		100%	\$15.00/hr	\$0.00/hr	\$10.00	Prorated	Standard
	Hoàng Lê Minh	Work	H		100%	\$10.00/hr	\$0.00/hr	\$0.00	Prorated	Standard
	Mai Hà Linh	Work	M		100%	\$15.00/hr	\$0.00/hr	\$10.00	Prorated	Standard
	Trần Ngọc Hà	Work	T		200%	\$15.00/hr	\$0.00/hr	\$10.00	Prorated	Standard
	Bùi Hoàng Quyền	Work	B		100%	\$15.00/hr	\$0.00/hr	\$10.00	Prorated	Standard
	OS	Material	O			\$250.00		\$0.00	Prorated	
	Hardisk	Material	H			\$120.00		\$0.00	Prorated	
	USB	Material	U			\$1.00		\$0.00	Prorated	
	Framework	Material	F			\$80.00		\$2.00	Prorated	
	Chi phí đi lại	Cost	C						Prorated	
	Chi phí công tác	Cost	C						Prorated	
	Thuế	Cost	T						Prorated	

Lab report – Project Management

COST OVERVIEW

FRI 4/3/26 - THU 5/21/26

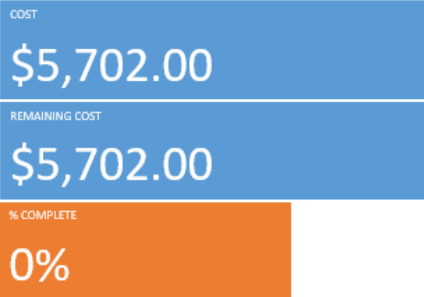


COST STATUS

Cost status for top level tasks.

Name	Actual Cost	Remaining Cost	Baseline Cost	Cost	Cost Variance
Khảo sát	\$0.00	\$270.00	\$0.00	\$270.00	\$270.00
Phân tích	\$0.00	\$1,067.00	\$0.00	\$1,067.00	\$1,067.00
Thiết kế	\$0.00	\$1,350.00	\$0.00	\$1,350.00	\$1,350.00
Xây dựng	\$0.00	\$1,270.00	\$0.00	\$1,270.00	\$1,270.00
Kiểm thử	\$0.00	\$430.00	\$0.00	\$430.00	\$430.00
Chuyển Giao	\$0.00	\$915.00	\$0.00	\$915.00	\$915.00
Hướng dẫn sử dụng	\$0.00	\$400.00	\$0.00	\$400.00	\$400.00

PROGRESS VERSUS COST


Progress made versus the cost spent over time. If % Complete line below the cumulative cost line, your project may be over budget.

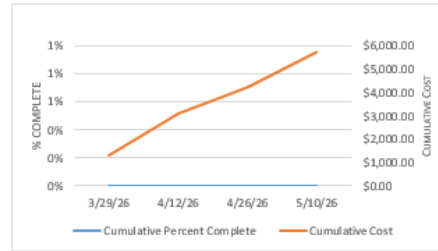

COST STATUS

Cost status for all top-level tasks. Is your baseline zero?

[Try setting as baseline](#)



PROJECT OVERVIEW

FRI 4/3/26 - THU 5/21/26




MILESTONES DUE

Milestones that are coming soon.

Name	Finish
------	--------

% COMPLETE

Status for all top-level tasks. To see the status for subtasks, click on the chart and update the outline level in the Field List.

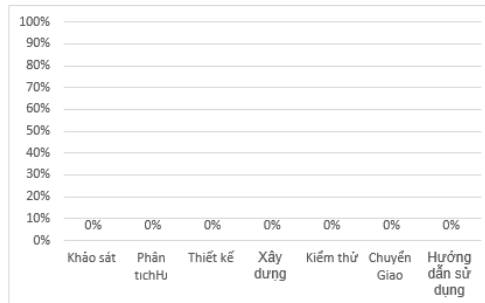

LATE TASKS

Tasks that are past due.

Name	Start	Finish	Duration	% Complete	Resource Names
------	-------	--------	----------	------------	----------------

Lab report – Project Management




WORK BURNDOWN

Shows how much work you have completed and how much you have left. If the remaining cumulative work line is steeper, then the project may be late.

Is your baseline work zero?

[Try setting a baseline](#)

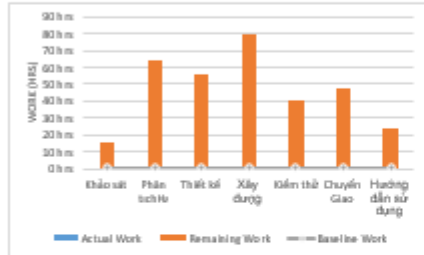

WORK STATS

Shows work stats for all top level tasks.



RESOURCE STATS

Shows work stats for all your resources.



WORK OVERVIEW

Fri 4/3/26 - Thu 5/21/26




REMAINING AVAILABILITY

Shows remaining availability for all work resources.

RESOURCE OVERVIEW

RESOURCE STATS

Work status for all work resources.

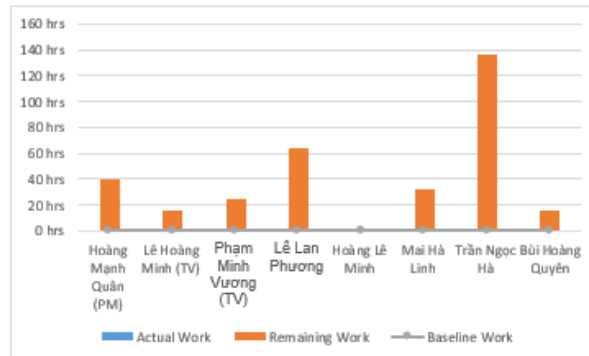

WORK STATUS

% work done by all the work resources.



RESOURCE STATUS

Remaining work for all work resources.

Name	Start	Finish	Remaining Work
Hoàng Mạnh Quân (PM)	Wed 5/6/26	Tue 5/12/26	40 hrs
Lê Hoàng Minh (TV)	Wed 5/13/26	Mon 5/18/26	16 hrs
Phạm Minh Vương (TV)	Tue 5/19/26	Thu 5/21/26	24 hrs
Lê Lan Phương	Tue 4/7/26	Fri 4/10/26	64 hrs
Hoàng Lê Minh	NA	NA	0 hrs
Mai Hà Linh	Wed 5/13/26	Mon 5/18/26	32 hrs
Trần Ngọc Hà	Mon 4/13/26	Tue 5/5/26	136 hrs
Bùi Hoàng Quyên	Fri 4/3/26	Mon 4/6/26	16 hrs
